## 2012 Bond Project Updates – September 2016 HISD Board of Education District V

## **BELLAIRE HIGH SCHOOL**

Budget: \$106.7 million

**Scope of Work:** New school incorporating the recently completed science classroom and laboratory wing and accommodating 2,800

to 3,100 students **Square Footage:** TBD

**Target Completion Date: TBD** 


**Contractor:** Turner Construction Company

**Architect: PBK Architects** 

 PAT meeting scheduled for September to discuss latest design and phasing options.

• Current options focus on keeping students on site throughout the construction project.

• Pending design decisions, construction is estimated to start in 1st quarter 2018.

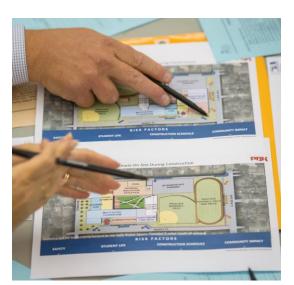

## **CONDIT ELEMENTARY SCHOOL**

Budget: \$24.3 million

Scope of Work: New school for 750 students

Square Footage: 82,968

Target Completion Date: Opened in 3rd Quarter

2016

Contractor: DivisionOne Construction

**Architect:** VLK Architects

- New facility opened to students for 2016-2017 school year.
- Completion of punch list and late changes ongoing.
- Old school demolished during summer 2016.
- New parking lots and park area being installed throughout the fall 2016 semester.

Placing an emphasis on modern learning styles, the two-story school features bright colors, open spaces, large windows that let in copious amounts of light, and curved walls that create lots of seating nooks. White boards are found throughout the hallways, creating pockets where students can gather and learn throughout the building.

