

# BOND OVERSIGHT COMMITTEE WORKBOOK





# TABLE OF CONTENTS

<b>Bond Program Oversight Committee Charter</b>	<b>5</b>
<b>Executive Summary</b>	<b>11</b>
<b>Project Update Report</b>	<b>15</b>
Bond Phasing Schedule	16
Project Update Report — Group 1	19
Project Update Report — Group 2	37
Project Update Report — Group 3	47
Project Update Report — Group 4	53
Districtwide Projects	65
<b>Supplier Diversity (M/WBE) Bond Report</b>	<b>69</b>
<b>Bond Financial Reports</b>	<b>81</b>
Project Budget/Commitment/Available Funds Report	83
<b>Strategic Engagement and Outreach Report</b>	<b>87</b>
<b>Glossary</b>	<b>91</b>
<b>Appendix</b>	<b>95</b>



It is the policy of the Houston Independent School District not to discriminate on the basis of age, color, handicap or disability, ancestry, national origin, marital status, race, religion, sex, veteran status, political affiliation, sexual orientation, gender identity and/or gender expression in its educational or employment programs and activities.



Kinder HSPVA



# BOND PROGRAM OVERSIGHT COMMITTEE CHARTER



Kinder HSPVA

## COMMITTEE MEMBERS

**Gary J. White,**  
Chairman

**Robert M. Eury**

**D.V. "Sonny" Flores,**  
Vice Chairman

**Craig Johnson**

**Gusta Booker III**

**David Quan**

**Michael G. Davis**

**Phoebe Tudor**

## PURPOSE OF CHARTER

**The Board of Education ("Board") for the District desires to make continual improvements to existing programs. As a result, the Bond Program Oversight Committee Charter ("Charter") is adopted to explain the mission, purpose, structure, membership, duties, responsibilities, and expectations. This Charter supersedes the previously adopted charter dated August 30, 2010.**

## COMMITTEE MISSION

**The HISD Board, in response to community interest in the effective and efficient use of bond proceeds, has established a mechanism to encourage greater accountability, transparency, public support, and confidence by creating the Committee. The Committee is an independent citizens' Committee that is responsible to the Superintendent, Board, and general public (in that order).**

**The Committee's charge is to monitor all applicable Bond funded construction projects and help interested Houstonians to stay informed about new construction and renovation projects in the District. Its purpose is to monitor performance and compliance in order to confirm that HISD implements Bond Program work in conformance with the program approved by the Board and make recommendations to maximize available resources to achieve construction goals in the most effective and cost efficient manner. Its focus should be oversight rather than limited to hindsight.**

## COMMITTEE STRUCTURE AND MEMBERSHIP

- a) The Committee has up to nine voting members, including a Chairperson and Vice Chairperson, who are appointed by the Superintendent. Formal action from the Committee requires a majority vote of the quorum present. Individual members of the Committee shall not exercise authority for the Committee as a whole and shall not act independently of the Committee. Written applications will be reviewed by members of the District's Executive Leadership team for each applicant's experiences and qualifications. The Executive Leadership team will submit recommendations to the Superintendent for approval and appointment to the Committee.
- b) Appointments will be staggered for one year and two year terms. Terms may be extended for additional one or two year terms upon approval by the Superintendent.
- c) The Committee will approve meeting minutes, review and approve the reasonableness of reports from the District, and approve the issuance of status reports and other communications from the Committee.
- d) All meetings will be open to the general public.
- e) Membership on the Committee shall consist of interested persons from the following groups who can remain objective and independent with the District's best interest at heart:
  - 1. Special preference for members with expertise or knowledge in the areas of building design/engineering, construction, construction project management, and/or finance.
  - 2. Members active in a business organization representing the business community located in the District.
  - 3. Members who are parents or guardians of a child enrolled in the District and also active in a parent-teacher organization.
  - 4. Members of the community at-large.

- f) The Committee members receive no direct or indirect compensation from the District for their services as members of the Committee.
- g) The Committee members may not have an active contract or be seeking a contract with the District or with any contractor or sub-contractors associated with the Bond Programs.
- h) The Committee may not include any employee or official of the District, or any vendor, contractor or consultant of the District.
- i) A Committee member serves the general interest of the public as opposed to any personal interest or special interest group.
- j) If a Committee member moves outside of the District's geographic boundaries, resigns, violates the Ethics Policy contained herein, fails to attend two consecutive Committee meetings without reasonable excuse, or otherwise becomes unable to serve on the Committee, the Superintendent may declare the position on the Committee to be vacant and appoint another qualified person to the Committee.

## COMMITTEE DUTIES AND RESPONSIBILITIES


The Committee shall inform the Superintendent, Board, and general public (in that order) concerning the District's overall project management of all Bond Programs, including but not limited to:

- a) Review periodic reports produced by the District to verify effective and efficient use of bond proceeds and compliance with the purposes set forth in the Bond Programs as approved by the Board. See reports issued by the District in the "District Duties and Responsibilities" section below.
- b) Ensure that bond revenues are expended for the purpose set forth in the Bond Programs as approved by the Board of Education, and that any deferred proposals or plans where considered necessary are appropriate.

- c) Validate that no bond funds are used for any teacher or administrative salaries or other school operating expense, other than administrative salaries whose primary purpose is to manage the District's Bond Programs.
- d) Review efforts by the District to maximize bond revenues by balancing best value, quality, and efficiency in meeting the District's goals and priorities.
- e) Evaluate risks and related controls associated with the District's Bond Programs, determine focus areas and strategic approach to review, and communicate any findings and recommendations for improvement via a periodic independent report to the Superintendent, Board, and general public. To maximize these efforts, the Committee may recommend the performance of specific audit projects based on its risk assessments and communications to the Board Audit Committee and HISD Office of Inspector General.
- f) Coordinate with the Superintendent's designee to visit District facilities and grounds for which bond proceeds have been or will be expended, in accordance with any necessary access procedures.
- g) Review copies of other bond reports published by the District.
- h) Review any performance audits of the District's Bond Programs to ensure the District is taking appropriate action to remediate any deficiencies identified in such reports.
- i) Review operational audits conducted by the HISD Office of Inspector General to ensure the adequacy of scope, management action plans, and remediation efforts of the District.
- j) Review any financial audits of the District's Bond Programs to ensure the District is taking appropriate action to remediate any deficiencies identified in such reports.
- k) Provide periodic status reports and an annual report regarding the results of its activities, in addition to any Committee findings, recommendations, and management action plans, to the Superintendent and







Board. These reports should include the Committee's opinion regarding the District's remediation efforts for any recommendations included in the performance audits, operational audits, or financial audits mentioned above and will be made available to the general public by inclusion on the District's website and other communication avenues.

- l) Perform other reasonable duties requested by the Superintendent.
- m) Disclose and sign an annual conflict of interest statement for existing conflicts and re-submit if any conflicts arise during a Committee member's tenure.
- n) Any perceived allegation of wrongdoing; potential waste, fraud, misuse or abuse; or non-compliance with Local, State, Federal laws/regulations, or District policies that becomes known to the Committee shall be communicated to the Superintendent, who shall refer such matters to the Board, Ethics and Compliance Officer, Office of Inspector General, and outside legal counsel where appropriate.

The Committee provides counsel and input to the administration and the Board, but it does not have management or policy-setting responsibilities. Also, the Committee does not have a fiduciary responsibility to the District or Board, nor are its members personally liable to the District or Board. The Committee is not responsible for:

- a) Approval of construction contracts or change orders;
- b) Appropriation of construction funds;
- c) Handling of legal matters;
- d) Approval of construction plans and schedules;
- e) Approval of the District's maintenance plan;
- f) Approval of the sale of bonds;
- g) Establishment of priorities and order of construction for the bond projects;
- h) Selection of architects, engineers, construction managers, project managers, and such other professional service firms;
- i) Approval of the design for each project including

exterior materials, paint color, interior finishes, site plan and construction means or methods;

- j) Selection of independent audit firm(s), performance audit consultants and such other consultants as are necessary to support the performance of the Bond Programs;
- k) Setting or approving schedules of design and construction activities;
- l) Investigations of alleged wrongdoing; potential waste, fraud, misuse or abuse; or non-compliance with Local, State, Federal laws/regulations, or District policies.
- m) Directing the activities of staff or consultants; or
- n) Activities, roles or responsibilities that have been delegated to staff or consultants by the Superintendent or his designee.

## COMMITTEE MEETINGS

- a) The Committee shall meet at least quarterly to review the District's Bond Program's status and related information, and to perform other duties as provided herein. The Superintendent, Chairperson, or Vice Chairperson may convene additional meetings, if necessary.
- b) All Committee meetings shall be held within the District's geographic boundaries.
- c) Minutes will be prepared by a representative of the District and will be distributed to the Committee within 15 business days. The minutes will be voted upon for the record at the next scheduled Committee meeting.

## DISTRICT DUTIES AND RESPONSIBILITIES

- a) The Chief Operating Officer shall act as the Superintendent's designee to the Committee.
- b) The Superintendent or his designee shall oversee management's action plan to respond to any



written report from the Committee with findings or suggestions for improvement within 15 business days. All recommendations and management action plans from inception to date will be tracked and made available to the Committee and Board. The District's website and other communication avenues will also publicize the Committee's report and management's action plan for use by the general public.

c) The District shall have a commitment to the Committee, provide open communication, and provide necessary technical and administrative assistance in a timely fashion as follows:

1. Provision of a meeting room, including any necessary audio/visual equipment;
2. Preparation and copies of any documentary meeting materials, such as agendas and reports; and distribution of those materials to the Committee in a timely manner;
3. Provision of a quarterly summary progress report covering the Bond Programs;
4. Access to other information to effectively perform its oversight function.
5. Retention of all Committee meeting records, and providing public access to such records on the District's website; and
6. Notify the public of Committee meeting times and locations. The meetings are open to the public.

d) Summary progress reports will communicate and provide an explanation for the following attributes in a clear concise manner. As part of reporting, HISD will identify projects that experience a significant impact to schedule, budget, or scope of work. Detail reports can be provided upon the Committee's request.

1. Project schedules with anticipated completion dates and current status.
2. Project scope
3. Contingency report (change allowance, encumbrances, and available budget)

4. Expenditure reports

5. Status of Minority/or Woman Owned Business Enterprise (M/WBE)

- e) The appropriate District staff, District consultants, and/or designees shall attend all Committee proceedings in order to provide a status update for their area of responsibility as it relates to the Bond Programs and answer any questions from Committee members.
- f) The Office of Inspector General will consider the input and specific audit requests of the Committee and HISD management during its development of the Annual Audit Plan. Audit projects conducted by the Office of Inspector General will be completed by the issuance of a formal audit report, which will be provided to the Board Audit Committee and made available to the Committee. Such reports will be publicized on the District's website for use by the general public.
- g) The District acknowledges that the Committee may request certain information that is sensitive or legally privileged. The District will use the counsel of its legal advisor to comply with such requests within the limits of Texas law and the best interest of the District.





## ETHICS POLICY

This Ethics Policy provides general guidelines for Committee members to follow in carrying out their roles. Not all ethical issues that Committee members face are covered in this Policy. However, this Policy captures some of the critical areas that help define ethical and professional conduct for Committee members. The provisions of this Policy were developed from existing laws, rules, policies and procedures as well as from concepts that define generally accepted good business practices. Committee members are expected to strictly adhere to the provisions of this Ethics Policy.

## POLICY

**CONFLICT OF INTEREST.** A Committee member shall not make or influence a District decision related to: (1) any contract funded by bond proceeds or (2) any construction project that will benefit the Committee member's outside employment, business, or provide a financial benefit to the Committee member or a family member, such as a spouse, child, parent, or sibling.

**OUTSIDE EMPLOYMENT.** A Committee member shall not use his or her authority over a particular matter to negotiate future employment with any person or organization that relates to: (1) any contract funded by bond proceeds; or (2) any construction project. A Committee member shall not make or influence a District decision related to any construction project involving the interest of a person with whom the member has an agreement concerning current or future employment, or remuneration of any kind. For a period of one (1) year after leaving the Committee, a former Committee member may not represent any person or organization for compensation in connection with any matter pending before the District that, as a Committee member, he or she participated in personally and substantially.

**COMMITMENT TO UPHOLD LAW.** A Committee member shall uphold the federal and Texas Constitutions, the laws and regulations of the United States and the State of Texas, and the policies, procedures, rules and regulations of the Houston Independent School District.

**COMMITMENT TO DISTRICT.** A Committee member shall place the interests of the District above any personal or business interest of the member.

**MEMBER CERTIFICATION.** A Committee member shall certify his or her understanding of Committee's Ethics Policy and disclose and sign an annual conflict of interest statement for existing conflicts and re-submit if any conflicts arise during their tenure.

# EXECUTIVE SUMMARY







## EXECUTIVE SUMMARY

The Houston Independent School District began 2019 with the opening of six new schools, making for an active first quarter as the 2012 Bond Program nears completion.

Schools welcoming students to new facilities upon their return from winter break on Jan. 7 include Kinder High School for the Performing and Visual Arts, Barbara Jordan Career Center, Wharton Dual Language Academy, Sam Houston Math, Science and Technology Center, and Madison and Worthing high schools. Additional site work, including abatement and demolition of old buildings, is ongoing at Madison, Sam Houston, and Jordan.

Only four bond schools remain under active construction for their original scope of work — Lamar, Bellaire, Northside, and Austin high schools. Of those, two — Northside and Lamar — will be completed and opened by the start of the 2019-2020 school year.

Aside from these projects, realignment projects continue across the district, with major construction at seven campuses — Westbury, Waltrip, Wisdom, Washington, Yates, and Milby high schools and Pilgrim Academy. These are new, board-approved projects that were not part of the original scope of work but are funded by surplus bond funds.

Work continues to rebuild four elementary schools — Scarborough, Braeburn, Kolter, and Mitchell — that sustained significant damage due to Hurricane Harvey. Currently, demolition and abatement has been completed at all four campuses. These projects are not funded by the bond program but are overseen by Bond Program and Construction Services staff.

The team also led the planning, promotion, and execution of three building dedication ceremonies, two grand opening celebrations, and the final groundbreaking ceremony of the 2012 Bond Program. Milestone event scheduling and planning is ongoing for 10 more schools.

## DESIGN MILESTONES

The Facilities Design team made significant progress on several ongoing projects. Design work concluded on several large realignment projects, including the Westbury High School Fine Arts wing and new indoor practice pool facilities at Milby, Washington, and Yates high schools.

Additionally, several schools were highlighted for their outstanding design. Energy Institute High School was featured in the Spring 2019 edition of Learning by Design magazine, a premier source for education design innovation and excellence. The Kinder High School for Performing and Visual Arts was named a Houston Business Journal 2019 Landmark award winner. This annual award program recognizes impressive real estate projects that make a significant impression on the Houston landscape and help sculpt the look, feel, and image of the city.

Three recently constructed schools also received Leadership in Energy and Environmental Design (LEED) certifications from the U.S. Green Building Council — Debakey High School for Health Professionals, High School for Law and Justice, and North Forest High School. This brings HISD's total number of LEED certified buildings to 29. Not only will these facilities serve as environmentally-friendly neighbors in their communities, but studies have shown that students and teachers who teach and learn in these buildings are more engaged and have increased achievement and fewer absences.

The Logistics and Furniture, Fixtures, and Equipment teams continue to work together on furniture selection, delivery, and installation. Installations and moves were completed at Wharton Dual Language Academy, Barbara Jordan Career Center, Sam Houston Math, Science and Technology Center, and Madison and Worthing high schools. Additional installations and moves are underway at Lamar High School and at the Westbury High School fine arts addition. To date, the Fixtures, Furniture and Equipment team has ordered more than 70,000 pieces of furniture, fixtures, and equipment.

## M/WBE NETWORKING ACTIVITIES

The Office of Business Assistance held and participated in multiple programs to promote HISD business, bid opportunities and pre-bid meetings to their extensive contact list of minority companies during the first quarter. The Supplier Diversity team sponsored three Workshop Wednesday meetings, which are held monthly to provide information to M/WBEs on topics of interest. First quarter workshop topics included how to do business with HISD, project management for controlled outcomes, and crisis communication planning.

The Business Assistance/Supplier Diversity team also participated in thirteen outreach events and continued its partnership with the Interagency Mentor-Protégé Program. The current M/WBE participation rate for 2012 Bond projects is 28.17 percent — above the 20 percent goal originally set by program officials.

## STRATEGIC ENGAGEMENT AND OUTREACH

The Strategic Engagement and Outreach team spent the first quarter providing communications support to ensure parents, community members, and all HISD stakeholders stayed abreast of the 2012 Bond progress.

The team started the first quarter providing opening-day coverage to highlight the first day of students at six new campuses, all of which opened their doors in January. Coverage included news stories, social media posts, and photos.

During the first quarter, there were six milestone celebrations, including building dedication ceremonies for Askew Elementary School, Parker Elementary School, and Wilson Montessori, grand opening celebrations for Worthing High School and Kinder High School for the Performing and Visual Arts, as well as the final groundbreaking ceremony of the 2012 Bond Program held at Bellaire High School.

The team continued to focus on promoting the significant progress made under the 2012 Bond through updating the bond website, writing and distributing project updates, coordinating media coverage, developing abstracts for 2012 Bond presentations at national conferences, publishing the monthly Building Excellence newsletter, and promoting the @Build\_HISD twitter account.

## REAL ESTATE

With all purchases complete under the 2012 Bond Program, the Real Estate department is maintaining and renewing current lease agreements as needed, assisting project managers with land planning issues, and searching for possible sites for future development. The department continues to supplement and maintain the centralized database of key documents for all HISD properties.







Bellaire High School



# PROJECT UPDATE REPORT



Kinder HSPVA



Project	Scope of Work	Proposed Project Budget
<b>High Schools:</b>		<b>\$</b>
Austin High School	New facility preserving the architecturally significant building structure for a campus accommodating 1,800 – 2,000 students.	68,429,000
Bellaire High School	New 2,800 – 3,100 student school that will incorporate the recently completed science classroom and laboratory wing.	106,724,000
Davis High School	New facility preserving the architecturally significant building structure for a campus accommodating 1,500 – 1,700 students.	46,764,000
DeBakey High School	New 900 – 1,000 student health professions school.	64,512,000
Eastwood Academy	New facility that will incorporate the new 2 story classroom wing for a campus accommodating 500 students.	10,875,000
Furr High School	New 1,100 – 1,300 student school.	55,100,000
Houston High School	New 2,550 – 2,750 student school that will incorporate the new science classroom and laboratory wing.	101,428,000
HSPVA	New 750 student performing and visual arts school.	80,178,000
Jones High School	Renovations to existing school facilities.	1,125,000
Jordan High School	New 600 – 800 student school.	36,693,000
Kashmere High School	Renovations to existing school facilities and site improvements.	17,000,000
Lamar High School	New facility preserving the architecturally significant building structure for a campus accommodating 2,800 – 3,100 students.	107,974,000
Lee High School	New 1,700 – 1,900 student school.	73,801,000
Madison High School	New 1,900 – 2,100 student school that will incorporate recent science and classroom building renovations.	82,736,000
Milby High school	New facility preserving the architecturally significant building structure for a campus accommodating 1,800 – 2,000 students.	68,810,000
North Early College	New 400 student early college school.	13,500,000
Scarborough High School	Renovations to existing school facilities and site improvements.	12,566,000
Sharpstown High School	New 1,300 – 1,500 student school.	54,944,000
Sharpstown International High School	Renovations to existing school facilities and site improvements.	6,125,000
South Early College	New 400 student early college school.	13,500,000
Sterling High School	New 1,600 – 1,800 student school.	72,304,000
Waltrip High School	Partial replacement and general renovations to accommodate 1,800 – 2,000 students.	30,115,000
Washington High School	New 1,100 – 1,300 student school.	51,732,000
Westbury High School	Partial replacement and general renovations to accommodate 2,300 – 2,500 students.	40,006,000
Worthing High School	New facility that will incorporate the new 2 story classroom wing for a campus accommodating 1,100 – 1,300 students.	30,180,000
Yates High School	New 1,300 – 1,500 student school.	59,481,000
Young Men's College Prep.	Partial replacement and general renovations to complement portions of the Howard Payne Carter Career Center for a campus accommodating 900 – 1,000 students.	28,675,000
Young Women's College Prep.	Partial replacement and general renovations for a campus accommodating 900 – 1,000 students.	27,159,000
	<b>High School Subtotal</b>	<b>\$1,362,436,000</b>

Project	Scope of Work	Proposed Project Budget
<b>Middle Schools:</b>		<b>\$</b>
Dowling Middle School	New 1,300 – 1,500 student school.	59,125,000
Grady Middle School	New addition to complete multi-phase master plan for the campus.	14,825,000
	<b>Middle School Subtotal</b>	<b>\$73,950,000</b>
<b>K-8s:</b>		
Garden Oaks Montessori K-8 School	New addition and general renovations of the existing facilities accommodating 750 – 900 students.	26,678,000
Mandarin Chinese Language Immersion School at Gordon K-8	New 750 – 900 student school.	32,161,000
Pilgrim Academy K-8	New addition for a campus accommodating 750 – 900 students.	7,989,000
Wharton Dual Language School K-8	New addition and general renovations of the existing facilities accommodating 750 – 900 students.	35,603,000
Wilson Montessori School K-8	New addition and general renovations of the existing facilities accommodating 750 – 900 students.	18,914,000
	<b>K-8 Subtotal</b>	<b>\$121,345,000</b>
<b>Elementary Schools:</b>		
Askew Elementary School	850 student new school — replacement.	26,632,000
Parker Elementary School	850 student new school — replacement.	29,485,000
Relief Elementary School	750 student new school to be built in the west Houston area.	23,417,000
	<b>Elementary Subtotal</b>	<b>\$79,534,000</b>
<b>All Schools</b>		<b>\$1,637,265,000</b>
<b>Districtwide Projects:</b>		
District Athletic Improvements	Replacement of regional field house(s) and athletic facility improvements.	44,675,000
District Wide Land Acquisition	Districtwide funds to supplement significant site/parking constraints.	55,767,000
Middle School Restroom Renovation	Districtwide middle school restroom renovations.	35,000,000
Districtwide Technology	Districtwide technology improvements.	100,000,000
Districtwide Safety and Security	Districtwide safety and security improvements.	17,293,000
	<b>Districtwide Total</b>	<b>\$252,735,000</b>
	<b>Grand Total</b>	<b>\$1,890,000,000</b>

1. Funding within this bond for North and South Early College will be combined with funds previously allocated from the 2007 bond for these projects to meet the schools programmatic needs.
2. HSPVA moved to district 8 due to a proposed site for the new school located at 1300 Capital.
3. Program costs allocated to each project budget will be separated into various program budgets to provide better oversight and financial management, at a later date.
4. New schools / replacement projects will undergo a school site specific ed-spec development process and all schools will undergo a scope to budget process.
5. Project budgets include allocations for planning, design, construction, administration, and other related costs.
6. The current allocation for the Young Men's College Preparatory Academy (YMCPA) will allow for a demolition of the EO Smith facility, the addition of a smaller facility, and the renovation of the HP Carter facility for use by the YMCPA. An alternate plan for the project to include the demolition of both the EO Smith and HP Carter facilities and the building of a new school would cost an additional \$13,727,000.
7. Condit ES will be rebuilt and funded from surplus bond funds and/or the sale of real estate.
8. High School for Law Enforcement and Criminal Justice will be rebuilt and funded from surplus bond funds and/or the sale of real estate.





Kinder HSPVA

# PROJECT UPDATE REPORT GROUP 1



Planning and Design — Early/Mid 2013 | Anticipated Construction to Begin — Mid/Late 2014

Complete In Progress Scheduled

	Planning	Design	Construction	Opening
<b>Condit</b> Elementary School				
<b>DeBakey</b> High School for Health Professions				
<b>Furr</b> High School				
<b>Tanglewood</b> Middle School				
<b>Kinder</b> High School for the Performing and Visual Arts				
<b>Wisdom</b> High School				
<b>Mandarin Immersion</b> Magnet School				
<b>Milby</b> High School				
<b>North Houston</b> Early College High School				
<b>Mark White</b> Elementary School				
<b>Sharpstown</b> High School				
<b>South</b> Early College High School				
<b>Sterling Aviation</b> High School				
<b>Waltrip</b> High School				
<b>Booker T. Washington</b> High School				
<b>Worthing</b> High School				
<b>Mickey Leland</b> College Preparatory Academy for Young Men				





## CONDIT ELEMENTARY SCHOOL

Condit Elementary School was originally built in 1909. The school moved to its current facility in Bellaire in 1914, with an addition built in 1927. The pre-K–5 campus offers a Spanish dual language program, as well as a Vanguard neighborhood program.

Original Budget: **\$24,293,919**

Trustee: **Sue Deigaard**

Location: **7000 South 3rd St.**

### DESIGN TEAM

HISD Manager	<b>Andreas Peebles</b>
Architect	<b>VLK Architects</b>
Contractor	<b>DivisionOne Construction</b>
Program Manager	<b>Heery International, Inc.</b>

### INFORMATION

Planning and Design Start	<b>Early/Mid 2013</b>
Construction Start	<b>Mid/Late 2014</b>
Phase	<b>Closeout</b>
Percent of Phase	<b>100%</b>

### MILESTONES COMPLETED

Programming/Conceptual Design	<b>Complete</b>	Bid & Award	<b>Complete</b>
Schematic Design Phase	<b>Complete</b>	Construction Start	<b>Complete</b>
Design Development	<b>Complete</b>	Construction Complete	<b>Complete</b>
Construction Documents	<b>Complete</b>	Closeout	<b>Complete</b>

PROJECT PHASE	2013	2014	2015	2016	2017	2018	2019	2020
Planning	■							
Design		■	■					
Construction			■	■	■			
Target Opening				■				

■ Complete 
 ■ In Progress 
 ■ Continued Site Development Progress 
 ■ Scheduled 
 ■ Continued Site Development



# DEBAKEY HIGH SCHOOL FOR HEALTH PROFESSIONS

The Michael E. DeBakey High School for Health Professions provides a rigorous and comprehensive pre-college program for students pursuing careers in the health and medical field. The new school is located on the western side of the Texas Medical Center. The location provides students with access to some of the best medical facilities in the world.

Original Budget: **\$64,512,000**

Supplemental Funding, Realignment  
Funding & Adjustments: **\$2,515,113**

Trustee: **Sue Deigaard**

Location: **2545 Pressler St.**

## DESIGN TEAM

HISD Manager	<b>Andreas Peeples</b>
Architect	<b>WHR   Lake-Flato</b>
Contractor	<b>Tellepsen Builders, L.P.</b>
Program Manager	<b>Heery International, Inc.</b>

## INFORMATION

Planning and Design Start	<b>Early/Mid 2013</b>
Construction Start	<b>Mid/Late 2014</b>
Phase	<b>Closeout</b>
Percent of Phase	<b>99%</b>

## MILESTONES COMPLETED

Programming/Conceptual Design	<b>Complete</b>	Bid & Award	<b>Complete</b>
Schematic Design Phase	<b>Complete</b>	Construction Start	<b>Complete</b>
Design Development	<b>Complete</b>	Construction Complete	<b>Complete</b>
Construction Documents	<b>Complete</b>	Closeout	

PROJECT PHASE	2013	2014	2015	2016	2017	2018	2019	2020
Planning	■							
Design		■	■	■	■			
Construction			■	■	■	■		
Target Opening					■			

■ Complete 
 ■ In Progress 
 ■ Continued Site Development Progress 
 ■ Scheduled 
 ■ Continued Site Development





## FURR HIGH SCHOOL

Furr High School opened in the fall of 1961 on Houston's east side. The school is home to the Futures Academy of Petroleum Engineering Technology at Furr. It also offers career pathways in energy and mass communications through linked learning, an educational approach that combines rigorous academics with hands-on, real-world experiences.

Original Budget: **\$55,100,000**

Supplemental Funding, Realignment  
Funding & Adjustments: **\$499,287**

Trustee: **Diana Dávila**

Location: **520 Mercury Drive**

### DESIGN TEAM

HISD Manager	<b>Andreas Peeples</b>
Architect	<b>ERO Architects Inc.</b>
Contractor	<b>Prime Contractors</b>
Program Manager	<b>Rice &amp; Gardner Consultants, Inc.</b>

### INFORMATION

Planning and Design Start	<b>Early/Mid 2013</b>
Construction Start	<b>Mid/Late 2015</b>
Phase	<b>Site Development/Closeout</b>
Percent of Phase	<b>98%/85%</b>

### MILESTONES COMPLETED

Programming/Conceptual Design	<b>Complete</b>	Bid & Award	Complete
Schematic Design Phase	<b>Complete</b>	Construction Start	Complete
Design Development	<b>Complete</b>	Construction Complete	Complete
Construction Documents	<b>Complete</b>	Closeout	

PROJECT PHASE	2013	2014	2015	2016	2017	2018	2019	2020
Planning	Complete							
Design		Complete	Complete					
Construction			In Progress	In Progress	In Progress	In Progress	In Progress	
Target Opening					In Progress			

■ Complete 
 ■ In Progress 
 ■ Continued Site Development Progress 
 ■ Scheduled 
 ■ Continued Site Development

# TANGLEWOOD MIDDLE SCHOOL

Tanglewood Middle School, located in Houston's Galleria area, was originally built in 1949. It was replaced by a new main school building, which was completed in 2012. As an International Baccalaureate school, Tanglewood offers a rigorous academic program that aims to develop knowledgeable, caring, inquisitive students who embrace multiculturalism and diversity and want to make the world a better place

Original Budget: **\$14,825,000**

Supplemental Funding, Realignment  
Funding & Adjustments: **\$96,404**

Trustee: **Anne Sung**

Location: **5215 San Felipe St.**

## DESIGN TEAM

HISD Manager	<b>Andreas Peeples</b>
Architect	<b>Natex Architects Inc.</b>
Contractor	<b>DivisionOne Construction</b>
Program Manager	<b>Rice &amp; Gardner Consultants, Inc.</b>

## INFORMATION


Planning and Design Start	<b>Early/Mid 2013</b>
Construction Start	<b>Mid/Late 2014</b>
Phase	<b>Closeout</b>
Percent of Phase	<b>100%</b>

## MILESTONES COMPLETED

Programming/Conceptual Design	<b>Complete</b>	Bid & Award	<b>Complete</b>
Schematic Design Phase	<b>Complete</b>	Construction Start	<b>Complete</b>
Design Development	<b>Complete</b>	Construction Complete	<b>Complete</b>
Construction Documents	<b>Complete</b>	Closeout	<b>Complete</b>

PROJECT PHASE	2013	2014	2015	2016	2017	2018	2019	2020
Planning	■							
Design		■	■	■				
Construction			■	■	■			
Target Opening				■				

■ Complete 
 ■ In Progress 
 ■ Continued Site Development Progress 
 ■ Scheduled 
 ■ Continued Site Development

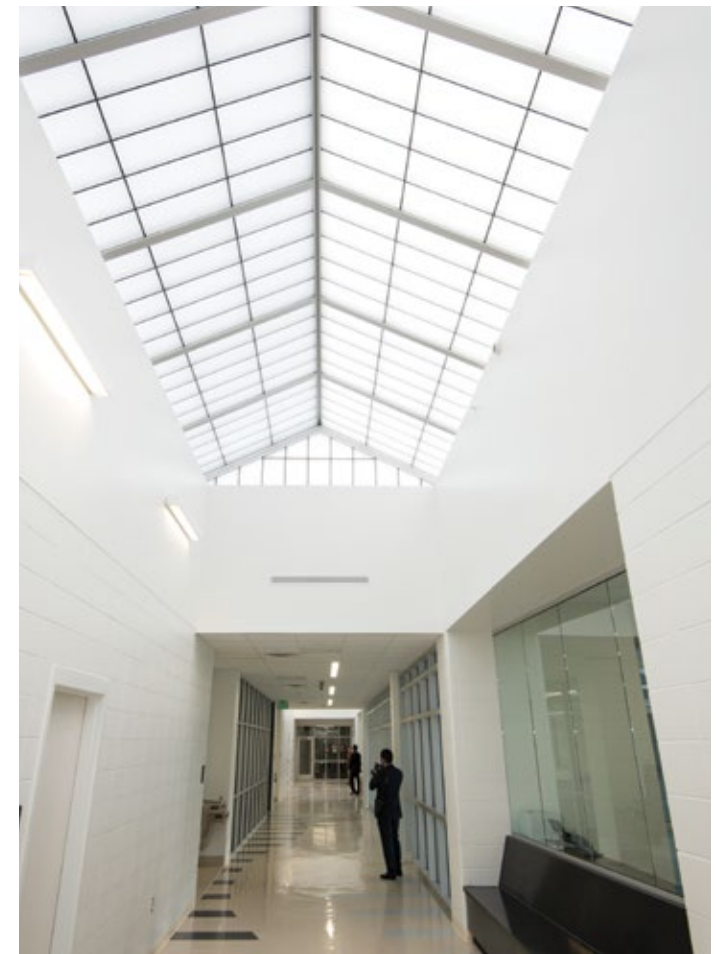





# KINDER HIGH SCHOOL FOR THE PERFORMING AND VISUAL ARTS (HSPVA)

HSPVA is a performing and visual arts magnet school and national model for combining arts and academics. The current facility was constructed in 1981. Under the 2012 bond program, a new facility will be built in downtown Houston near other arts and theatrical venues located in the city's Theater District on district property that spans a city block.

Original Budget: **\$80,178,000**

Supplemental Funding, Realignment Funding & Adjustments: **\$6,587,477**

Trustee: **Diana Dávila**

Location: **790 Austin St.**

DESIGN TEAM		INFORMATION	
HISD Manager	<b>Andreas Peeples</b>	Planning and Design Start	<b>Early/Mid 2013</b>
Architect	<b>Gensler</b>	Construction Start	<b>Mid/Late 2016</b>
Contractor	<b>McCarthy</b>	Phase	<b>Closeout</b>
Program Manager	<b>Rice &amp; Gardner Consultants, Inc.</b>	Percent of Phase	<b>80%</b>

MILESTONES COMPLETED			
Programming/Conceptual Design	<b>Complete</b>	Bid & Award	<b>Complete</b>
Schematic Design Phase	<b>Complete</b>	Construction Start	<b>Complete</b>
Design Development	<b>Complete</b>	Construction Complete	<b>Complete</b>
Construction Documents	<b>Complete</b>	Closeout	

PROJECT PHASE	2013	2014	2015	2016	2017	2018	2019	2020
Planning	Complete							
Design		Complete	Complete					
Construction				Complete	Complete	Complete		
Target Opening							Complete	

■ Complete 
 ■ In Progress 
 ■ Continued Site Development Progress 
 ■ Scheduled 
 ■ Continued Site Development

# WISDOM HIGH SCHOOL

Wisdom High School was originally built in 1962 in west Houston. The comprehensive high school offers career pathways in construction and design through linked learning, an educational approach that combines rigorous academics with hands-on, real-world experiences.

Original Budget: **\$73,801,000**

Supplemental Funding, Realignment  
Funding & Adjustments: **\$3,785,865**

Trustee: **Anne Sung**

Location: **6529 Beverly Hill St.**

## DESIGN TEAM

HISD Manager	<b>Andreas Peeples</b>	Planning and Design Start	<b>Early/Mid 2013</b>
Architect	<b>WHR Architects, Inc.</b>	Construction Start	<b>Mid/Late 2014</b>
Contractor	<b>Satterfield and Pontikes Construction, Inc.</b>	Phase	<b>Site Development/Closeout</b>
Program Manager	<b>HISD</b>	Percent of Phase	<b>65%/35%</b>

## MILESTONES COMPLETED

Programming/Conceptual Design	<b>Complete</b>	Bid & Award	<b>Complete</b>
Schematic Design Phase	<b>Complete</b>	Construction Start	<b>Complete</b>
Design Development	<b>Complete</b>	Construction Complete	<b>Complete</b>
Construction Documents	<b>Complete</b>	Closeout	

PROJECT PHASE	2013	2014	2015	2016	2017	2018	2019	2020
Planning	■							
Design		■						
Construction			■	■	■	■	■	
Target Opening					■			

■ Complete 
 ■ In Progress 
 ■ Continued Site Development Progress 
 ■ Scheduled 
 ■ Continued Site Development





## MANDARIN IMMERSION MAGNET SCHOOL (MIMS)

The Mandarin Immersion Magnet School is currently housed in a small elementary school that was built in 1953 in Bellaire. The school opened in the fall of 2012, becoming one of the first in Texas to offer Mandarin language immersion. The school started with pre-kindergarten through second grades, with plans to add additional grades each year, eventually becoming a K-8 campus.

Original Budget: **\$32,161,000**

Supplemental Funding, Realignment Funding & Adjustments: **\$2,087,906**

Trustee: **Anne Sung**

Location: **5445 W. Alabama St.**

### DESIGN TEAM

HISD Manager	<b>Andreas Peeples</b>
Architect	<b>PBK Architects</b>
Contractor	<b>Satterfield &amp; Pontikes Construction, Inc.</b>
Program Manager	<b>Heery International, Inc.</b>

### INFORMATION

Planning and Design Start	<b>Early/Mid 2013</b>
Construction Start	<b>Mid/Late 2014</b>
Phase	<b>Closeout</b>
Percent of Phase	<b>100%</b>

### MILESTONES COMPLETED

Programming/Conceptual Design	<b>Complete</b>	Bid & Award	<b>Complete</b>
Schematic Design Phase	<b>Complete</b>	Construction Start	<b>Complete</b>
Design Development	<b>Complete</b>	Construction Complete	<b>Complete</b>
Construction Documents	<b>Complete</b>	Closeout	<b>Complete</b>

PROJECT PHASE	2013	2014	2015	2016	2017	2018	2019	2020
Planning	Complete							
Design		Complete						
Construction			Complete					
Target Opening				Complete				

■ Complete 
 ■ In Progress 
 ■ Continued Site Development Progress 
 ■ Scheduled 
 ■ Continued Site Development



# MICKEY LELAND COLLEGE PREPARATORY ACADEMY FOR YOUNG MEN

Mickey Leland College Preparatory Academy was transformed into an all-male college preparatory academy in 2011. Serving students in grades 6–12, the campus offers a small, inclusive environment and rigorous college preparatory curriculum with an emphasis on Advanced Placement and STEM (Science, Technology, Engineering and Math) courses.

Original Budget: **\$28,675,000**

Supplemental Funding, Realignment  
Funding & Adjustments: **\$835,976**

Trustee: **Rhonda Skillern-Jones**

Location: **1700 Gregg St.**

## DESIGN TEAM


HISD Manager	<b>Andreas Peebles</b>	Planning and Design Start	<b>Early/Mid 2013</b>
Architect	<b>Harrison Kornberg with Corgan Associates</b>	Construction Start	<b>Mid/Late 2014</b>
Contractor	<b>Prime Contractors</b>	Phase	<b>Site Development/Closeout</b>
Program Manager	<b>Rice &amp; Gardner Consultants, Inc.</b>	Percent of Phase	<b>99%</b>

## MILESTONES COMPLETED

Programming/Conceptual Design	<b>Complete</b>	Bid & Award	<b>Complete</b>
Schematic Design Phase	<b>Complete</b>	Construction Start	<b>Complete</b>
Design Development	<b>Complete</b>	Construction Complete	<b>Complete</b>
Construction Documents	<b>Complete</b>	Closeout	

PROJECT PHASE	2013	2014	2015	2016	2017	2018	2019	2020
Planning	■							
Design		■	■	■				
Construction			■	■	■	■	■	
Target Opening					■			

■ Complete 
 ■ In Progress 
 ■ Continued Site Development Progress 
 ■ Scheduled 
 ■ Continued Site Development

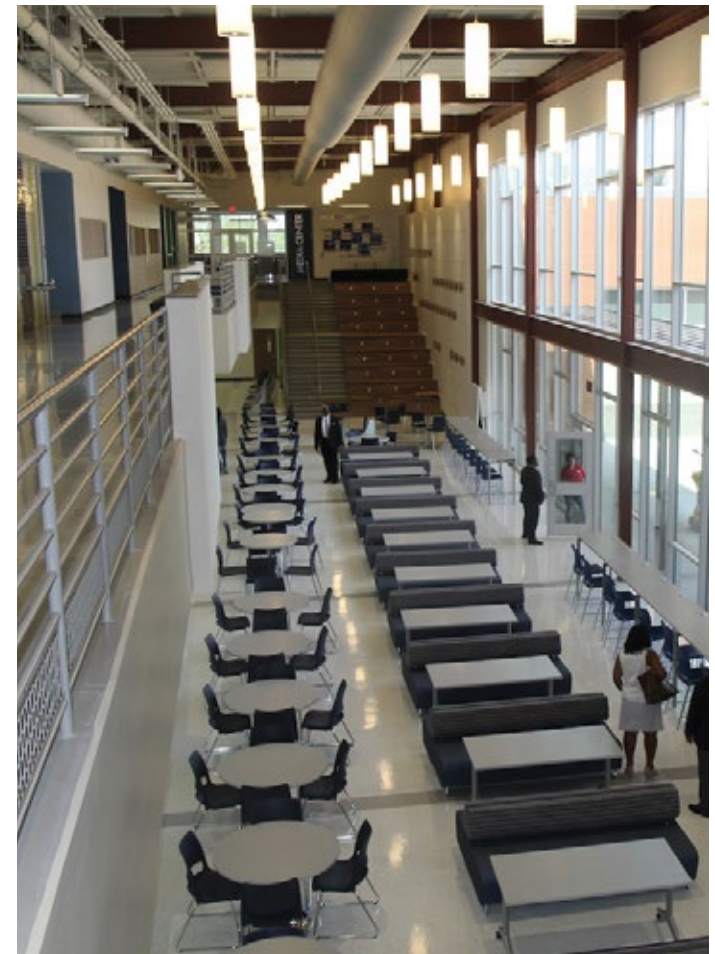



## MILBY HIGH SCHOOL

Milby High School was constructed in 1926 in east Houston. The campus has seen numerous additions over the years and is home to a STEM magnet program with three strands — Applied Science Health Professions, Computing Science, and Petroleum Exploration and Engineering. Through linked learning the school also offers career pathways in culinary arts, cosmetology, welding, graphics technology and HVAC heating and cooling systems.

Original Budget: **\$68,810,000**

Supplemental Funding, Realignment Funding & Adjustments: **\$13,114,723**

Trustee: **Sergio Lira**

Location: **1601 Broadway St.**

### DESIGN TEAM

HISD Manager	<b>Andreas Peebles</b>
Architect	<b>Kirksey Architecture</b>
Contractor	<b>Tellepsen Builders, LP</b>
Program Manager	<b>Heery International, Inc.</b>

### INFORMATION

Planning and Design Start	<b>Early/Mid 2013</b>
Construction Start	<b>Mid/Late 2014</b>
Phase	<b>Closeout</b>
Percent of Phase	<b>99%</b>

### MILESTONES COMPLETED

Programming/Conceptual Design	<b>Complete</b>	Bid & Award	<b>Complete</b>
Schematic Design Phase	<b>Complete</b>	Construction Start	<b>Complete</b>
Design Development	<b>Complete</b>	Construction Complete	<b>Complete</b>
Construction Documents	<b>Complete</b>	Closeout	

PROJECT PHASE	2013	2014	2015	2016	2017	2018	2019	2020
Planning	Complete							
Design		Complete						
Construction			Complete	Complete	Complete			
Target Opening					Complete			

■ Complete 
 ■ In Progress 
 ■ Continued Site Development Progress 
 ■ Scheduled 
 ■ Continued Site Development

# NORTH HOUSTON EARLY COLLEGE HIGH SCHOOL

North Houston Early College High School is one of five HISD early college campuses offering students the chance to earn both a high school diploma and an associate's degree while still in high school. The new school features modern science labs, flexible learning spaces, and a college resource center, where students can obtain scholarship and registration information, as well as access to counselors.

Original Budget: **\$13,500,000**

Trustee: **Elizabeth Santos**

Location: **8001 Fulton St.**




DESIGN TEAM		INFORMATION	
HISD Manager	<b>Andreas Peebles</b>	Planning and Design Start	<b>Early/Mid 2013</b>
Architect	<b>RdIR Architects</b>	Construction Start	<b>Mid/Late 2014</b>
Contractor	<b>Drymalla</b>	Phase	<b>Closeout</b>
Program Manager	<b>N/A</b>	Percent of Phase	<b>100%</b>

MILESTONES COMPLETED			
Programming/Conceptual Design	<b>Complete</b>	Bid & Award	<b>Complete</b>
Schematic Design Phase	<b>Complete</b>	Construction Start	<b>Complete</b>
Design Development	<b>Complete</b>	Construction Complete	<b>Complete</b>
Construction Documents	<b>Complete</b>	Closeout	<b>Complete</b>

PROJECT PHASE	2013	2014	2015	2016	2017	2018	2019	2020
Planning	Complete							
Design		Complete	Complete					
Construction			Complete	Complete				
Target Opening				Complete				

■ Complete 
 ■ In Progress 
 ■ Continued Site Development Progress 
 ■ Scheduled 
 ■ Continued Site Development

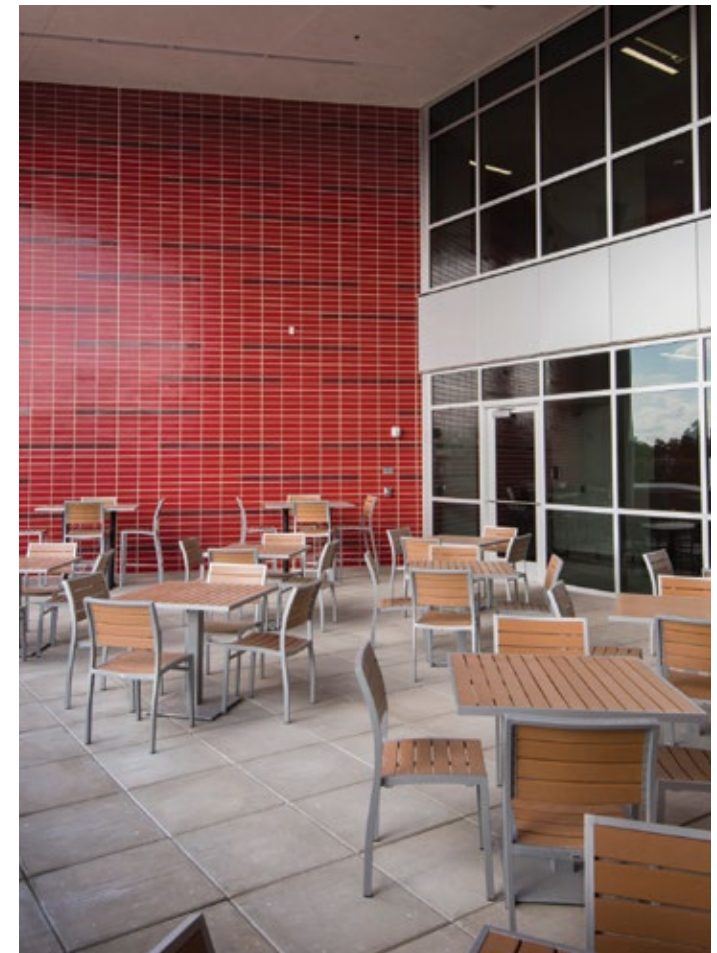





# SHARPSTOWN HIGH SCHOOL

Sharpstown High School is located in southwest Houston. It originally opened in 1968 as Sharpstown Junior-Senior High School, but separated from the middle school and moved to its current location the following year. The comprehensive high school offers a variety of special programs, including Business Management and Administration, Career Development, Finance, Health Science, and Information Technology.

Original Budget: **\$54,944,000**

Supplemental Funding, Realignment  
Funding & Adjustments: **\$5,646,534**

Trustee: **Holly Maria Flynn Vilaseca**

Location: **7504 Bissonnet St.**

DESIGN TEAM		INFORMATION	
HISD Manager	Andreas Peeples	Planning and Design Start	Early/Mid 2013
Architect	Kell-Munoz Co.	Construction Start	Mid/Late 2014
Contractor	ICI Construction	Phase	Site Development/Closeout
Program Manager	HISD	Percent of Phase	90%/85%

MILESTONES COMPLETED			
Programming/Conceptual Design	Complete	Bid & Award	Complete
Schematic Design Phase	Complete	Construction Start	Complete
Design Development	Complete	Construction Complete	Complete
Construction Documents	Complete	Closeout	

PROJECT PHASE	2013	2014	2015	2016	2017	2018	2019	2020
Planning	Complete							
Design		Complete						
Construction			Complete	Complete	Complete	In Progress	In Progress	
Target Opening					In Progress			

■ Complete 
 ■ In Progress 
 ■ Continued Site Development Progress 
 ■ Scheduled 
 ■ Continued Site Development

# SOUTH EARLY COLLEGE HIGH SCHOOL

South Early College High School is one of five HISD early college campuses offering students the chance to earn both a high school diploma and an associate's degree while still in high school. The new school features flexible learning spaces that accommodate the school's technological programs, including robotics, computer technology, and software engineering.

Original Budget: **\$13,500,000**

Trustee: **Wanda Adams**

Location: **1930 Airport Blvd.**

## DESIGN TEAM

HISD Manager	<b>Andreas Peebles</b>
Architect	<b>Smith &amp; Co.</b>
Contractor	<b>Drymalla</b>
Program Manager	<b>N/A</b>

## INFORMATION


Planning and Design Start	<b>Early/Mid 2013</b>
Construction Start	<b>Mid/Late 2014</b>
Phase	<b>Site Development/Closeout</b>
Percent of Phase	<b>100%</b>

## MILESTONES COMPLETED

Programming/Conceptual Design	<b>Complete</b>	Bid & Award	<b>Complete</b>
Schematic Design Phase	<b>Complete</b>	Construction Start	<b>Complete</b>
Design Development	<b>Complete</b>	Construction Complete	<b>Complete</b>
Construction Documents	<b>Complete</b>	Closeout	<b>Complete</b>

PROJECT PHASE	2013	2014	2015	2016	2017	2018	2019	2020
Planning	■							
Design		■	■	■				
Construction			■	■	■			
Target Opening				■				

■ Complete 
 ■ In Progress 
 ■ Continued Site Development Progress 
 ■ Scheduled 
 ■ Continued Site Development

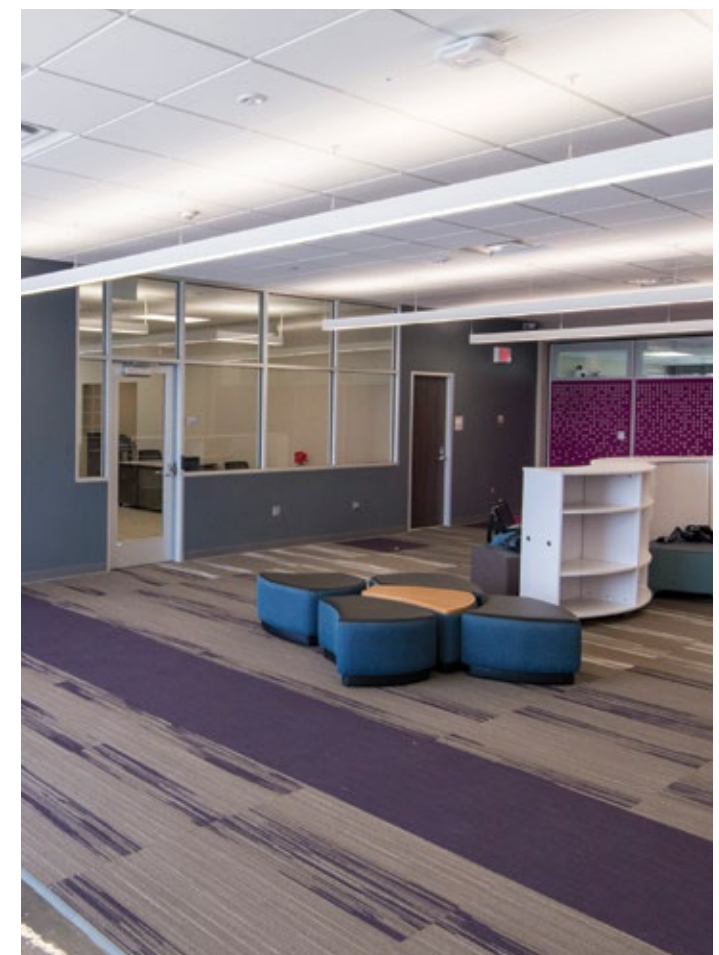



## STERLING AVIATION HIGH SCHOOL

Sterling Aviation High School, constructed in 1965, consists of five main school buildings. The comprehensive high school is home to the Futures Academy of Logistics and Global Supply at Sterling. It also places a strong emphasis on its career pathway in aviation, which is offered through linked learning, an educational approach that combines rigorous academics with real-world experiences.

Original Budget: **\$72,304,000**

Trustee: **Jolanda Jones**

Location: **11625 Martindale Road**

### DESIGN TEAM

HISD Manager	<b>Andreas Peeples</b>
Architect	<b>SHW Group</b>
Contractor	<b>Cadence McShane Construction, LLC</b>
Program Manager	<b>Heery International, Inc.</b>

### INFORMATION

Planning and Design Start	<b>Early/Mid 2013</b>
Construction Start	<b>Mid/Late 2014</b>
Phase	<b>Closeout</b>
Percent of Phase	<b>98%</b>

### MILESTONES COMPLETED

Programming/Conceptual Design	<b>Complete</b>	Bid & Award	<b>Complete</b>
Schematic Design Phase	<b>Complete</b>	Construction Start	<b>Complete</b>
Design Development	<b>Complete</b>	Construction Complete	<b>Complete</b>
Construction Documents	<b>Complete</b>	Closeout	

PROJECT PHASE	2013	2014	2015	2016	2017	2018	2019	2020
Planning	■							
Design		■	■	■				
Construction			■	■	■	■		
Target Opening					■			

■ Complete 
 ■ In Progress 
 ■ Continued Site Development Progress 
 ■ Scheduled 
 ■ Continued Site Development



# WALTRIP HIGH SCHOOL

Waltrip High School opened in 1959 in the Oak Forest neighborhood in north Houston. The comprehensive high school offers a magnet program and linked learning career pathway in Research & Technology. Linked Learning is an educational approach that combines rigorous academics and real-world experiences with the goal of readying students for college and careers.

Original Budget: **\$30,115,000**

Supplemental Funding, Realignment  
Funding & Adjustments: **\$5,123,961**

Trustee: **Elizabeth Santos**

Location: **1900 West 34th St.**

## DESIGN TEAM

HISD Manager	<b>Andreas Peeples</b>	Planning and Design Start	<b>Early/Mid 2013</b>
Architect	<b>Gensler</b>	Construction Start	<b>Mid/Late 2014</b>
Contractor	<b>Satterfield &amp; Pontikes Construction, Inc.</b>	Phase	<b>Closeout</b>
Program Manager	<b>N/A</b>	Percent of Phase	<b>98%</b>

## MILESTONES COMPLETED

Programming/Conceptual Design	<b>Complete</b>	Bid & Award	<b>Complete</b>
Schematic Design Phase	<b>Complete</b>	Construction Start	<b>Complete</b>
Design Development	<b>Complete</b>	Construction Complete	<b>Complete</b>
Construction Documents	<b>Complete</b>	Closeout	

PROJECT PHASE	2013	2014	2015	2016	2017	2018	2019	2020
Planning	■							
Design		■	■	■				
Construction		■	■	■	■	■		
Target Opening					■			

■ Complete 
 ■ In Progress 
 ■ Continued Site Development Progress 
 ■ Scheduled 
 ■ Continued Site Development





## WASHINGTON HIGH SCHOOL

Booker T. Washington High School, named after an education pioneer, was constructed in 1958 in northwest Houston. The comprehensive high school is home to the Futures Academy of Engineering Sciences at Washington. It also offers career pathways in building and construction through its linked learning program, an approach that combines rigorous academics with real-world experiences.

Original Budget: **\$51,732,000**

Supplemental Funding, Realignment  
Funding & Adjustments: **\$10,847,934**

Trustee: **Rhonda Skillern-Jones**

Location: **119 E. 39th St.**

### DESIGN TEAM

HISD Manager	<b>Andreas Peeples</b>
Architect	<b>Fanning-Howey/House Partners</b>
Contractor	<b>Prime Contractors</b>
Program Manager	<b>N/A</b>

### INFORMATION

Planning and Design Start	<b>Early/Mid 2013</b>
Construction Start	<b>Mid/Late 2014</b>
Phase	<b>Site Development/Closeout</b>
Percent of Phase	<b>70%/50%</b>

### MILESTONES COMPLETED

Programming/Conceptual Design	<b>Complete</b>	Bid & Award	<b>Complete</b>
Schematic Design Phase	<b>Complete</b>	Construction Start	<b>Complete</b>
Design Development	<b>Complete</b>	Construction Complete	<b>Complete</b>
Construction Documents	<b>Complete</b>	Closeout	

PROJECT PHASE	2013	2014	2015	2016	2017	2018	2019	2020
Planning	■							
Design		■	■	■				
Construction			■	■	■	■	■	
Target Opening						■		

■ Complete 
 ■ In Progress 
 ■ Continued Site Development Progress 
 ■ Scheduled 
 ■ Continued Site Development

# MARK WHITE ELEMENTARY SCHOOL

Demographic projections and current student populations indicated a need for a new elementary school in the west Houston area. The campus was built to help address overcrowding in four neighboring schools. In addition to a standard elementary curriculum, Mark White Elementary also offers a French language immersion program — the first of its kind in Texas.

Original Budget: **\$23,417,000**

Trustee: **Anne Sung**

Location: **2515 Old Farm Road**

## DESIGN TEAM

HISD Manager	<b>Andreas Peeples</b>
Architect	<b>Gensler</b>
Contractor	<b>Satterfield &amp; Pontikes Construction, Inc.</b>
Program Manager	<b>Rice &amp; Gardner Consultants, Inc.</b>

## INFORMATION


Planning and Design Start	<b>Early/Mid 2013</b>
Construction Start	<b>Mid/Late 2014</b>
Phase	<b>Closeout</b>
Percent of Phase	<b>90%</b>

## MILESTONES COMPLETED

Programming/Conceptual Design	<b>Complete</b>	Bid & Award	<b>Complete</b>
Schematic Design Phase	<b>Complete</b>	Construction Start	<b>Complete</b>
Design Development	<b>Complete</b>	Construction Complete	<b>Complete</b>
Construction Documents	<b>Complete</b>	Closeout	

PROJECT PHASE	2013	2014	2015	2016	2017	2018	2019	2020
Planning	■							
Design		■	■	■				
Construction			■	■	■			
Target Opening				■				

■ Complete 
 ■ In Progress 
 ■ Continued Site Development Progress 
 ■ Scheduled 
 ■ Continued Site Development

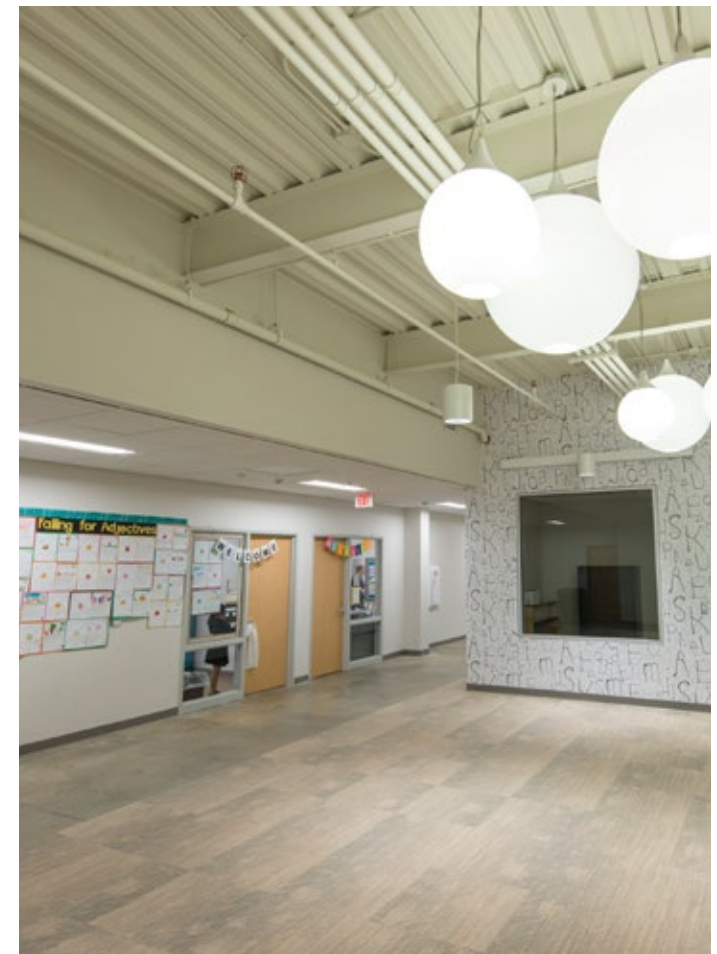





## WORTHING HIGH SCHOOL

The main building at Worthing High School was constructed in 1959. The school provides a comprehensive academic curriculum, along with career and technology programs, including career pathways in hotel and restaurant management through linked learning, an educational approach that combines rigorous academics with real-world experiences.

Original Budget: **\$30,180,000**

Supplemental Funding, Realignment  
Funding & Adjustments: **\$2,897,460**

Trustee: **Wanda Adams**

Location: **9215 Scott St.**

### DESIGN TEAM

HISD Manager	<b>Andreas Peeples</b>
Architect	<b>Molina Walker Architects</b>
Contractor	<b>Prime Contractors</b>
Program Manager	<b>N/A</b>

### INFORMATION

Planning and Design Start	<b>Early/Mid 2013</b>
Construction Start	<b>Mid/Late 2014</b>
Phase	<b>Closeout</b>
Percent of Phase	<b>10%</b>

### MILESTONES COMPLETED

Programming/Conceptual Design	<b>Complete</b>	Bid & Award	<b>Complete</b>
Schematic Design Phase	<b>Complete</b>	Construction Start	<b>Complete</b>
Design Development	<b>Complete</b>	Construction Complete	<b>Complete</b>
Construction Documents	<b>Complete</b>	Closeout	

PROJECT PHASE	2013	2014	2015	2016	2017	2018	2019	2020
Planning	Complete							
Design		Complete	Complete					
Construction			Complete	Complete	Complete	Complete		
Target Opening							Complete	

■ Complete 
 ■ In Progress 
 ■ Continued Site Development Progress 
 ■ Scheduled 
 ■ Continued Site Development

# PROJECT UPDATE REPORT GROUP 2



Lamar High School

Planning and Design — Early/Mid 2014 | Anticipated Construction to Begin — Mid/Late 2015

Complete In Progress Scheduled

	Planning	Design	Construction	Opening
<b>Bellaire</b> High School	Complete	Complete	In Progress	Scheduled
<b>Northside</b> High School	Complete	Complete	In Progress	Scheduled
<b>Lawson</b> Middle School	Complete	Complete	Complete	Complete
<b>Eastwood</b> Academy	Complete	Complete	Complete	Complete
High School for <b>Law &amp; Justice</b>	Complete	Complete	Complete	Complete
<b>Lamar</b> High School	Complete	Complete	In Progress	Scheduled
<b>Parker</b> Elementary School	Complete	Complete	Complete	Complete
<b>Yates</b> High School	Complete	Complete	Complete	Complete



# BELLAIRE HIGH SCHOOL

Bellaire High School serves more than 3,700 students and offers a variety of special programs, including a World Languages magnet program and International Baccalaureate, a rigorous academic program that aims to develop knowledgeable, caring, inquisitive students who embrace multiculturalism and diversity and want to make the world a better place.

Original Budget: **\$106,724,000**  
 Supplemental Funding, Realignment  
 Funding & Adjustments: **\$34,790,428**  
 Trustee: **Sue Deigaard**  
 Location: **5100 Maple St., Bellaire**

DESIGN TEAM		INFORMATION	
HISD Manager	<b>Dan Bankhead</b>	Planning and Design Start	<b>Early/Mid 2013</b>
Architect	<b>PBK Architects</b>	Construction Start	<b>Mid/Late 2014</b>
Contractor	<b>Turner Construction Company</b>	Phase	<b>Phase 1 Construction/ Construction Documents</b>
Program Manager	<b>Heery International, Inc.</b>	Percent of Phase	<b>99%/95%</b>

MILESTONES COMPLETED			
Programming/Conceptual Design	<b>Complete</b>	Bid & Award	
Schematic Design Phase	<b>Complete</b>	Construction Start	
Design Development	<b>Complete</b>	Construction Complete	
Construction Documents		Closeout	

PROJECT PHASE	2013	2014	2015	2016	2017	2018	2019	2020	2021
Planning									
Design									
Construction									
Target Opening									

Complete In Progress Continued Site Development Progress Scheduled Continued Site Development



# NORTHSIDE HIGH SCHOOL

Northside High School was built in 1926 in Houston's Northside. The school features a magnet for Culinary Arts, Hotel Management, and Media. In conjunction with the magnet program, the school also offers career pathways in hospitality and tourism through linked learning, an approach that combines rigorous academics and real-world experiences.

Original Budget: **\$46,764,000**

Supplemental Funding, Realignment  
Funding & Adjustments: **\$19,633,657**

Trustee: **Elizabeth Santos**

Location: **1101 Quitman St.**

## DESIGN TEAM

HISD Manager	<b>Andreas Peeples</b>
Architect	<b>Bay-IBI Group Architects</b>
Contractor	<b>Satterfield &amp; Pontikes</b>
Program Manager	<b>Heery International, Inc.</b>

## INFORMATION


Planning and Design Start	<b>Early/Mid 2014</b>
Construction Start	<b>Mid/Late 2015</b>
Phase	<b>Construction</b>
Percent of Phase	<b>84%</b>

## MILESTONES COMPLETED

Programming/Conceptual Design	<b>Complete</b>	Bid & Award	<b>Complete</b>
Schematic Design Phase	<b>Complete</b>	Construction Start	<b>Complete</b>
Design Development	<b>Complete</b>	Construction Complete	
Construction Documents	<b>Complete</b>	Closeout	

PROJECT PHASE	2013	2014	2015	2016	2017	2018	2019	2020
Planning	Complete	Complete						
Design		Complete	Complete	Complete				
Construction				In Progress	In Progress	In Progress	Scheduled	
Target Opening								

■ Complete 
 ■ In Progress 
 ■ Continued Site Development Progress 
 ■ Scheduled 
 ■ Continued Site Development

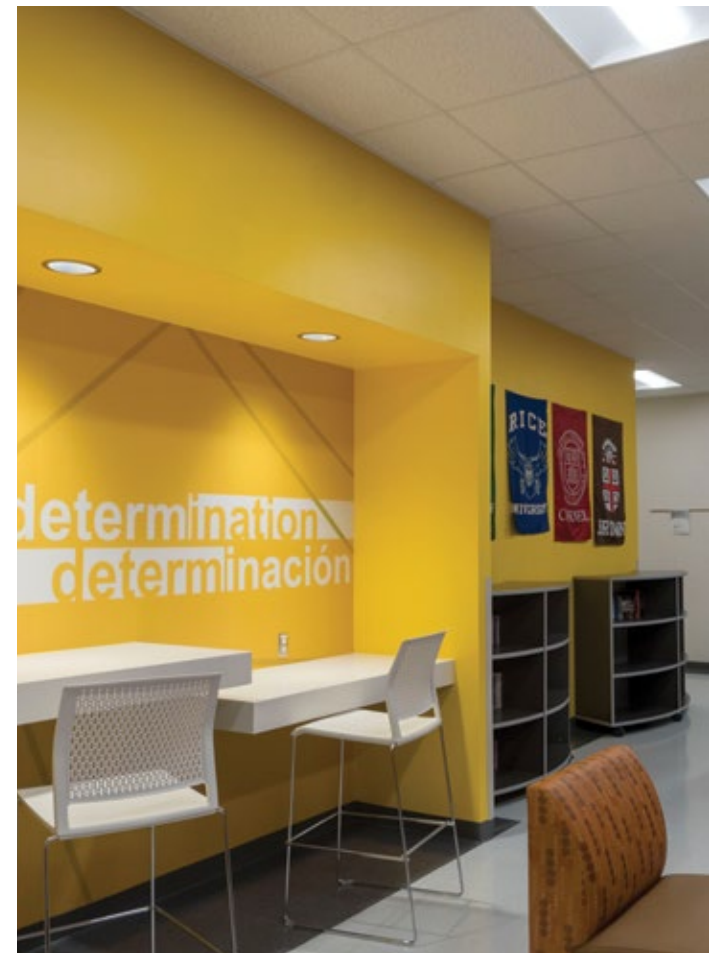



## LAWSON MIDDLE SCHOOL

Lawson Middle School serves students in grades 6 through 8. Located in south Houston, the school offers a performing and visual arts magnet program as part of its academic program. The main building at Lawson Middle School was constructed in 1966, and over the years the campus has grown to include several small ancillary buildings and 17 temporary classroom buildings.

Original Budget: **\$59,125,000**

Supplemental Funding, Realignment Funding & Adjustments: **\$4,081,598**

Trustee: **Wanda Adams**

Location: **14000 Stancliff St.**

DESIGN TEAM		INFORMATION	
HISD Manager	<b>Andreas Peeples</b>	Planning and Design Start	<b>Early/Mid 2014</b>
Architect	<b>Harrison Kornberg</b>	Construction Start	<b>Early/Mid 2016</b>
Contractor	<b>Turner Construction Company</b>	Phase	<b>Site Development/Closeout</b>
Program Manager	<b>Rice &amp; Gardner Consultants Inc.</b>	Percent of Phase	<b>85%/75%</b>

MILESTONES COMPLETED			
Programming/Conceptual Design	<b>Complete</b>	Bid & Award	<b>Complete</b>
Schematic Design Phase	<b>Complete</b>	Construction Start	<b>Complete</b>
Design Development	<b>Complete</b>	Construction Complete	<b>Complete</b>
Construction Documents	<b>Complete</b>	Closeout	

PROJECT PHASE	2013	2014	2015	2016	2017	2018	2019	2020
Planning								
Design								
Construction								
Target Opening								

■ Complete 
 ■ In Progress 
 ■ Continued Site Development Progress 
 ■ Scheduled 
 ■ Continued Site Development

# EASTWOOD ACADEMY

Eastwood Academy is a small college preparatory high school southeast of downtown Houston. All of Eastwood Academy's students take a rigorous college-preparatory curriculum and complete 80 hours of community volunteer work prior to graduation.

Original Budget: **\$10,875,000**

Supplemental Funding, Realignment  
Funding & Adjustments: **\$432,421**

Trustee: **Diana Dávila**

Location: **1315 Dumble St.**

## DESIGN TEAM

HISD Manager	<b>Andreas Peeples</b>
Architect	<b>Prosign</b>
Contractor	<b>Patriot Contracting, LLC</b>
Program Manager	<b>Rice &amp; Gardner Consultants, Inc.</b>

## INFORMATION

Planning and Design Start	<b>Early/Mid 2014</b>
Construction Start	<b>Early/Mid 2016</b>
Phase	<b>Site Development/ Closeout</b>
Percent of Phase	<b>98%/90%</b>

## MILESTONES COMPLETED

Programming/Conceptual Design	<b>Complete</b>	Bid & Award	<b>Complete</b>
Schematic Design Phase	<b>Complete</b>	Construction Start	<b>Complete</b>
Design Development	<b>Complete</b>	Construction Complete	<b>Complete</b>
Construction Documents	<b>Complete</b>	Closeout	

PROJECT PHASE	2013	2014	2015	2016	2017	2018	2019	2020
Planning		■						
Design		■	■	■	■			
Construction				■	■	■	■	
Target Opening						■		

■ Complete 
 ■ In Progress 
 ■ Continued Site Development Progress 
 ■ Scheduled 
 ■ Continued Site Development







## HIGH SCHOOL FOR LAW & JUSTICE

The mission of the High School for Law & Justice is to provide students and staff with a safe facility where students receive a strong academic education in conjunction with an in-depth study of law enforcement and criminal justice. The school offers a magnet program in legal studies, law enforcement and fire technology.

Original Budget: **\$39,998,131**

Trustee: **Diana Dávila**

Location: **3505 Coyle St.**

### DESIGN TEAM

HISD Manager	<b>Andreas Peebles</b>
Architect	<b>Page   DLR</b>
Contractor	<b>B3Ci</b>
Program Manager	<b>Rice &amp; Gardner Consultants, Inc.</b>

### INFORMATION

Planning and Design Start	<b>Early/Mid 2014</b>
Construction Start	<b>Early/Mid 2016</b>
Phase	<b>Closeout</b>
Percent of Phase	<b>50%</b>

### MILESTONES COMPLETED

Programming/Conceptual Design	<b>Complete</b>	Bid & Award	<b>Complete</b>
Schematic Design Phase	<b>Complete</b>	Construction Start	<b>Complete</b>
Design Development	<b>Complete</b>	Construction Complete	<b>Complete</b>
Construction Documents	<b>Complete</b>	Closeout	

PROJECT PHASE	2013	2014	2015	2016	2017	2018	2019	2020
Planning								
Design								
Construction								
Target Opening								

■ Complete 
 ■ In Progress 
 ■ Continued Site Development Progress 
 ■ Scheduled 
 ■ Continued Site Development

# LAMAR HIGH SCHOOL

Lamar High School offers a Business Administration magnet program and International Baccalaureate, a rigorous academic program that aims to develop knowledgeable, caring, inquisitive students who embrace multiculturalism and diversity and want to make the world a better place.

Original Budget: **\$107,974,000**

Supplemental Funding, Realignment  
Funding & Adjustments: **\$14,927,465**

Trustee: **Anne Sung**

Location: **3325 Westheimer Road**

## DESIGN TEAM


HISD Manager	<b>Andreas Peebles</b>	Planning and Design Start	<b>Early/Mid 2014</b>
Architect	<b>Perkins + Will</b>	Construction Start	<b>Early/Mid 2016</b>
Contractor	<b>Gilbane Building Company</b>	Phase	<b>Construction</b>
Program Manager	<b>Heery International, Inc.</b>	Percent of Phase	<b>65%</b>

## MILESTONES COMPLETED

Programming/Conceptual Design	<b>Complete</b>	Bid & Award	<b>Complete</b>
Schematic Design Phase	<b>Complete</b>	Construction Start	<b>Complete</b>
Design Development	<b>Complete</b>	Construction Complete	
Construction Documents	<b>Complete</b>	Closeout	

PROJECT PHASE	2013	2014	2015	2016	2017	2018	2019	2020
Planning	■	■						
Design		■	■	■				
Construction					■	■	■	
Target Opening							■	

■ Complete 
 ■ In Progress 
 ■ Continued Site Development Progress 
 ■ Scheduled 
 ■ Continued Site Development

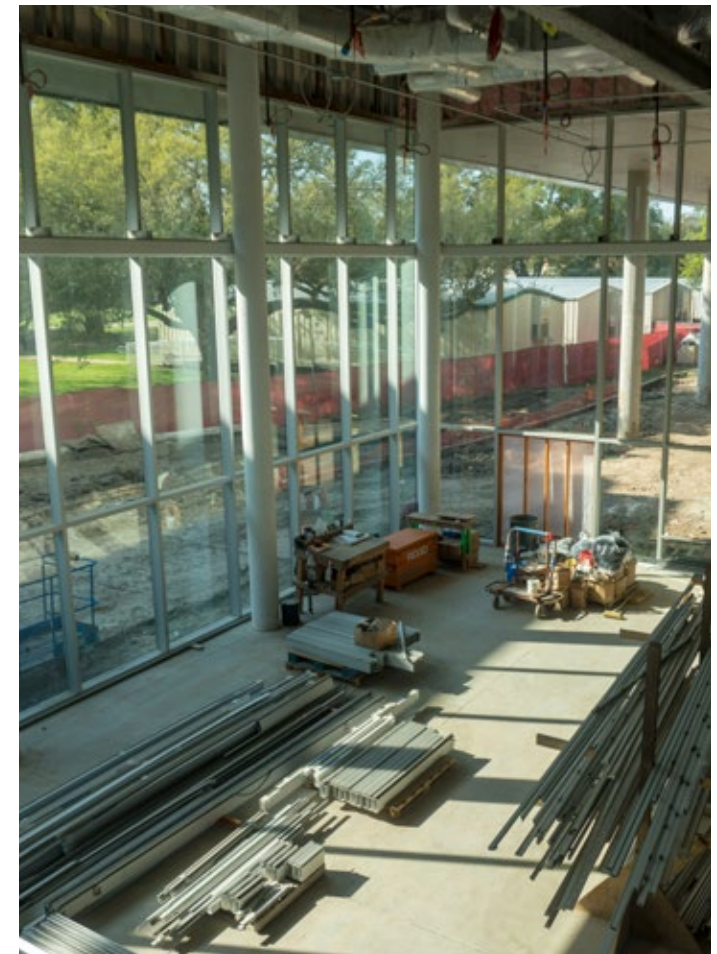



## PARKER ELEMENTARY SCHOOL

Parker Elementary in southwest Houston is a music magnet school. The original campus of Parker Elementary School was constructed in 1959. The campus also includes five temporary classroom buildings.

Original Budget: **\$29,485,000**

Supplemental Funding, Realignment  
Funding & Adjustments: **\$1,814,820**

Trustee: **Wanda Adams**

Location: **10626 Atwell Drive**

DESIGN TEAM		INFORMATION	
HISD Manager	<b>Andreas Peeples</b>	Planning and Design Start	<b>Early/Mid 2014</b>
Architect	<b>Bravé Architecture</b>	Construction Start	<b>Early/Mid 2016</b>
Contractor	<b>Patriot Contracting</b>	Phase	<b>Site Development/Closeout</b>
Program Manager	<b>N/A</b>	Percent of Phase	<b>99%/95%</b>

MILESTONES COMPLETED			
Programming/Conceptual Design	<b>Complete</b>	Bid & Award	<b>Complete</b>
Schematic Design Phase	<b>Complete</b>	Construction Start	<b>Complete</b>
Design Development	<b>Complete</b>	Construction Complete	<b>Complete</b>
Construction Documents	<b>Complete</b>	Closeout	

PROJECT PHASE	2013	2014	2015	2016	2017	2018	2019	2020
Planning	■	■						
Design		■ ■ ■ ■ ■	■ ■ ■ ■ ■	■ ■ ■ ■ ■				
Construction			■ ■ ■ ■ ■	■ ■ ■ ■ ■	■ ■ ■ ■ ■	■ ■ ■ ■ ■		
Target Opening						■ ■ ■ ■ ■		

■ Complete 
 ■ In Progress 
 ■ Continued Site Development Progress 
 ■ Scheduled 
 ■ Continued Site Development



# YATES HIGH SCHOOL

Yates High School, located in Houston's third ward, is a comprehensive high school that features communications and maritime magnet programs. The main building at Yates High School was constructed in 1958.

Original Budget: **\$59,481,000**

Supplemental Funding, Realignment  
Funding & Adjustments: **\$16,124,271**

Trustee: **Jolanda Jones**

Location: **3703 Sampson St.**

## DESIGN TEAM

HISD Manager	<b>Andreas Peeples</b>
Architect	<b>Moody Nolan</b>
Contractor	<b>Turner Construction</b>
Program Manager	<b>HISD</b>

## INFORMATION

Planning and Design Start	<b>Early/Mid 2014</b>
Construction Start	<b>Mid/Late 2015</b>
Phase	<b>Site Development/Closeout</b>
Percent of Phase	<b>75%/50%</b>

## MILESTONES COMPLETED

Programming/Conceptual Design	<b>Complete</b>	Bid & Award	<b>Complete</b>
Schematic Design Phase	<b>Complete</b>	Construction Start	<b>Complete</b>
Design Development	<b>Complete</b>	Construction Complete	<b>Complete</b>
Construction Documents	<b>Complete</b>	Closeout	

PROJECT PHASE	2013	2014	2015	2016	2017	2018	2019	2020
Planning	■	■						
Design		■	■	■				
Construction				■	■	■	■	
Target Opening						■		

■ Complete 
 ■ In Progress 
 ■ Continued Site Development Progress 
 ■ Scheduled 
 ■ Continued Site Development





Askew Elementary School



# PROJECT UPDATE REPORT GROUP 3



Sam Houston Math, Science, and Technology Center

Planning and Design — Early/Mid 2013 | Anticipated Construction to Begin — Mid/Late 2014

Complete In Progress Scheduled

	Planning	Design	Construction	Opening
<b>Askew</b> Elementary School	Complete	Complete	Complete	Complete
<b>Barbara Jordan</b> Career Center	Complete	Complete	In Progress	Complete
<b>Sam Houston</b> Math, Science, and Technology Center	Complete	Complete	In Progress	Complete
<b>Young Women's</b> College Preparatory Academy (YWCPA)	Complete	Complete	Complete	Complete





## ASKEW ELEMENTARY SCHOOL

Askew Elementary School is a pre-K – 5 school with a Vanguard magnet program. The campus includes 22 classrooms in temporary buildings.

Original Budget: **\$26,632,000**

Supplemental Funding, Realignment  
Funding & Adjustments: **\$1,254,972**

Trustee: **Holly Maria Flynn Vilaseca**

Location: **11200 Wood Lodge Drive**

DESIGN TEAM		INFORMATION	
HISD Manager	<b>Andreas Peebles</b>	Planning and Design Start	<b>Early/Mid 2015</b>
Architect	<b>Cre8 Architects</b>	Construction Start	<b>Mid/Late 2016</b>
Contractor	<b>Drymalla Construction</b>	Phase	<b>Closeout</b>
Program Manager	<b>Rice &amp; Gardner Consultants, Inc.</b>	Percent of Phase	<b>75%</b>

MILESTONES COMPLETED			
Programming/Conceptual Design	<b>Complete</b>	Bid & Award	<b>Complete</b>
Schematic Design Phase	<b>Complete</b>	Construction Start	<b>Complete</b>
Design Development	<b>Complete</b>	Construction Complete	<b>Complete</b>
Construction Documents	<b>Complete</b>	Closeout	

PROJECT PHASE	2013	2014	2015	2016	2017	2018	2019	2020
Planning								
Design								
Construction								
Target Opening								

■ Complete 
 ■ In Progress 
 ■ Continued Site Development Progress 
 ■ Scheduled 
 ■ Continued Site Development

# BARBARA JORDAN CAREER CENTER

Barbara Jordan Career Center is a regional Career Hub. Located in northeast Houston, the school provides students from area high schools with real-world experiences in a variety of professions, including Auto/Diesel, Audio/Visual, Construction Management, Cosmetology, Culinary Arts, Marketing/Entrepreneurship, STEM (Electronics), and Welding.

Original Budget: **\$36,693,000**

Supplemental Funding, Realignment  
Funding & Adjustments: **\$331,913**

Trustee: **Rhonda Skillern-Jones**

Location: **5800 Eastex Freeway**

## DESIGN TEAM

HISD Manager	<b>Dan Bankhead</b>
Architect	<b>Corgan Associates, Inc. dba Corgan</b>
Contractor	<b>Cadence McShane</b>
Program Manager	<b>Heery International, Inc.</b>

## INFORMATION

Planning and Design Start	<b>Early/Mid 2015</b>
Construction Start	<b>Mid/Late 2016</b>
Phase	<b>Construction</b>
Percent of Phase	<b>99%</b>


## MILESTONES COMPLETED

Programming/Conceptual Design	<b>Complete</b>	Bid & Award	<b>Complete</b>
Schematic Design Phase	<b>Complete</b>	Construction Start	<b>Complete</b>
Design Development	<b>Complete</b>	Construction Complete	
Construction Documents	<b>Complete</b>	Closeout	

PROJECT PHASE	2013	2014	2015	2016	2017	2018	2019	2020
Planning								
Design								
Construction								
Target Opening								

■ Complete 
 ■ In Progress 
 ■ Continued Site Development Progress 
 ■ Scheduled 
 ■ Continued Site Development



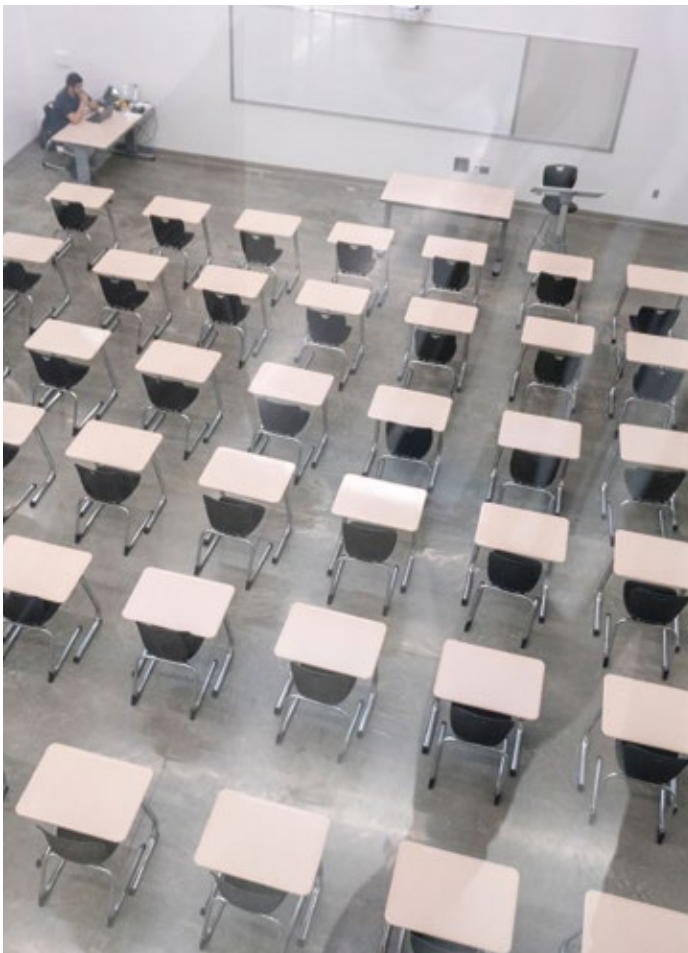

# SAM HOUSTON MATH, SCIENCE, AND TECHNOLOGY CENTER

Sam Houston Math, Science and Technology Center High School was built in 1934 in north Houston. The comprehensive high school offers career pathways in Information Technology through linked learning, an approach that combines rigorous academics with real-world experiences. The school has undergone several renovations, most recently the addition of a new science and laboratory building to support the school's mission of college and career readiness.

Original Budget: **\$101,428,000**  
 Supplemental Funding, Realignment Funding & Adjustments: **\$5,291,029**  
 Trustee: **Elizabeth Santos**  
 Location: **9400 Irvington Blvd.**

DESIGN TEAM		INFORMATION	
HISD Manager	<b>Dan Bankhead</b>	Planning and Design Start	<b>Early/Mid 2015</b>
Architect	<b>Stantec Architecture, Inc.</b>	Construction Start	<b>Mid/Late 2016</b>
Contractor	<b>Satterfield &amp; Pontikes</b>	Phase	<b>Construction</b>
Program Manager	<b>HISD</b>	Percent of Phase	<b>99%</b>

MILESTONES COMPLETED			
Programming/Conceptual Design	<b>Complete</b>	Bid & Award	<b>Complete</b>
Schematic Design Phase	<b>Complete</b>	Construction Start	<b>Complete</b>
Design Development	<b>Complete</b>	Construction Complete	
Construction Documents	<b>Complete</b>	Closeout	

PROJECT PHASE	2013	2014	2015	2016	2017	2018	2019	2020
Planning								
Design								
Construction								
Target Opening								

■ Complete
 ■ In Progress
 ■ Continued Site Development Progress
 ■ Scheduled
 ■ Continued Site Development



# YOUNG WOMEN'S COLLEGE PREPARATORY ACADEMY (YWCPA)

YWCPA opened in the fall of 2011 in midtown to allow young women to experience a small and inclusive environment enriched with a rigorous college preparatory curriculum. Serving students in grades 6 – 12, the campus places a strong emphasis on Advanced Placement and STEM (Science, Technology, Engineering and Math) courses.

Original Budget: **\$27,159,000**

Supplemental Funding, Realignment  
Funding & Adjustments: **\$4,009,189**

Trustee: **Jolanda Jones**

Location: **1906 Cleburne St.**

## DESIGN TEAM


HISD Manager	<b>Andreas Peeples</b>	Planning and Design Start	<b>Early/Mid 2015</b>
Architect	<b>Natex Corporation</b>	Construction Start	<b>Mid/Late 2016</b>
Contractor	<b>Satterfield &amp; Pontikes</b>	Phase	<b>Closeout</b>
Program Manager	<b>Heery International, Inc.</b>	Percent of Phase	<b>90%</b>

## MILESTONES COMPLETED

Programming/Conceptual Design	<b>Complete</b>	Bid & Award	<b>Complete</b>
Schematic Design Phase	<b>Complete</b>	Construction Start	<b>Complete</b>
Design Development	<b>Complete</b>	Construction Complete	<b>Complete</b>
Construction Documents	<b>Complete</b>	Closeout	

PROJECT PHASE	2013	2014	2015	2016	2017	2018	2019	2020
Planning								
Design								
Construction								
Target Opening								

Complete
  In Progress
  Continued Site Development Progress
  Scheduled
  Continued Site Development

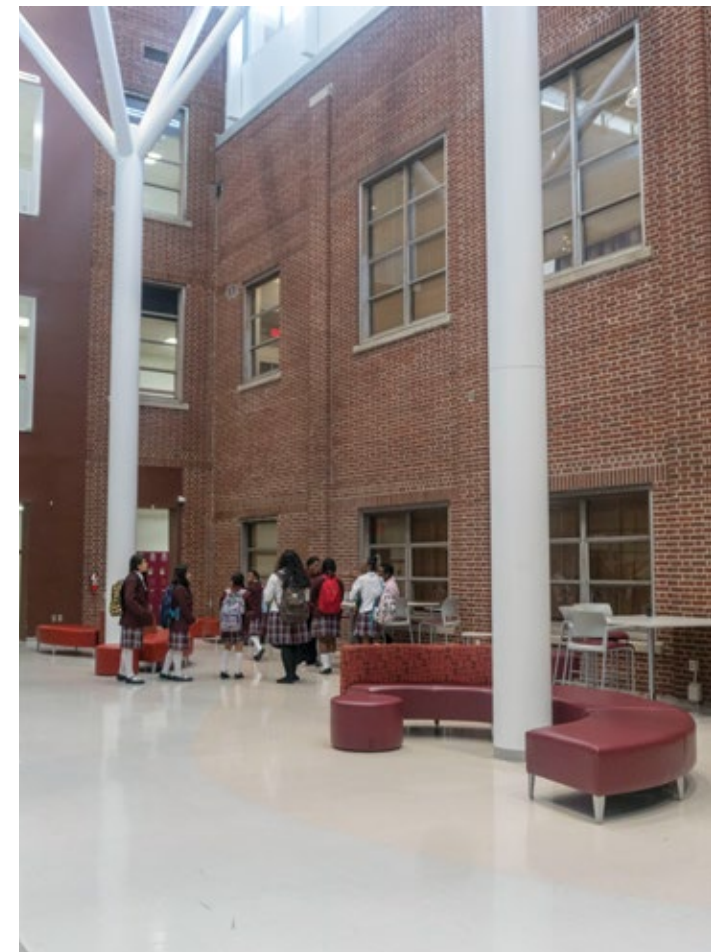



Wilson Montessori



# PROJECT UPDATE REPORT GROUP 4



Garden Oaks Montessori

Planning and Design — Early/Mid 2013 | Anticipated Construction to Begin — Mid/Late 2014

■ Complete    ■ In Progress    ■ Scheduled

	Planning	Design	Construction	Opening
<b>Austin</b> High School	Complete	Complete	In Progress	Scheduled
<b>Garden Oaks</b> Montessori	Complete	Complete	Complete	Complete
<b>Jones</b> Futures Academy	Complete	Complete	Complete	Complete
<b>Kashmere</b> High School	Complete	Complete	Complete	Complete
<b>Madison</b> High School	Complete	Complete	In Progress	Complete
<b>Pilgrim</b> Academy	Complete	Complete	Complete	Complete
<b>Scarborough</b> High School	Complete	Complete	Complete	Complete
<b>Sharpstown</b> International School	Complete	Complete	Complete	Complete
<b>Westbury</b> High School	Complete	Complete	Complete	Complete
<b>Wharton</b> Dual Language Academy	Complete	Complete	Complete	Complete
<b>Wilson</b> Montessori	Complete	Complete	Complete	Complete





# AUSTIN HIGH SCHOOL

Stephen F. Austin High School is located in Houston's East End. The comprehensive high school features career magnet programs in maritime and the teaching professions. The school's main building was built in 1937.

Original Budget: **\$68,429,000**

Supplemental Funding, Realignment Funding & Adjustments: **\$12,511,679**

Trustee: **Diana Dávila**

Location: **1700 Dumble St.**

DESIGN TEAM		INFORMATION	
HISD Manager	<b>Dan Bankhead</b>	Planning and Design Start	<b>Late 2015/Early 2016</b>
Architect	<b>ERO Architects</b>	Construction Start	<b>Late 2016</b>
Contractor	<b>Pepper-Lawson Construction, LP</b>	Phase	<b>Construction</b>
Program Manager	<b>Heery International, Inc.</b>	Percent of Phase	<b>35%</b>

MILESTONES COMPLETED			
Programming/Conceptual Design	<b>Complete</b>	Bid & Award	<b>Complete</b>
Schematic Design Phase	<b>Complete</b>	Construction Start	<b>Complete</b>
Design Development	<b>Complete</b>	Construction Complete	
Construction Documents	<b>Complete</b>	Closeout	

PROJECT PHASE	2013	2014	2015	2016	2017	2018	2019	2020
Planning								
Design								
Construction								
Target Opening								

■ Complete 
 ■ In Progress 
 ■ Continued Site Development Progress 
 ■ Scheduled 
 ■ Continued Site Development

# GARDEN OAKS MONTESSORI

Garden Oaks Montessori is located in Houston's Garden Oaks neighborhood, north of Interstate 610. The school features a Montessori magnet with an emphasis on environmental sciences. The original school was built in 1979 with an addition built in 1981, and relied on eight temporary buildings, as well as a temporary restroom.

Original Budget: **\$26,678,000**

Supplemental Funding, Realignment  
Funding & Adjustments: **\$4,195,956**

Trustee: **Elizabeth Santos**

Location: **901 Sue Barnett Drive**

## DESIGN TEAM

HISD Manager	<b>Andreas Peebles</b>
Architect	<b>Hill Swart Chu Architects, LLC</b>
Contractor	<b>B3CI</b>
Program Manager	<b>Rice &amp; Gardner Consultants, Inc.</b>

## INFORMATION


Planning and Design Start	<b>Late 2015/Early 2016</b>
Construction Start	<b>Mid/Late 2016</b>
Phase	<b>Site Development/Closeout</b>
Percent of Phase	<b>99%/55%</b>

## MILESTONES COMPLETED

Programming/Conceptual Design	<b>Complete</b>	Bid & Award	<b>Complete</b>
Schematic Design Phase	<b>Complete</b>	Construction Start	<b>Complete</b>
Design Development	<b>Complete</b>	Construction Complete	<b>Complete</b>
Construction Documents	<b>Complete</b>	Closeout	

PROJECT PHASE	2013	2014	2015	2016	2017	2018	2019	2020
Planning								
Design								
Construction								
Target Opening								

Complete
  In Progress
  Continued Site Development Progress
  Scheduled
  Continued Site Development

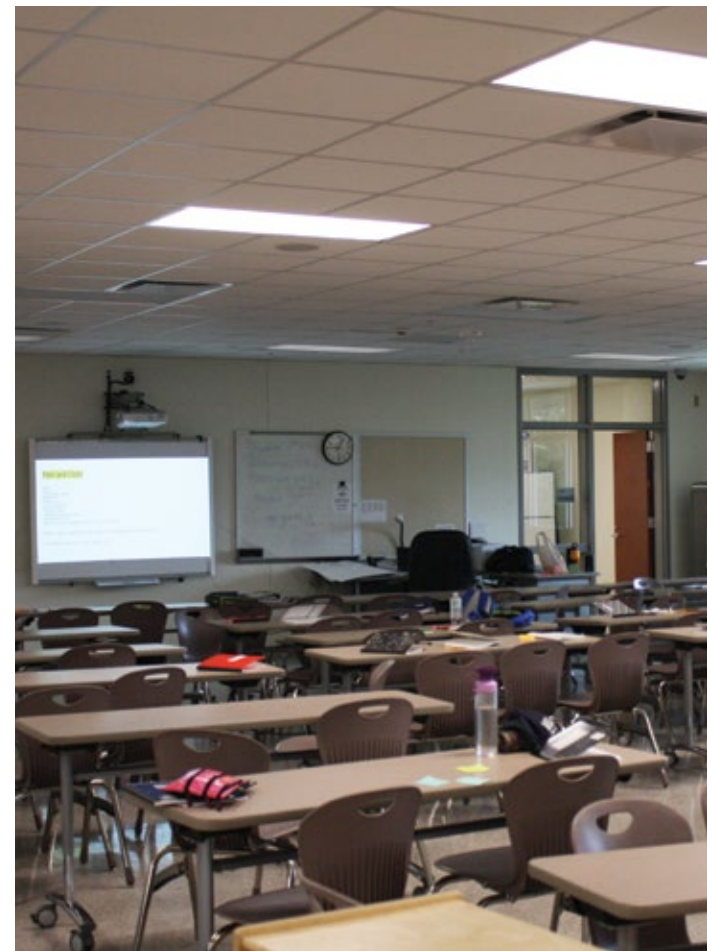



## JONES FUTURES ACADEMY

Original Budget: **\$1,125,000**

Supplemental Funding, Realignment  
Funding & Adjustments: **\$296,011**

Trustee: **Jolanda Jones**

Location: **7414 St. Lo Road**

Jones Futures Academy was constructed in 1956 in southeast Houston. The campus was repurposed into a speciality school in 2014. It now is home to Futures Academy programs in Allied Health and Construction Technology.

### DESIGN TEAM

HISD Manager	<b>Dan Bankhead</b>
Architect	<b>N/A</b>
Contractor	<b>P2MG/Aries</b>
Program Manager	<b>N/A</b>

### INFORMATION

Planning and Design Start	<b>Late 2015/Early 2016</b>
Construction Start	<b>Mid 2016</b>
Phase	<b>Closeout</b>
Percent of Phase	<b>100%</b>

### MILESTONES COMPLETED

Programming/Conceptual Design	<b>Complete</b>	Bid & Award	<b>Complete</b>
Schematic Design Phase	<b>Complete</b>	Construction Start	<b>Complete</b>
Design Development	<b>Complete</b>	Construction Complete	<b>Complete</b>
Construction Documents	<b>Complete</b>	Closeout	<b>Complete</b>

PROJECT PHASE	2013	2014	2015	2016	2017	2018	2019	2020
Planning			■	■				
Design				■				
Construction				■				
Target Opening				■				

■ Complete 
 ■ In Progress 
 ■ Continued Site Development Progress 
 ■ Scheduled 
 ■ Continued Site Development



# KASHMERE HIGH SCHOOL

Kashmere High School is located on Houston's northeast side. It is home to the Futures Academy of Computer Engineering Technology at Kashmere. It also offers a Chemical and Process Technology Institute STEM (Science, Technology, Engineering and Math) magnet, as well as a performing and visual arts magnet. The school was constructed in 1969 and was last renovated in 2000.

Original Budget: **\$17,000,000**

Supplemental Funding, Realignment  
Funding & Adjustments: **\$2,053,729**

Trustee: **Rhonda Skillern-Jones**

Location: **6900 Wileyvale Road**

## DESIGN TEAM


HISD Manager	<b>Andreas Peeples</b>	Planning and Design Start	<b>Late 2015/Early 2016</b>
Architect	<b>Natex Corporation</b>	Construction Start	<b>Early/Mid 2016</b>
Contractor	<b>DT Construction</b>	Phase	<b>Closeout</b>
Program Manager	<b>HISD</b>	Percent of Phase	<b>75%</b>

## MILESTONES COMPLETED

Programming/Conceptual Design	<b>Complete</b>	Bid & Award	<b>Complete</b>
Schematic Design Phase	<b>Complete</b>	Construction Start	<b>Complete</b>
Design Development	<b>Complete</b>	Construction Complete	<b>Complete</b>
Construction Documents	<b>Complete</b>	Closeout	

PROJECT PHASE	2013	2014	2015	2016	2017	2018	2019	2020
Planning								
Design								
Construction								
Target Opening								

Complete
  In Progress
  Continued Site Development Progress
  Scheduled
  Continued Site Development

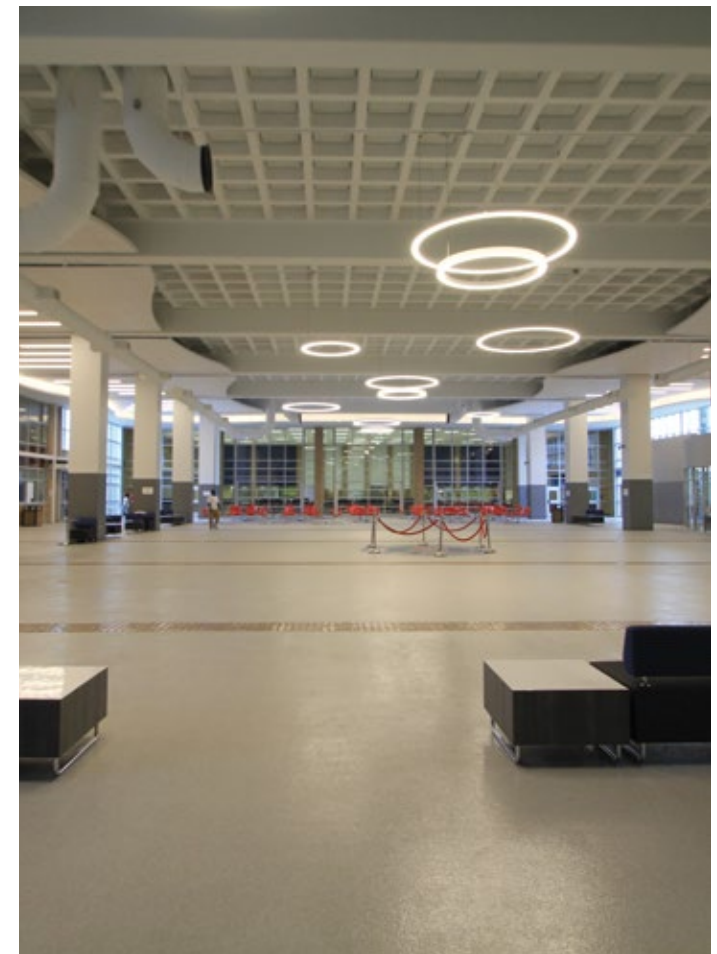



## MADISON HIGH SCHOOL

James Madison High School is a comprehensive high school offering career pathways in environmental science professions and robotics through linked learning, an approach that combines rigorous academics with real-world experiences.

Original Budget: **\$82,736,000**

Supplemental Funding, Realignment  
Funding & Adjustments: **\$4,037,444**

Trustee: **Wanda Adams**

Location: **13719 White Heather Drive**

DESIGN TEAM		INFORMATION	
HISD Manager	<b>Andreas Peeples</b>	Planning and Design Start	<b>Late 2015/Early 2016</b>
Architect	<b>Morris Architects, Inc.</b>	Construction Start	<b>Late 2016</b>
Contractor	<b>Satterfield &amp; Pontikes Construction, Inc.</b>	Phase	<b>Site Development/ Closeout</b>
Program Manager	<b>Heery International, Inc.</b>	Percent of Phase	<b>15%/15%</b>

MILESTONES COMPLETED			
Programming/Conceptual Design	<b>Complete</b>	Bid & Award	<b>Complete</b>
Schematic Design Phase	<b>Complete</b>	Construction Start	<b>Complete</b>
Design Development	<b>Complete</b>	Construction Complete	
Construction Documents	<b>Complete</b>	Closeout	

PROJECT PHASE	2013	2014	2015	2016	2017	2018	2019	2020
Planning								
Design								
Construction								
Target Opening								

■ Complete
 ■ In Progress
 ■ Continued Site Development Progress
 ■ Scheduled
 ■ Continued Site Development

# PILGRIM ACADEMY

Pilgrim Academy was built in 2007 as a neighborhood elementary school in the Galleria area. It that has since expanded to include a middle school program.

Original Budget: **\$7,989,000**

Supplemental Funding, Realignment  
Funding & Adjustments: **\$960,481**

Trustee: **Anne Sung**

Location: **6302 Skyline Drive**

## DESIGN TEAM

HISD Manager	<b>Andreas Peeples</b>	Planning and Design Start	<b>Late 2015/Early 2016</b>
Architect	<b>RDC Architects, PLLC</b>	Construction Start	<b>Mid 2016</b>
Contractor	<b>DT Construction</b>	Phase	<b>Realignment Construction</b>
Program Manager	<b>Heery International, Inc.</b>	Percent of Phase	<b>10%</b>

## MILESTONES COMPLETED

Programming/Conceptual Design	<b>Complete</b>	Bid & Award	<b>Complete</b>
Schematic Design Phase	<b>Complete</b>	Construction Start	<b>Complete</b>
Design Development	<b>Complete</b>	Construction Complete	<b>Complete</b>
Construction Documents	<b>Complete</b>	Closeout	

PROJECT PHASE	2013	2014	2015	2016	2017	2018	2019	2020
Planning								
Design								
Construction								
Target Opening								

■ Complete 
 ■ In Progress 
 ■ Continued Site Development Progress 
 ■ Scheduled 
 ■ Continued Site Development







## SCARBOROUGH HIGH SCHOOL

Scarborough High School is a comprehensive high school located in northwest Houston. The school is home to the Futures Academy for Network & Computer Administration at Scarborough, and also offers career pathways in retail management through linked learning, an approach that combines rigorous academics with real-world experiences.

Original Budget: **\$12,566,000**

Supplemental Funding, Realignment  
Funding & Adjustments: **\$2,077,625**

Trustee: **Elizabeth Santos**

Location: **4141 Costa Rica Road**

DESIGN TEAM		INFORMATION	
HISD Manager	<b>Andreas Peebles</b>	Planning and Design Start	<b>Late 2015/Early 2016</b>
Architect	<b>Randall-Porterfield Architects, Inc.</b>	Construction Start	<b>Mid/Late 2016</b>
Contractor	<b>DT Construction</b>	Phase	<b>Closeout</b>
Program Manager	<b>HISD</b>	Percent of Phase	<b>75%</b>

MILESTONES COMPLETED			
Programming/Conceptual Design	<b>Complete</b>	Bid & Award	<b>Complete</b>
Schematic Design Phase	<b>Complete</b>	Construction Start	<b>Complete</b>
Design Development	<b>Complete</b>	Construction Complete	<b>Complete</b>
Construction Documents	<b>Complete</b>	Closeout	

PROJECT PHASE	2013	2014	2015	2016	2017	2018	2019	2020
Planning								
Design								
Construction								
Target Opening								

Complete
  In Progress
  Continued Site Development Progress
  Scheduled
  Continued Site Development

# SHARPSTOWN INTERNATIONAL SCHOOL

Sharpstown International School was created through the 2011-2012 consolidation of Sharpstown Middle School and the International High School at Sharpstown, a partnership between the district and the Asia Society's International Studies Schools Network.

Original Budget: **\$6,125,000**

Supplemental Funding, Realignment  
Funding & Adjustments: **\$808,379**

Trustee: **Holly Maria Flynn Vilaseca**


Location: **8330 Triola Lane**

DESIGN TEAM		INFORMATION	
HISD Manager	<b>Andreas Peeples</b>	Planning and Design Start	<b>Late 2015/Mid 2016</b>
Architect	<b>Autoarch Architects, Inc.</b>	Construction Start	<b>Early/Mid 2016</b>
Contractor	<b>DT Construction</b>	Phase	<b>Closeout</b>
Program Manager	<b>Rice &amp; Gardner Consultants, Inc.</b>	Percent of Phase	<b>99%</b>

MILESTONES COMPLETED			
Programming/Conceptual Design	<b>Complete</b>	Bid & Award	<b>Complete</b>
Schematic Design Phase	<b>Complete</b>	Construction Start	<b>Complete</b>
Design Development	<b>Complete</b>	Construction Complete	<b>Complete</b>
Construction Documents	<b>Complete</b>	Closeout	

PROJECT PHASE	2013	2014	2015	2016	2017	2018	2019	2020
Planning								
Design								
Construction								
Target Opening								

■ Complete 
 ■ In Progress 
 ■ Continued Site Development Progress 
 ■ Scheduled 
 ■ Continued Site Development





# WESTBURY HIGH SCHOOL

Westbury is a comprehensive high school with a performing and visual arts magnet program, and career pathways in public safety through linked learning, an approach that combines rigorous academics with real-world experiences.

Original Budget: **\$40,006,000**  
 Supplemental Funding, Realignment Funding & Adjustments: **\$20,257,598**  
 Trustee: **Wanda Adams**  
 Location: **11911 Chimney Rock Road**

DESIGN TEAM		INFORMATION	
HISD Manager	Andreas Peeples	Planning and Design Start	Late 2015/Early 2016
Architect	Joiner Partnership, Inc.	Construction Start	Late 2016
Contractor	Satterfield & Pontikes	Phase	Realignment Design
Program Manager	Rice & Gardner Consultants, Inc.	Percent of Phase	95%

MILESTONES COMPLETED			
Programming/Conceptual Design	Complete	Bid & Award	Complete
Schematic Design Phase	Complete	Construction Start	Complete
Design Development	Complete	Construction Complete	Complete
Construction Documents	Complete	Closeout	

PROJECT PHASE	2013	2014	2015	2016	2017	2018	2019	2020
Planning								
Design								
Construction								
Target Opening								

Complete
  In Progress
  Continued Site Development Progress
  Scheduled
  Continued Site Development



# WHARTON DUAL LANGUAGE ACADEMY

Wharton Dual Language Academy features a Spanish dual language magnet program, as well as an International Baccalaureate Primary Years Programme, which encourages younger students to become inquisitive, lifelong learners. It serves students in pre-K through 8th grade.

Original Budget: **\$35,603,000**

Supplemental Funding, Realignment  
Funding & Adjustments: **\$2,482,075**

Trustee: **Diana Dávila**

Location: **900 West Gray St.**

## DESIGN TEAM


HISD Manager	<b>Dan Bankhead</b>	Planning and Design Start	<b>Late 2015/Early 2016</b>
Architect	<b>H. Munoz &amp; Company, Inc.</b>	Construction Start	<b>Late 2016</b>
Contractor	<b>Division One</b>	Phase	<b>Closeout</b>
Program Manager	<b>Heery International, Inc.</b>	Percent of Phase	<b>15%</b>

## MILESTONES COMPLETED

Programming/Conceptual Design	<b>Complete</b>	Bid & Award	<b>Complete</b>
Schematic Design Phase	<b>Complete</b>	Construction Start	<b>Complete</b>
Design Development	<b>Complete</b>	Construction Complete	<b>Complete</b>
Construction Documents	<b>Complete</b>	Closeout	

PROJECT PHASE	2013	2014	2015	2016	2017	2018	2019	2020
Planning								
Design								
Construction								
Target Opening								

■ Complete 
 ■ In Progress 
 ■ Continued Site Development Progress 
 ■ Scheduled 
 ■ Continued Site Development

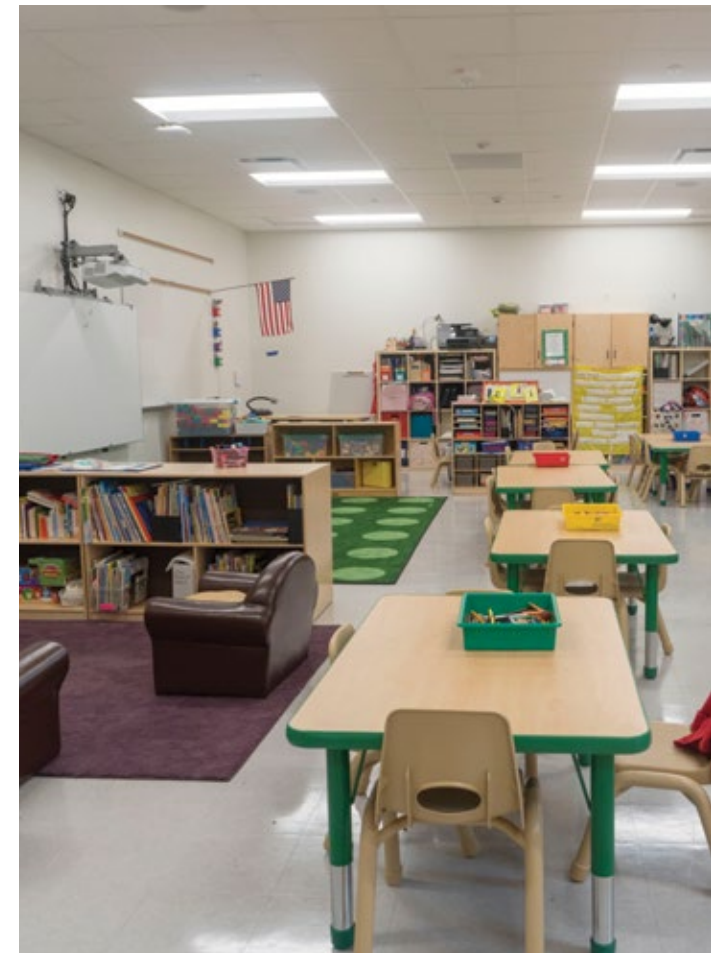



## WILSON MONTESSORI

Wilson Montessori, located in the Montrose area, was constructed as a small elementary school in 1924 and renovated in 2004. In February 2005, HISD and the Friends of Montessori non-profit organization joined together to create HISD's first all-Montessori school.

Original Budget: **\$18,914,000**

Supplemental Funding, Realignment Funding & Adjustments: **\$5,808,033**

Trustee: **Anne Sung**

Location: **2100 Yupon St.**

DESIGN TEAM		INFORMATION	
HISD Manager	<b>Andreas Peeples</b>	Planning and Design Start	<b>Late 2015/Early 2016</b>
Architect	<b>Smith &amp; Company Architects, Inc.</b>	Construction Start	<b>Late 2016</b>
Contractor	<b>Drymalla Construction Co.</b>	Phase	<b>Closeout</b>
Program Manager	<b>Rice &amp; Gardner Consultants, Inc</b>	Percent of Phase	<b>25%</b>

MILESTONES COMPLETED			
Programming/Conceptual Design	<b>Complete</b>	Bid & Award	<b>Complete</b>
Schematic Design Phase	<b>Complete</b>	Construction Start	<b>Complete</b>
Design Development	<b>Complete</b>	Construction Complete	<b>Complete</b>
Construction Documents	<b>Complete</b>	Closeout	

PROJECT PHASE	2013	2014	2015	2016	2017	2018	2019	2020
Planning								
Design								
Construction								
Target Opening								

■ Complete 
 ■ In Progress 
 ■ Continued Site Development Progress 
 ■ Scheduled 
 ■ Continued Site Development



# DISTRICTWIDE PROJECTS



Garden Oaks Montessori





## DISTRICTWIDE PROJECTS

2012 Project Update Report

### **Technology upgrades at all schools: \$100 M**

The 2012 Bond allocated funding for network improvements and wireless expansion.

#### **Project Status**

The 2012 Bond Program allocated \$100 million in funding for technology upgrades, network improvements, and wireless expansion at schools across the district. The scope of the work includes the addition of wireless access points, cabling, and other infrastructure equipment, such as network switches and Voice over Internet Protocol (VoIP). These improvements allow for the expansion of digital instruction, as well as safety and security improvements like telephones in classrooms. As the installation of technology upgrades continue throughout the district, the VoIP project has completed installation of handsets in every classroom and additional phases are still ongoing.

For more information, please visit [HoustonISD.org/voip](http://HoustonISD.org/voip).

### **Middle school restroom renovations: \$35 M**

Renovations of the restrooms in middle schools across HISD.

#### **Project Status**

All projects are complete, and no funds remain. The projects are now in closeout.

### **Safety and security improvements: \$17.3 M**

Improvements include fencing, security cameras, and access control.

#### **Project Status**

All projects have been completed, and no funds remain. The following projects have been completed with 2012 Safety & Security funds:


- Controlled Access - all campuses completed,
- Security Camera upgrades
- Fire Alarm upgrades

### **Land acquisition: \$55.8 million**

Funds to supplement significant site/parking constraints.

#### **Project Status**

With all purchases complete under the 2012 Bond program, the Real Estate department is maintaining and renewing current lease agreements as needed, assisting project managers with land planning issues, and searching for possible sites for future development. The department continues to supplement and maintain the centralized database of key documents for all HISD properties.

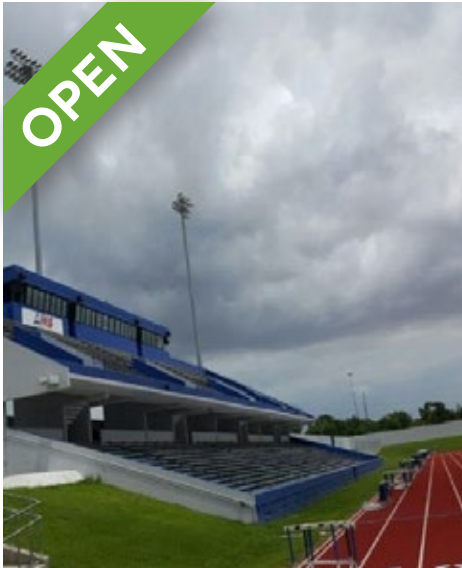

## BARNETT ATHLETIC COMPLEX

Barnett Athletic Complex is a multipurpose facility, including an 8,000-seat football stadium, baseball fields, and fieldhouse.


<b>TOTAL BUDGET</b>	<b>\$4,804,255</b>
---------------------	--------------------

### DESIGN TEAM

HISD Manager	<b>Andreas Peeples</b>
Architect	<b>PBK Architects</b>
Contractor	<b>Prime Contractors</b>
Program Manager	<b>N/A</b>

### INFORMATION

Construction Start	<b>Late 2014</b>
Construction Completion	<b>Early/Mid 2016</b>
Phase	<b>Closeout</b>
Percent of Phase	<b>100%</b>

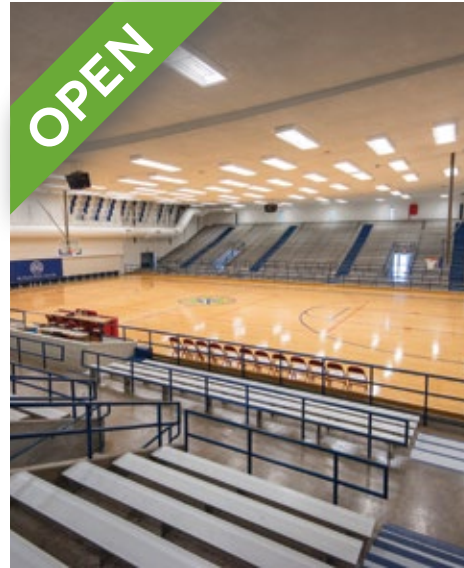

## BUTLER ATHLETIC COMPLEX

Butler Athletic Complex is a multipurpose facility, including an 8,000-seat football stadium, baseball fields, and fieldhouse.

<b>TOTAL BUDGET</b>	<b>\$4,591,811</b>
---------------------	--------------------

### DESIGN TEAM

HISD Manager	<b>Andreas Peeples</b>
Architect	<b>PBK Architects</b>
Contractor	<b>Prime Contractors</b>
Program Manager	<b>N/A</b>

### INFORMATION

Construction Start	<b>Late 2014</b>
Construction Completion	<b>Early 2016</b>
Phase	<b>Closeout</b>
Percent of Phase	<b>100%</b>



## DELMAR FIELDHOUSE

Delmar Fieldhouse is a multipurpose facility, including a 12,000-seat football stadium, baseball fields, and a fieldhouse.

<b>TOTAL BUDGET</b>	<b>\$35,278,934</b>
---------------------	---------------------

### DESIGN TEAM

HISD Manager	<b>Andreas Peeples</b>
Architect	<b>PBK Architects</b>
Contractor	<b>DivisionOne Construction</b>
Program Manager	<b>Rice &amp; Gardner Consultants, Inc.</b>

### INFORMATION

Construction Start	<b>Late 2014</b>
Construction Completion	<b>Early/Mid 2016</b>
Phase	<b>Closeout</b>
Percent of Phase	<b>90%</b>



Kinder HSPVA



# SUPPLIER DIVERSITY (M/WBE) BOND REPORT



**Alexis Licata**  
*Officer, Business Logistics & Purchasing*  
4400 W. 18<sup>th</sup> Street, Level 1 South  
Houston, Texas 77092  
[BusinessAssistance@HoustonISD.org](mailto:BusinessAssistance@HoustonISD.org)



## HISD WORKSHOPS

### WORKSHOP WEDNESDAY

- January – **“How to Do Business With HISD,”** Presenter: Yesenia Taylor, General Manager, Business Solutions
- February – **“Project Management for Controlled Outcomes,”** Presenter: Edgartt Melton, CEO, 7th Echelon LLC
- March – **“Crisis Communication Planning,”** Presenter: Marina A. Coryat, CEO Refined Communications LLC

## M/WBE OUTREACH EVENTS

### EAST END CHAMBER OF COMMERCE

- Business Development Committee Meeting
- Vision Luncheon 2019 Exhibitor

### GREATER HOUSTON BUSINESS PROCUREMENT FORUM

- Procurement Breakfast Exhibitor

### HOUSTON COMMUNITY COLLEGE

- Procurement Expo – “Access To HCC”

### HOUSTON HISPANIC ARCHITECTS AND ENGINEERS

- Luncheon, Guest Speaker

### HOUSTON HISPANIC CHAMBER OF COMMERCE

- 2019 Women’s Leadership Conference & Business Expo

### HOUSTON MINORITY SUPPLIER DEVELOPMENT COUNCIL

- Supplier Diversity Advisory Committee Meeting

### METRO

- METRO Stakeholders Meeting

### NAMC

- National Mid-Winter Conference, MBE Contractor Business Expo

### WOMEN’S BUSINESS ENTERPRISE ALLIANCE

- Corporate Advisory Committee Meeting


## 2012 BOND CONSTRUCTION M/WBE BREAKDOWN BY PROJECT TYPE

Calculations based on numbers reported as of March 31, 2019

### ARCHITECT PROJECTS

TOTAL AWARDED: \$75,822,252


TOTAL COMMITTED: \$40,842,225

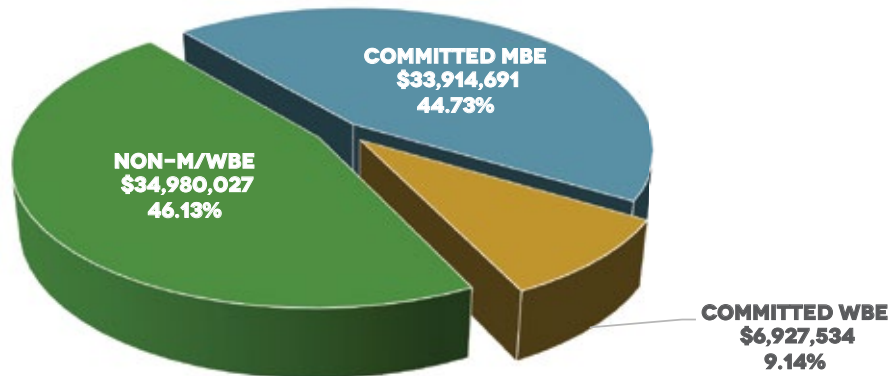

### CONSTRUCTION FIRM PROJECTS

TOTAL AWARDED: \$1,420,548,915

TOTAL COMMITTED: \$313,761,856

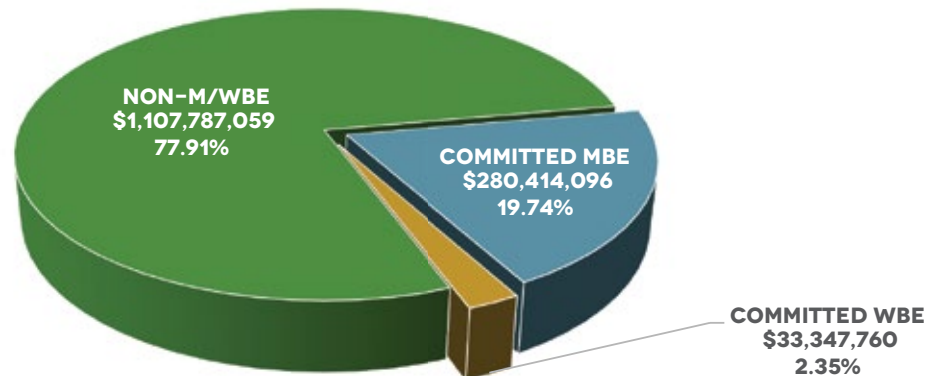




## 2012 BOND CONSTRUCTION M/WBE BREAKDOWN BY PROJECT TYPE

Calculations based on numbers reported as of March 31, 2019

### PROGRAM MANAGEMENT FIRM PROJECTS

**TOTAL AWARDED: \$46,122,559**

**TOTAL COMMITTED: \$19,142,366**

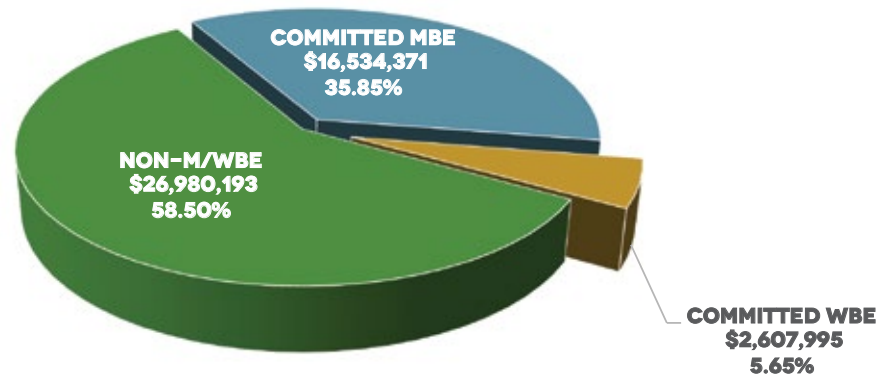


### OTHER PROJECTS/VARIOUS VENDOR COSTS

(INCLUDING OTHER PROGRAM MANAGEMENT FEES & COSTS)


**TOTAL AWARDED: \$297,896,296**

**ACTUAL SPEND: \$144,646,708**

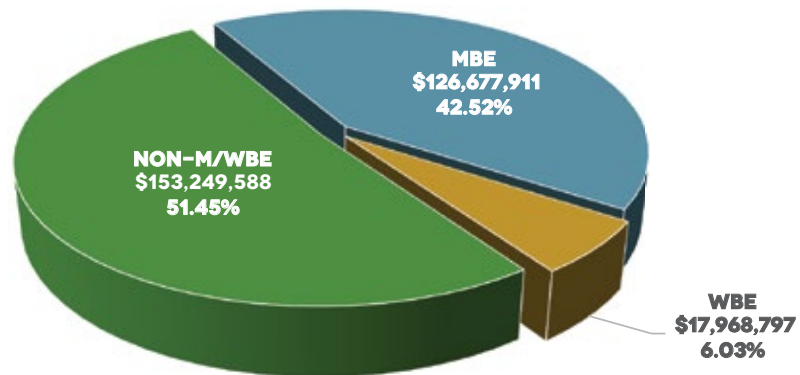

## 2012 BOND CONSTRUCTION M/WBE BREAKDOWN BY PROJECT TYPE

Calculations based on numbers reported as of March 31, 2019

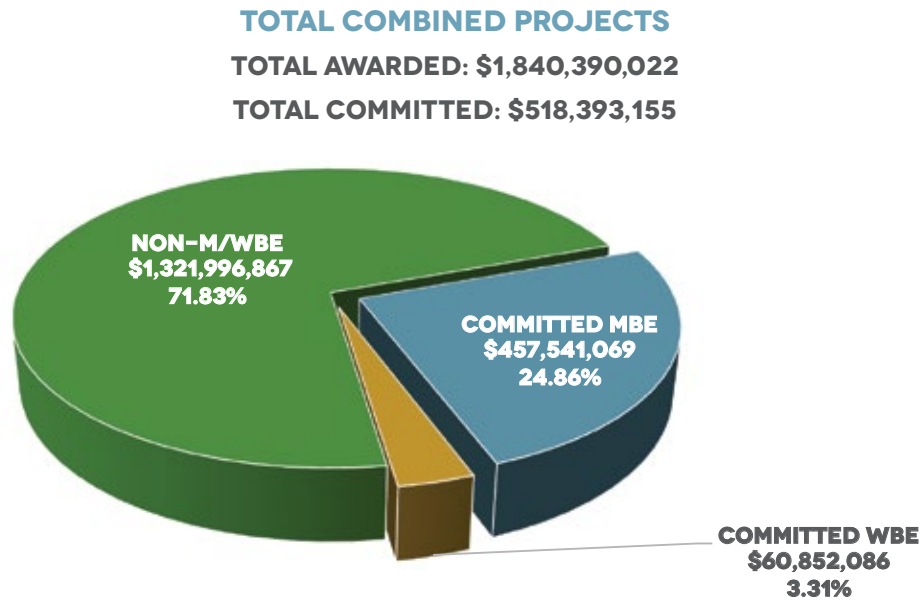

School Name	Vendor / Project Type	VID	Vendor Name	Contracted Amount	Payments to Date	"First Tier MBE Spend"	"First Tier WBE Spend"	Additional MBE Spend	Additional WBE Spend	Second Tier MBE Spend	Second Tier WBE Spend	Actual M/WBE Spend Amount	Actual M/ WBE Spend Percentage	MBE Total Committed	WBE Total Committed
DEBAKEY H S H P	Architect	93999	WHR Architects	\$2,653,473.87	\$2,653,473.87	\$0.00	\$0.00	\$0.00	\$0.00	\$660,760.00	\$143,296.00	\$804,056.00	30.30%	25.00%	
DEBAKEY H S H P	CMAR	85499	Tellepsen Builders, L. P.	\$49,598,236.63	\$49,598,236.63	\$0.00	\$0.00	\$0.00	\$0.00	\$353,963.52	\$4,029,692.96	\$4,383,656.48	8.84%	20.00%	
DEBAKEY H S H P	Other	0	Various Vendors	\$6,661,421.83	\$6,626,137.68	\$1,895,311.47	\$246,373.56	\$0.00	\$0.00	\$0.00	\$0.00	\$2,141,685.03	32.32%		
Total			\$58,913,132.33	\$58,877,848.18											
TANGLEWOOD (FORMERLY GRADY) MIDDLE SCHOOL	Architect	28883	Natex	\$666,711.83	\$666,711.83	\$0.00	\$666,711.83	\$0.00	\$0.00	\$0.00	\$0.00	\$666,711.83	100.00%		100.00%
TANGLEWOOD (FORMERLY GRADY) MIDDLE SCHOOL	CMAR	69826	DivisionOne Construction, LLC	\$10,605,235.52	\$10,605,235.52	\$0.00	\$0.00	\$0.00	\$0.00	\$3,290,060.84	\$25,519.00	\$3,315,579.84	31.26%	29.76%	0.24%
TANGLEWOOD (FORMERLY GRADY) MIDDLE SCHOOL	Other	0	Various Vendors	\$2,346,234.77	\$2,346,234.77	\$1,003,989.32	\$120,767.70	\$0.00	\$0.00	\$0.00	\$0.00	\$1,124,757.02	47.94%		
Total			\$13,618,182.12	\$13,618,182.12											
WISDOM (FORMERLY LEE) HIGH SCHOOL	Architect	93999	WHR/Lake Flato	\$3,342,911.55	\$3,118,208.97	\$0.00	\$0.00	\$0.00	\$0.00	\$189,632.81	\$686,163.00	\$875,795.81	28.09%	25.00%	
WISDOM (FORMERLY LEE) HIGH SCHOOL	CMAR	49451	Satterfield & Pontikes Construction Co.	\$61,245,705.29	\$60,844,253.28	\$0.00	\$0.00	\$0.00	\$0.00	\$131,592.85	\$9,923,053.30	\$10,054,646.15	16.53%	20.00%	
WISDOM (FORMERLY LEE) HIGH SCHOOL	Other	0	Various Vendors	\$6,961,459.47	\$6,844,222.13	\$1,682,286.59	\$1,325,899.52	\$0.00	\$0.00	\$0.00	\$0.00	\$3,008,186.11	43.95%		
Total			\$71,550,076.31	\$70,806,684.38											
MANDARIN CHINESE LANGUAGE IMMERSION MAGNET SCHOOL	Architect	43325	PBK Architects	\$1,273,717.47	\$1,273,717.47	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$126,568.03	\$126,568.03	9.94%	25.00%	
MANDARIN CHINESE LANGUAGE IMMERSION MAGNET SCHOOL	CMAR	49451	Satterfield & Pontikes Construction Co.	\$27,801,689.56	\$27,801,689.56	\$0.00	\$0.00	\$0.00	\$0.00	\$8,741,709.31	\$50,226.79	\$8,791,936.10	31.62%	20.00%	
MANDARIN CHINESE LANGUAGE IMMERSION MAGNET SCHOOL	Other	0	Various Vendors	\$3,016,770.57	\$3,013,148.07	\$1,045,912.31	\$113,732.46	\$0.00	\$0.00	\$0.00	\$0.00	\$1,159,644.77	38.44%		
Total			\$32,092,177.60	\$32,088,555.10											
MARK WHITE ELEMENTARY SCHOOL	Architect	42900	English & Associates	\$875,707.24	\$868,051.04	\$0.00	\$875,707.24	\$0.00	\$0.00	\$0.00	\$0.00	\$875,707.24	100.00%		100.00%
MARK WHITE ELEMENTARY SCHOOL	CMAR	69826	DivisionOne Construction, LLC	\$17,744,123.00	\$17,744,123.00	\$0.00	\$0.00	\$0.00	\$0.00	\$3,990,179.33	\$0.00	\$3,990,179.33	22.49%	20.00%	
MARK WHITE ELEMENTARY SCHOOL	Other	0	Various Vendors	\$4,059,035.79	\$4,057,562.84	\$2,538,951.14	\$173,371.78	\$0.00	\$0.00	\$0.00	\$0.00	\$2,712,322.92	66.82%		
Total			\$22,678,866.03	\$22,669,736.88											
MICKEY LELAND COLLEGE PREPARATORY ACADEMY (YMCPA)	Architect	85021	Harrison Kornberg	\$1,398,632.55	\$1,385,097.50	\$1,398,632.55	\$0.00	\$446,257.50	\$0.00	\$446,257.50	\$0.00	\$1,844,890.05	131.91%	100.00%	
MICKEY LELAND COLLEGE PREPARATORY ACADEMY (YMCPA)	CSP	22036	Prime Contractors	\$24,941,586.02	\$24,941,586.02	\$0.00	\$0.00	\$0.00	\$0.00	\$316,360.94	\$5,332,771.85	\$5,649,132.79	22.65%		20.76%
MICKEY LELAND COLLEGE PREPARATORY ACADEMY (YMCPA)	Other	0	Various Vendors	\$1,573,539.00	\$1,522,733.55	\$2,955,658.11	\$245,345.73	\$0.00	\$0.00	\$0.00	\$0.00	\$3,201,003.84	210.21%		
Total			\$27,913,757.57	\$27,849,417.07											
MILBY HIGH SCHOOL	Architect	46141	Kirksey Architecture	\$3,198,410.48	\$3,198,410.48	\$0.00	\$0.00	\$0.00	\$0.00	\$864,645.01	\$38,675.00	\$903,320.01	28.24%	25.00%	
MILBY HIGH SCHOOL	CMAR	85499	Tellepsen Builders, L. P.	\$58,455,316.17	\$58,377,710.17	\$0.00	\$0.00	\$0.00	\$0.00	\$7,999,962.45	\$3,990.00	\$8,003,952.45	13.71%	12.14%	7.86%
MILBY HIGH SCHOOL	Other	0	Various Vendors	\$14,665,327.61	\$11,934,235.22	\$5,089,426.18	\$1,059,917.36	\$0.00	\$0.00	\$0.00	\$0.00	\$6,149,343.54	41.93%		
Total			\$76,319,054.26	\$73,510,355.87											
NORTH HOUSTON EARLY COLLEGE HIGH SCHOOL	Architect	54154	RDLR Architects	\$665,228.31	\$665,228.31	\$665,228.31	\$0.00	\$39,971.00	\$12,000.00	\$39,971.00	\$12,000.00	\$717,199.31	107.81%	100.00%	
NORTH HOUSTON EARLY COLLEGE HIGH SCHOOL	CMAR	50632	Drymalla Construction Company Inc.	\$11,597,258.11	\$11,597,258.11	\$0.00	\$0.00	\$0.00	\$0.00	\$2,341,368.61	\$107,588.95	\$2,448,957.56	21.12%	16.19%	3.81%
NORTH HOUSTON EARLY COLLEGE HIGH SCHOOL	Other	0	Various Vendors	\$-2,236,836.87	\$-2,240,696.04	\$588,645.72	\$135,635.98	\$0.00	\$0.00	\$0.00	\$0.00	\$724,281.70	-32.32%		
Total			\$10,025,649.55	\$10,021,790.38											
SHARPSTOWN HIGH SCHOOL	Architect	94041	Munoz & Company	\$2,205,002.11	\$2,143,091.67	\$2,205,002.11	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$2,205,002.11	100.00%	100.00%	
SHARPSTOWN HIGH SCHOOL	CMAR	31464	ICI Construction	\$47,500,156.64	\$47,020,235.73	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$526,591.63	\$526,591.63	1.11%	20.00%	3.50%
SHARPSTOWN HIGH SCHOOL	Other	0	Various Vendors	\$6,241,413.66	\$6,018,903.10	\$2,965,612.39	\$155,731.85	\$0.00	\$0.00	\$0.00	\$0.00	\$3,121,344.24	50.01%		
Total			\$55,946,572.41	\$55,182,230.50											



School Name	Vendor / Project Type	VID	Vendor Name	Contracted Amount	Payments to Date	*First Tier MBE Spend	*First Tier WBE Spend	Additional MBE Spend	Additional WBE Spend	Second Tier MBE Spend	Second Tier WBE Spend	Actual M/WBE Spend Amount	Actual M/ WBE Spend Percentage	MBE Total Committed	WBE Total Committed
SOUTH EARLY COLLEGE HIGH SCHOOL (EMPOWERMENT)	Architect	84380	Smith & Company Architects, Inc.	\$642,300.00	\$623,365.00	\$642,300.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$642,300.00	100.00%	100.00%	
SOUTH EARLY COLLEGE HIGH SCHOOL (EMPOWERMENT)	CMAR	50632	Drymalla Construction Company Inc.	\$10,706,650.29	\$10,706,650.29	\$0.00	\$0.00	\$499,999.88	\$948,129.30	\$499,999.88	\$948,129.30	\$1,448,129.18	13.53%	12.54%	7.46%
SOUTH EARLY COLLEGE HIGH SCHOOL (EMPOWERMENT)	Other	0	Various Vendors	-\$1,655,823.41	-\$1,668,445.91	\$951,583.74	\$60,290.36	\$0.00	\$0.00	\$0.00	\$0.00	\$1,011,874.10	-60.65%		
Total				\$0,693,126.88	\$9,661,569.38										
STERLING HIGH SCHOOL	Architect	95998	Stantec Architecture Inc.	\$773,488.62	\$773,488.62	\$0.00	\$0.00	\$0.00	\$0.00	\$178,200.00	\$511,870.00	\$690,070.00	89.22%	25.00%	
STERLING HIGH SCHOOL	CMAR	86036	Cadence McShane Construction, Inc.	\$49,870,336.63	\$49,870,336.63	\$0.00	\$0.00	\$0.00	\$0.00	\$7,627,739.80	\$1,725,792.99	\$9,353,532.19	18.76%	20.00%	1.00%
STERLING HIGH SCHOOL	Other	0	Various Vendors	\$6,951,644.58	\$6,912,179.56	\$1,947,132.53	\$156,931.97	\$0.00	\$0.00	\$0.00	\$0.00	\$2,104,064.50	30.44%		
Total				\$57,595,469.83	\$57,556,004.81										
WALTRIP HIGH SCHOOL	Architect	66051	Gensler	\$1,301,029.05	\$1,301,029.05	\$0.00	\$0.00	\$0.00	\$0.00	\$242,210.00	\$50,035.00	\$292,245.00	22.46%	25.00%	
WALTRIP HIGH SCHOOL	CMAR	49451	Satterfield & Pontikes Construction Co.	\$35,318,620.59	\$35,201,141.59	\$0.00	\$0.00	\$0.00	\$0.00	\$5,477,089.02	\$0.00	\$5,477,089.02	15.56%	20.00%	
WALTRIP HIGH SCHOOL	Other	0	Various Vendors	-\$6,874,858.59	-\$7,296,458.91	\$556,994.73	\$406,133.29	\$0.00	\$0.00	\$0.00	\$0.00	\$963,128.02	-13.20%		
Total				\$29,744,791.05	\$29,205,711.73										
WASHINGTON HIGH SCHOOL	Architect	93882	Fanning-Howey House Partners, Liliac	\$2,543,788.09	\$2,526,316.10	\$0.00	\$0.00	\$0.00	\$0.00	\$1,045,686.56	\$43,886.00	\$1,089,572.56	42.83%	35.00%	
WASHINGTON HIGH SCHOOL	CMAR	83660	Corner Rock Construction, LLC	\$396,802.20	\$390,135.55	\$0.00	\$396,802.20	\$0.00	\$0.00	\$0.00	\$0.00	\$396,802.20	100.00%	100.00%	
WASHINGTON HIGH SCHOOL	CMAR	22036	Prime Contractors	\$46,387,491.75	\$46,216,211.67	\$0.00	\$0.00	\$0.00	\$0.00	\$7,822,916.22	\$572,048.96	\$8,394,965.18	18.10%	20.38%	
WASHINGTON HIGH SCHOOL	Other	0	Various Vendors	\$8,773,498.12	\$5,776,120.60	\$2,278,436.92	\$1,274,492.23	\$0.00	\$0.00	\$0.00	\$0.00	\$3,552,929.15	40.50%		
Total				\$58,101,580.16	\$54,908,783.92										
WORTHING HIGH SCHOOL	Architect	19286	Molina Walker Architects, Inc.	\$643,781.78	\$622,400.45	\$0.00	\$643,781.78	\$0.00	\$0.00	\$0.00	\$0.00	\$643,781.78	100.00%		100.00%
WORTHING HIGH SCHOOL-PHASE I	CMAR	94301	Balfour/3CI ( A Joint Venture-B3CI)	\$18,942,052.27	\$18,942,052.27	\$0.00	\$0.00	\$0.00	\$0.00	\$8,145,434.17	\$414,313.13	\$8,559,747.30	45.19%	40.00%	
WORTHING HIGH SCHOOL	CSP	22036	Prime Contractors	\$22,212,789.09	\$22,002,653.03	\$0.00	\$0.00	\$0.00	\$0.00	\$4,722,597.05	\$1,744,725.43	\$6,467,322.48	29.39%	20.40%	
WORTHING HIGH SCHOOL	Other	0	Various Vendors	-\$11,306,344.34	-\$11,487,271.70	\$640,450.87	\$72,821.09	\$0.00	\$0.00	\$0.00	\$0.00	\$713,271.96	-6.21%		
Total				\$30,492,278.80	\$30,079,834.05										
BELLAIRE HIGH SCHOOL	Architect	43325	PBK Architects	\$7,007,103.94	\$4,602,683.12	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$235,093.32	\$235,093.32	5.11%	25.00%	
BELLAIRE HIGH SCHOOL	CMAR	87068	Turner Construction Company	\$29,386,537.00	\$8,339,754.24	\$0.00	\$0.00	\$0.00	\$0.00	\$934,791.83	\$2,130,695.26	\$3,065,487.09	0.00%	20.00%	
BELLAIRE HIGH SCHOOL	Other	0	Various Vendors	\$1,306,341.79	\$1,101,752.81	\$305,830.88	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$305,830.88	27.76%		
Total				\$37,699,982.73	\$14,044,190.17										
NORTHSIDE (FORMERLY DAVIS) HIGH SCHOOL	Architect	42898	BAY-IBI	\$3,403,728.64	\$2,965,994.89	\$0.00	\$0.00	\$0.00	\$0.00	\$106,734.54	\$617,863.42	\$724,597.96	24.43%	27.00%	
NORTHSIDE (FORMERLY DAVIS) HIGH SCHOOL	CMAR	49451	Satterfield & Pontikes Const.	\$47,702,971.64	\$37,104,766.71	\$0.00	\$0.00	\$0.00	\$0.00	\$6,845,691.78	\$339,882.62	\$7,185,574.40	19.37%	20.00%	
NORTHSIDE (FORMERLY DAVIS) HIGH SCHOOL	Other	0	Various Vendors	\$6,188,610.25	\$5,080,309.03	\$3,882,099.02	\$488,385.24	\$0.00	\$0.00	\$0.00	\$0.00	\$4,370,484.26	86.03%		
Total				\$57,295,310.53	\$45,151,070.63										
LAWSON (FORMERLY DOWLING) MIDDLE SCHOOL	Architect	85021	Harrison Kornberg	\$2,241,204.55	\$2,124,142.62	\$2,241,204.55	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$2,241,204.55	100.00%	100.00%	
LAWSON (FORMERLY DOWLING) MIDDLE SCHOOL	CMAR	87068	Turner Construction Company	\$49,631,687.39	\$48,563,721.73	\$0.00	\$0.00	\$0.00	\$0.00	\$1,394,211.50	\$5,619,607.64	\$7,013,819.14	14.44%	20.00%	
LAWSON (FORMERLY DOWLING) MIDDLE SCHOOL	Other	0	Various Vendors	\$4,888,075.20	\$4,621,539.83	\$1,628,187.24	\$100,011.93	\$0.00	\$0.00	\$0.00	\$0.00	\$1,728,199.17	37.39%		
Total				\$56,760,967.14	\$55,309,404.18										
EASTWOOD ACADEMY HIGH SCHOOL	Architect	18703	Prozign	\$452,016.12	\$439,725.12	\$0.00	\$0.00	\$0.00	\$0.00	\$76,175.80	\$10,350.00	\$86,525.80	19.68%	26.00%	
EASTWOOD ACADEMY HIGH SCHOOL	CSP	95323	Patriot Contracting, LLC	\$10,332,547.77	\$10,441,218.82	\$0.00	\$0.00	\$0.00	\$0.00	\$423,954.90	\$1,408,250.12	\$1,832,205.02	17.55%	20.13%	
EASTWOOD ACADEMY HIGH SCHOOL	Other	0	Various Vendors	\$241,115.00	-\$9,586.48	\$508,680.42	\$31,570.34	\$0.00	\$0.00	\$0.00	\$0.00	\$540,250.76	-5635.55%		
Total				\$11,025,678.89	\$10,871,357.46										

School Name	Vendor / Project Type	VID	Vendor Name	Contracted Amount	Payments to Date	"First Tier MBE Spend"	"First Tier WBE Spend"	Additional MBE Spend	Additional WBE Spend	Second Tier MBE Spend	Second Tier WBE Spend	Actual M/WBE Spend Amount	Actual M/ WBE Spend Percentage	MBE Total Committed	WBE Total Committed
LAMAR HIGH SCHOOL	Architect	93937	Perkins-Will	\$5,628,045.57	\$4,516,449.68	\$0.00	\$0.00	\$0.00	\$0.00	\$475,838.80	\$664,477.78	\$1,140,316.58	25.25%	30.00%	
LAMAR HIGH SCHOOL	CMAR	39943	Gilbane Building Company	\$105,450,359.00	\$69,330,998.01	\$0.00	\$0.00	\$0.00	\$0.00	\$5,700.00	\$4,552,170.66	\$4,552,870.66	6.57%	25.00%	5.00%
LAMAR HIGH SCHOOL	Other	0	Various Vendors	-\$756,281.99	-\$3,800,557.44	\$2,556,344.15	\$55,910.00	\$0.00	\$0.00	\$0.00	\$0.00	\$2,612,254.15	-72.55%		
Total			\$110,322,122.58	\$70,246,890.25											
PARKER ELEMENTARY SCHOOL	Architect	65961	Brave Architecture	\$1,505,643.25	\$1,448,842.28	\$1,505,643.25	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$1,505,643.25	100.00%	100.00%	
PARKER ELEMENTARY SCHOOL	CMAR	95323	Patriot Contracting, LLC	\$23,905,068.81	\$23,904,200.43	\$0.00	\$0.00	\$0.00	\$0.00	\$722,445.58	\$4,951,712.98	\$5,674,158.56	23.74%	15.04%	5.00%
PARKER ELEMENTARY SCHOOL	Other	0	Various Vendors	\$4,265,360.18	\$4,021,647.17	\$2,198,816.62	\$246,220.46	\$0.00	\$0.00	\$0.00	\$0.00	\$2,445,037.08	60.80%		
Total			\$29,676,072.24	\$29,374,689.88											
YATES HIGH SCHOOL	Architect	94088	Moody-NotariHuerta Associates	\$2,422,806.21	\$2,289,886.72	\$2,422,806.21	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$2,422,806.21	100.00%	100.00%	
YATES HIGH SCHOOL	CMAR	87068	Turner Construction Company	\$56,020,390.99	\$53,251,124.39	\$0.00	\$0.00	\$0.00	\$0.00	\$7,142,958.75	\$1,476,696.42	\$8,619,655.17	16.19%	20.00%	
YATES HIGH SCHOOL	Other	0	Various Vendors	\$9,589,176.45	\$6,046,659.79	\$2,417,696.36	\$47,134.35	\$0.00	\$0.00	\$0.00	\$0.00	\$2,464,830.71	40.76%		
Total			\$68,032,373.65	\$61,587,670.90											
ASKEW ELEMENTARY SCHOOL	Architect	68861	Cre8 Architects	\$943,114.33	\$868,618.33	\$943,114.33	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$943,114.33	100.00%	100.00%	
ASKEW ELEMENTARY SCHOOL	CMAR	50632	Drymalla Construction Company Inc.	\$19,230,254.00	\$18,951,014.00	\$0.00	\$0.00	\$0.00	\$0.00	\$4,648,639.39	\$616,610.80	\$5,265,250.19	27.78%	24.61%	3.39%
ASKEW ELEMENTARY SCHOOL	Other	0	Various Vendors	\$5,303,502.95	\$5,032,516.98	\$1,455,013.38	\$1,088,428.09	\$0.00	\$0.00	\$0.00	\$0.00	\$2,543,441.47	50.54%		
Total			\$25,476,871.28	\$24,852,149.31											
FURR HIGH SCHOOL	Architect	93936	ERO International LLP	\$1,942,912.37	\$1,918,027.55	\$1,942,912.37	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$1,942,912.37	100.00%	100.00%	
FURR HIGH SCHOOL	CSP	22036	Prime Contractors	\$44,350,326.23	\$43,575,726.71	\$0.00	\$0.00	\$0.00	\$0.00	\$2,510,246.14	\$9,600,261.19	\$12,110,507.33	27.79%	20.00%	3.67%
FURR HIGH SCHOOL	Other	0	Various Vendors	\$4,573,148.10	\$4,390,406.56	\$1,223,020.37	\$1,106,369.49	\$0.00	\$0.00	\$0.00	\$0.00	\$2,329,389.86	53.06%		
Total			\$50,866,386.70	\$49,884,160.82											
HIGH SCHOOL FOR PERFORMING & VISUALARTS	Architect	66051	Gensler	\$3,398,436.49	\$3,361,617.51	\$0.00	\$0.00	\$0.00	\$0.00	\$1,041,953.97	\$98,500.00	\$1,140,453.97	33.93%	25.00%	
HIGH SCHOOL FOR PERFORMING & VISUALARTS	CMAR	97384	Mccarthy Building Companies	\$78,121,873.66	\$78,044,514.30	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$96,812.50	\$96,812.50	0.12%	20.00%	
HIGH SCHOOL FOR PERFORMING & VISUALARTS	Other	0	Various Vendors	\$1,676,559.07	\$1,360,440.65	\$1,223,901.06	\$952,969.68	\$0.00	\$0.00	\$300.00	\$9,133.00	\$2,186,303.74	160.71%		
Total			\$83,196,869.22	\$82,766,572.46											
JORDAN HIGH SCHOOL	Architect	85938	Corgan Associates, Inc. DBA Corgan	\$1,359,485.97	\$1,202,199.97	\$0.00	\$0.00	\$0.00	\$0.00	\$238,869.50	\$75,410.00	\$314,279.50	26.14%	20.50%	4.50%
JORDAN HIGH SCHOOL	CSP	86036	Cadence McShane Construction, Inc.	\$29,017,875.00	\$25,307,627.02	\$0.00	\$0.00	\$0.00	\$0.00	\$624,137.21	\$3,146,546.30	\$3,770,683.51	14.90%	13.37%	9.89%
JORDAN HIGH SCHOOL	Other	0	Various Vendors	-\$438,900.38	-\$1,152,502.67	\$1,771,120.18	\$46,812.05	\$0.00	\$0.00	\$56,566.25	\$0.00	\$1,874,498.48	-162.65%		
Total			\$29,938,460.59	\$25,357,324.32											
SAM HOUSTON MATH SCIENCE AND TECHNOLOGY CENTER	Architect	95998	Stantec Architecture Inc.	\$4,239,146.20	\$3,687,662.30	\$0.00	\$0.00	\$0.00	\$0.00	\$450,057.80	\$404,500.41	\$854,558.21	23.17%	25.00%	
SAM HOUSTON MATH SCIENCE AND TECHNOLOGY CENTER	CMAR	49451	Satterfield & Pontikes Construction Co.	\$80,302,331.00	\$74,896,306.36	\$0.00	\$0.00	\$0.00	\$0.00	\$13,900,642.70	\$1,761,005.31	\$15,661,648.01	20.91%	20.00%	
SAM HOUSTON MATH SCIENCE AND TECHNOLOGY CENTER	Other	0	Various Vendors	\$10,156,050.89	\$8,240,531.96	\$2,570,508.59	\$179,341.20	\$0.00	\$0.00	\$0.00	\$0.00	\$2,749,849.79	33.37%		
Total			\$94,697,528.09	\$86,824,500.62											
YOUNG WOMEN'S COLLEGE PREPARATORY ACADEMY (YWCPA)	Architect	28883	Natex	\$1,394,747.09	\$1,386,687.08	\$0.00	\$1,394,747.09	\$0.00	\$0.00	\$0.00	\$0.00	\$1,394,747.09	100.00%		100.00%
YOUNG WOMEN'S COLLEGE PREPARATORY ACADEMY (YWCPA)	CMAR	49451	Satterfield & Pontikes Const.	\$25,136,617.86	\$25,111,670.09	\$0.00	\$0.00	\$0.00	\$0.00	\$4,552,151.97	\$501,345.71	\$5,053,497.68	20.12%	20.00%	
YOUNG WOMEN'S COLLEGE PREPARATORY ACADEMY (YWCPA)	Other	0	Various Vendors	\$2,943,660.46	\$2,747,955.18	\$1,096,686.28	\$290,046.30	\$0.00	\$0.00	\$0.00	\$0.00	\$1,386,732.58	50.46%		
Total			\$29,475,025.41	\$29,246,312.35											

School Name	Vendor / Project Type	VID	Vendor Name	Contracted Amount	Payments to Date	"First Tier MBE Spend"	"First Tier WBE Spend"	Additional MBE Spend	Additional WBE Spend	Second Tier MBE Spend	Second Tier WBE Spend	Actual M/WBE Spend Amount	Actual M/ WBE Spend Percentage	MBE Total Committed	WBE Total Committed
AUSTIN HIGH SCHOOL	Architect	93036	ERO International LLP	\$2,801,625.11	\$2,140,473.11	\$2,801,625.11	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$2,801,625.11	100.00%	100.00%	
AUSTIN HIGH SCHOOL	CMAR	99538	Pepper-Lawson Construction, L.P.	\$63,876,159.37	\$20,615,548.77	\$0.00	\$0.00	\$0.00	\$0.00	\$1,761,026.93	\$0.00	\$1,761,026.93	8.54%	22.00%	
AUSTIN HIGH SCHOOL	Other	0	Various Vendors	\$5,471,276.95	\$3,258,865.47	\$1,937,157.35	\$116,863.30	\$0.00	\$0.00	\$0.00	\$0.00	\$2,054,020.65	63.03%		
Total			\$72,149,061.43	\$26,014,887.35											
GARDEN OAKS MONTESSORI	Architect	96882	Hill Swart Chu Architects	\$1,261,667.27	\$1,196,324.61	\$0.00	\$1,261,667.27	\$0.00	\$0.00	\$0.00	\$0.00	\$1,261,667.27	100.00%		100.00%
GARDEN OAKS MONTESSORI	CMAR	94301	Balfour/3CI ( A Joint Venture-B3CI)	\$22,331,617.00	\$21,553,382.67	\$0.00	\$0.00	\$0.00	\$0.00	\$6,673,779.46	\$1,338,182.77	\$8,011,962.23	37.17%	30.00%	
GARDEN OAKS MONTESSORI	Other	0	Various Vendors	\$3,711,492.61	\$3,473,679.90	\$1,362,982.81	\$230,184.55	\$0.00	\$0.00	\$0.00	\$0.00	\$1,593,167.36	45.86%		
Total			\$27,304,776.88	\$26,223,387.18											
JONES FUTURES ACADEMY	Other	0	Various Vendors	\$531,498.00	\$531,498.00	\$209,782.54	\$64,296.84	\$0.00	\$0.00	\$0.00	\$0.00	\$274,079.38	0.00%		
Total			\$531,498.00	\$531,498.00											
KASHMERE HIGH SCHOOL	Architect	28883	Natex	\$816,618.44	\$807,467.57	\$0.00	\$816,618.44	\$0.00	\$0.00	\$0.00	\$0.00	\$816,618.44	100.00%		100.00%
KASHMERE HIGH SCHOOL	CSP	52387	Dt Construction	\$14,219,592.91	\$14,219,592.91	\$0.00	\$0.00	\$0.00	\$0.00	\$586,075.35	\$3,586,993.31	\$4,173,068.66	29.35%	5.00%	15.00%
KASHMERE HIGH SCHOOL	Other	0	Various Vendors	\$1,916,178.55	\$1,824,308.05	\$735,024.27	\$277,427.90	\$0.00	\$0.00	\$0.00	\$0.00	\$1,012,452.17	55.50%		
Total			\$16,962,389.90	\$16,851,368.53											
MADISON HIGH SCHOOL	Architect	95996	Morris Architects, Inc.	\$3,077,762.83	\$2,827,655.83	\$0.00	\$0.00	\$0.00	\$0.00	\$491,451.10	\$782,847.00	\$1,274,298.10	45.07%	52.00%	
MADISON HIGH SCHOOL	CMAR	49451	Satterfield and Pontikes Construction, Inc.	\$60,943,392.61	\$54,509,105.31	\$0.00	\$0.00	\$0.00	\$0.00	\$948,291.60	\$99,396.33	\$1,047,687.93	1.92%	20.00%	
MADISON HIGH SCHOOL	Other	0	Various Vendors	\$11,644,516.18	\$10,497,845.00	\$3,679,112.08	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$3,679,112.08	35.05%		
Total			\$75,665,671.62	\$67,834,606.14											
PILGRIM ACADEMY	Architect	34980	RDC Architects	\$284,040.18	\$258,467.38	\$284,040.18	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$284,040.18	100.00%	100.00%	
PILGRIM ACADEMY	CSP	52387	Dt Construction	\$5,572,369.81	\$5,572,369.81	\$0.00	\$0.00	\$0.00	\$0.00	\$899,847.66	\$217,370.43	\$1,117,218.09	20.05%	20.19%	
PILGRIM ACADEMY	Other	0	Various Vendors	\$1,723,267.66	\$1,520,394.71	\$817,487.17	\$21,846.98	\$0.00	\$0.00	\$0.00	\$0.00	\$839,334.15	54.88%		
Total			\$7,579,677.65	\$7,360,231.90											
SCARBOROUGH HIGH SCHOOL	Architect	95997	Randall-Porterfield	\$763,615.04	\$762,467.47	\$0.00	\$0.00	\$0.00	\$0.00	\$68,346.81	\$0.00	\$68,346.81	8.96%	25.00%	
SCARBOROUGH HIGH SCHOOL	CSP	52387	Dt Construction	\$9,678,650.88	\$9,678,650.88	\$0.00	\$0.00	\$0.00	\$0.00	\$1,987,583.67	\$328,529.39	\$2,316,113.06	23.93%	16.97%	3.22%
SCARBOROUGH HIGH SCHOOL	Other	0	Various Vendors	\$1,763,165.53	\$1,699,163.18	\$782,619.39	\$447,355.77	\$0.00	\$0.00	\$0.00	\$0.00	\$1,229,975.16	72.39%		
Total			\$12,205,431.45	\$12,140,281.53											
SHARPSTOWN INTERNATIONAL SCHOOL	Architect	95794	Autoarch Architects	\$254,758.61	\$227,070.61	\$0.00	\$254,758.61	\$0.00	\$0.00	\$0.00	\$0.00	\$254,758.61	100.00%		100.00%
SHARPSTOWN INTERNATIONAL SCHOOL	CSP	52387	Dt Construction	\$3,895,621.79	\$3,895,621.79	\$0.00	\$0.00	\$0.00	\$0.00	\$551,929.02	\$305,907.88	\$857,836.90	22.02%	10.27%	9.73%
SHARPSTOWN INTERNATIONAL SCHOOL	Other	0	Various Vendors	\$616,464.21	\$501,032.76	\$147,642.00	\$98,988.63	\$0.00	\$0.00	\$0.00	\$0.00	\$246,630.63	49.22%		
Total			\$4,766,844.61	\$4,623,725.16											
WESTBURY HIGH SCHOOL	Architect	43260	Joiner Partnership, Inc.	\$1,910,565.36	\$1,478,973.36	\$0.00	\$0.00	\$0.00	\$0.00	\$530,563.25	\$0.00	\$530,563.25	35.87%	55.00%	
WESTBURY HIGH SCHOOL	CMAR	49451	Satterfield & Pontikes Construction Co.	\$47,810,157.33	\$40,481,693.97	\$0.00	\$0.00	\$0.00	\$0.00	\$3,958,325.69	\$235,548.40	\$4,193,874.09	10.36%	20.00%	
WESTBURY HIGH SCHOOL	Other	0	Various Vendors	\$3,857,832.11	\$3,676,182.65	\$1,034,263.71	\$1,048,226.07	\$0.00	\$0.00	\$0.00	\$0.00	\$2,082,489.78	56.65%		
Total			\$53,578,554.80	\$45,636,849.98											
WHARTON K-8 DUAL LANGUAGE ACADEMY	Architect	94041	Munoz & Company	\$1,142,587.00	\$1,106,244.09	\$1,142,587.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$1,142,587.00	100.00%	100.00%	
WHARTON K-8 DUAL LANGUAGE ACADEMY	CMAR	69826	DivisionOne Construction	\$26,802,461.21	\$26,331,676.92	\$0.00	\$0.00	\$0.00	\$0.00	\$2,776,384.65	\$3,306,890.44	\$6,083,275.09	23.10%	20.00%	5.00%
WHARTON K-8 DUAL LANGUAGE ACADEMY	Other	0	Various Vendors	\$7,559,029.31	\$6,260,772.24	\$1,567,247.19	\$1,438,079.96	\$0.00	\$0.00	\$0.00	\$0.00	\$3,005,327.15	48.00%		
Total			\$35,504,077.52	\$33,698,693.25											



School Name	Vendor / Project Type	VID	Vendor Name	Contracted Amount	Payments to Date	"First Tier MBE Spend"	"First Tier WBE Spend"	Additional MBE Spend	Additional WBE Spend	Second Tier MBE Spend	Second Tier WBE Spend	Actual M/WBE Spend Amount	Actual M/ WBE Spend Percentage	MBE Total Committed	WBE Total Committed
WILSON MONTESSORI	Architect	84380	Smith & Company Architects, Inc.	\$913,556.30	\$750,535.95	\$913,556.30	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$913,556.30	100.00%	100.00%	
WILSON MONTESSORI	CMAR	50632	Drymalla Construction Company Inc.	\$17,837,939.42	\$17,837,939.42	\$0.00	\$0.00	\$0.00	\$0.00	\$2,032,034.49	\$1,599,148.05	\$3,631,182.54	20.36%	11.90%	8.24%
WILSON MONTESSORI	Other	0	Various Vendors	\$3,304,319.98	\$2,897,284.83	\$1,310,633.57	\$228,391.24	\$0.00	\$0.00	\$0.00	\$0.00	\$1,539,024.81	53.12%		
Total				\$22,055,815.70	\$21,485,760.20										
BARNETT FIELD HOUSE	Architect	43325	PBK Architects	\$217,349.21	\$217,349.21	\$0.00	\$0.00	\$0.00	\$0.00	\$60,398.99	\$1,666.00	\$62,064.99	28.56%	25.00%	
BARNETT FIELD HOUSE	CSP	22036	Prime Contractors	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$1,952,484.45	\$0.00	\$1,952,484.45	0.00%	22.72%	
BARNETT FIELD HOUSE	Other	0	Various Vendors	-\$20,855.95	-\$20,855.95	\$20,654.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$20,654.00	-99.03%		
BUTLER FIELD HOUSE	Architect	43325	PBK Architects	\$192,615.09	\$192,615.09	\$0.00	\$0.00	\$0.00	\$0.00	\$63,700.59	\$13,209.71	\$76,910.30	39.93%	25.00%	
BUTLER FIELD HOUSE	CSP	22036	Prime Contractors	\$858,703.44	\$858,703.44	\$0.00	\$0.00	\$0.00	\$0.00	\$670,597.84	\$98,384.76	\$768,982.60	89.55%	24.68%	
BUTLER FIELD HOUSE	Other	0	Various Vendors	\$201,539.35	\$201,539.35	\$31,706.38	\$14,184.31	\$0.00	\$0.00	\$0.00	\$0.00	\$45,890.69	22.77%		
DELMAR FIELD HOUSE	Architect	43325	PBK Architects	\$2,041,976.09	\$2,041,976.09	\$0.00	\$0.00	\$0.00	\$0.00	\$356,124.40	\$188,723.62	\$544,848.02	26.68%	25.00%	
DELMAR FIELD HOUSE	CMAR	69826	DivisionOne Construction	\$37,109,128.78	\$37,023,737.32	\$0.00	\$0.00	\$0.00	\$0.00	\$10,000,962.07	\$0.00	\$10,000,962.07	27.01%	19.10%	10.90%
DELMAR FIELD HOUSE	Other	0	Various Vendors	\$1,343,905.53	\$1,082,505.53	\$1,619,616.78	\$121,214.41	\$0.00	\$0.00	\$0.00	\$0.00	\$1,740,831.19	160.81%		
Total				\$41,944,361.54	\$41,597,570.08										
MIDDLE SCHOOL RESTROOMS	Architect	94816	Robert Adams, Inc.	\$523,818.00	\$523,818.00	\$523,818.00	\$0.00	\$0.00	\$1,525.00	\$0.00	\$1,525.00	\$525,343.00	100.29%	100.00%	
MIDDLE SCHOOL RESTROOMS	Architect	51528	Courtney Harper + Partners, Inc.	\$635,661.59	\$635,593.04	\$0.00	\$635,661.59	\$0.00	\$0.00	\$0.00	\$0.00	\$635,661.59	100.00%		100.00%
MIDDLE SCHOOL RESTROOMS	Architect	42900	English & Associates	\$316,703.23	\$303,620.36	\$0.00	\$316,703.23	\$0.00	\$0.00	\$0.00	\$0.00	\$316,703.23	100.00%		100.00%
MIDDLE SCHOOL RESTROOMS	Architect	94762	VCS	\$544,758.53	\$544,757.73	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$137,421.45	\$137,421.45	25.23%	25.00%	
MIDDLE SCHOOL RESTROOMS	CSP	52387	Dt Construction	\$3,273,418.41	\$3,273,418.41	\$0.00	\$0.00	\$0.00	\$0.00	\$801,495.13	\$0.00	\$801,495.13	24.48%	10.27%	9.73%
MIDDLE SCHOOL RESTROOMS	CSP	22036	Prime Contractors	\$14,426,812.45	\$14,356,417.77	\$0.00	\$0.00	\$0.00	\$0.00	\$3,736,813.04	\$151,890.00	\$3,888,703.04	27.09%	20.00%	9.73%
MIDDLE SCHOOL RESTROOMS	Other	0	Various Vendors	\$6,405,959.19	\$6,334,330.17	\$2,619,627.08	\$40,921.50	\$0.00	\$0.00	\$0.00	\$0.00	\$2,660,548.58	42.00%		
Total				\$26,127,131.40	\$25,971,955.48										
TECHNOLOGY	Other	0	Various Vendors	\$52,976,418.04	\$51,851,669.69	\$45,518,935.21	\$695,627.36	\$0.00	\$0.00	\$0.00	\$0.00	\$48,214,562.57	89.13%		
SAFETY & SECURITY	Other	0	Various Vendors	\$17,548,782.87	\$17,732,984.65	\$7,617,342.39	\$2,731,833.68	\$0.00	\$0.00	\$0.00	\$0.00	\$10,349,176.07	58.36%		
LAND	Other	0	Various Vendors	\$46,904,000.70	\$46,897,159.51	\$1,401,738.32	\$157,218.61	\$0.00	\$0.00	\$0.00	\$0.00	\$1,558,956.93	3.32%		
Total				\$117,429,201.61	\$116,481,813.85										
HEERY INTERNATIONAL, INC.	PMF	9128	Heery International, Inc.	\$23,306,479.90	\$20,375,860.01	\$0.00	\$0.00	\$0.00	\$0.00	\$4,036,320.37	\$1,785,124.00	\$5,821,444.37	28.57%	20.81%	11.19%
Total				\$23,306,479.90	\$20,375,860.01										
JACOBS PROJECT MANAGMENT CO.	PMF	91651	Jacobs Project Management Co.	\$1,398,731.48	\$1,398,731.48	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%		
Total				\$1,398,731.48	\$1,398,731.48										
KWAME BUILDING GROUP, INC.	PMF	93038	Kwame Building Group, Inc.	\$3,352,621.93	\$3,352,621.93	\$3,352,621.93	\$0.00	\$64,911.23	\$109,133.25	\$64,911.23	\$109,133.25	\$3,526,666.41	105.19%	100.00%	
Total				\$3,352,621.93	\$3,352,621.93				\$0.00	\$0.00					
RICE & GARDNER CONSULTANTS	PMF	72745	Rice & Gardner Consultants	\$12,674,785.00	\$11,830,621.49	\$0.00	\$0.00	\$0.00	\$0.00	\$834,837.25	\$2,989,174.30	\$3,824,011.55	32.32%	50.00%	
Total				\$12,674,785.00	\$11,830,621.49										
URS CORPORATION	PMF	93886	Urs Corporation	\$5,389,941.00	\$5,389,941.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%	37.00%	
Total				\$5,389,941.00	\$5,389,941.00										
Other Program Management Fees & Costs	Other	0	Various Vendors	\$41,324,605.91	\$41,498,575.58	\$5,229,176.26	\$46,359.13	\$0.00	\$0.00	\$0.00	\$0.00	\$5,275,535.39	12.71%		
Total				\$41,324,605.91	\$41,498,575.58										

School Name	Vendor / Project Type	VID	Vendor Name	Contracted Amount	Payments to Date	"First Tier MBE Spend"	"First Tier WBE Spend"	Additional MBE Spend	Additional WBE Spend	Second Tier MBE Spend	Second Tier WBE Spend	Actual M/WBE Spend Amount	Actual M/ WBE Spend Percentage	MBE Total Committed	WBE Total Committed
			Design & Construction Total	\$1,496,371,167.08	\$1,347,536,548.28	\$19,632,470.27	\$7,263,159.28	\$986,228.38	\$961,654.30	\$152,131,755.02	\$77,718,363.90	\$256,745,748.47	19.05%		
			Technology, Safety & Security and Land Total	\$117,429,201.61	\$116,481,813.85	\$54,538,015.92	\$3,584,679.65	\$0.00	\$0.00	\$0.00	\$0.00	\$58,122,695.57	49.90%		
			Other Project Cost Total (Various Vendors)	\$139,142,489.37	\$113,987,264.22	\$66,853,852.89	\$14,328,625.47	\$0.00	\$0.00	\$56,866.25	\$9,133.00	\$81,248,477.61	71.28%		
			Other Project Cost Total (Various Vendors, Tech., Land and S&S)	\$256,571,690.98	\$230,469,078.07	\$121,391,868.81	\$17,913,305.12	\$0.00	\$0.00	\$56,866.25	\$9,133.00	\$139,371,173.18	60.47%		
			Other Program Management Fees & Costs	\$41,324,605.91	\$41,498,575.58	\$5,229,176.26	\$46,359.13	\$0.00	\$0.00	\$0.00	\$0.00	\$5,275,535.39	12.71%		
			Program Management Firms	\$46,122,559.31	\$42,347,775.91	\$3,352,621.93	\$0.00	\$64,911.23	\$109,133.25	\$4,936,068.85	\$4,883,431.55	\$13,172,122.33	31.10%		
			Grand Total*	\$1,840,390,023.28	\$1,661,851,977.84	\$149,606,137.27	\$25,222,823.53	\$1,051,139.61	\$1,070,787.55	\$157,124,690.12	\$82,610,928.45	\$414,564,579.37	24.95%		

## CERTIFIED MINORITY/WOMEN OWNED BUSINESSES BREAKDOWN BY PROJECT TYPE

Calculations based on numbers reported as of March 31, 2019

### 2012 CMAR PROJECTS\*

Project	Awarded CMAR	M/WBE Commitment
Askew Elementary School	Drymalla Construction Company, Inc.	28.00%
Austin High School	Pepper-Lawson Construction, L. P.	22.00%
Barnett Fieldhouse (CSP)	Prime Contractors Inc.	22.72%
Bellaire High School	Turner Construction Company	20.00%
Butler Fieldhouse (CSP)	Prime Contractors Inc.	24.68%
Condit Elementary School	DivisionOne Construction, LLC	30.00%
DeBakey High School	Tellepsen Builders, L. P.	20.00%
Delmar Tusa Fieldhouse	DivisionOne Construction, LLC	30.00%
Eastwood Academy (CSP)	Patriot Contracting, LLC	20.13%
Furr High School (CSP)	Prime Contractors Inc.	23.67%
Garden Oaks Montessori	Balfour/3Ci a Joint Venture (B3CI)	30.00%
Golfcrest Elementary School (CSP)	Amerian Construction	10.00%
HS for Law Enforcement & Criminal Justice	Balfour/3Ci a Joint Venture (B3CI)	30.00%
HSPVA	McCarthy Building Companies	20.00%
Jordan High School (CSP)	Cadence McShane Construction, LLC	23.50%
Kashmere High School	DT Construction, LP	20.00%
Lamar High School	Gilbane Building Company	30.00%
Lawson (Formerly Dowling) Middle School	Turner Construction Company	20.00%
Madison High School (CSP)	Satterfield & Pontikes Const., Inc.	20.00%
Mandarin Chinese Language Immersion	Satterfield & Pontikes Const., Inc.	20.00%
Mark White Elementary School	DivisionOne Construction, LLC	30.00%
Mickey Leland College Preparatory Academy (CSP)	Prime Contractors Inc.	20.76%
Milby High School	Tellepsen Builders, L. P.	20.00%

Project	Awarded CMAR	M/WBE Commitment
North Houston Early College High School	Drymalla Construction Company, Inc.	20.00%
Northside (Formerly Davis) High School	Satterfield & Pontikes Const., Inc.	20.00%
Parker Elementary School (CSP)	Patriot Contracting, LLC	20.04%
Pilgrim Academy	DT Construction, LP	20.00%
Sam Houston Math, Science, and Technology Center	Satterfield & Pontikes Const., Inc.	20.00%
Scarborough High School (CSP)	DT Construction, LP	20.19%
Sharpstown High School (CSP)	ICI Construction	23.50%
Sharpstown International School (CSP)	DT Construction, LP	20.00%
South Early College High School	Drymalla Construction Company, Inc.	12.97%
Sterling High School	Cadence McShane Const., LLC	21.00%
Tanglewood (Formerly Grady) Middle School	DivisionOne Construction, LLC	30.00%
Waltrip High School	Satterfield & Pontikes Const., Inc.	20.00%
Washington High School (CSP)	Prime Contractors Inc.	20.38%
Westbury High School	Satterfield & Pontikes Const., Inc.	20.00%
Wharton Dual Language School	DivisionOne Construction, LLC	25.00%
Wilson Montessori School	Drymalla Construction Company, Inc.	20.14%
Wisdom (Formerly Lee) High School	Satterfield & Pontikes Const., Inc.	20.00%
Worthing High School (CSP)	Prime Contractors Inc.	20.40%
Yates High School	Turner Construction Company	20.00%
Young Women's College Preparatory Academy	Satterfield & Pontikes Const., Inc.	20.00%

\*M/WBE Percentage reflects contractor's commitment.



# BOND FINANCIAL REPORT



**Sherrie Robinson**  
*Controller*


Office of the Controller, 3 Northeast  
4400 W. 18th St.  
Houston, Texas 77092

## 2012 BOND FINANCIAL REPORT

The total budget for the 2012 Bond Program is \$1.89 billion. Additionally, the Board approved \$212.4 million in October 2015 for a total of \$2.102 billion. Of that amount, \$1,840,390,023 is committed including encumbrances of \$179,484,447 and actual expenditures of \$1,660,905,576. A total of \$262,059,940 is available to complete projects.


### TOTAL BUDGET, COMMITMENTS & AVAILABLE FUNDING TO DATE

TOTAL BUDGET \$2.1 BILLION

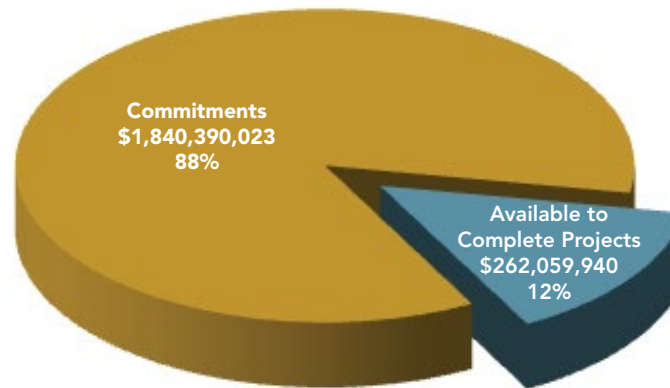

### TOTAL BOND REFERENDUM \$1.89 BILLION

(ISSUANCE SALES IN MILLIONS)

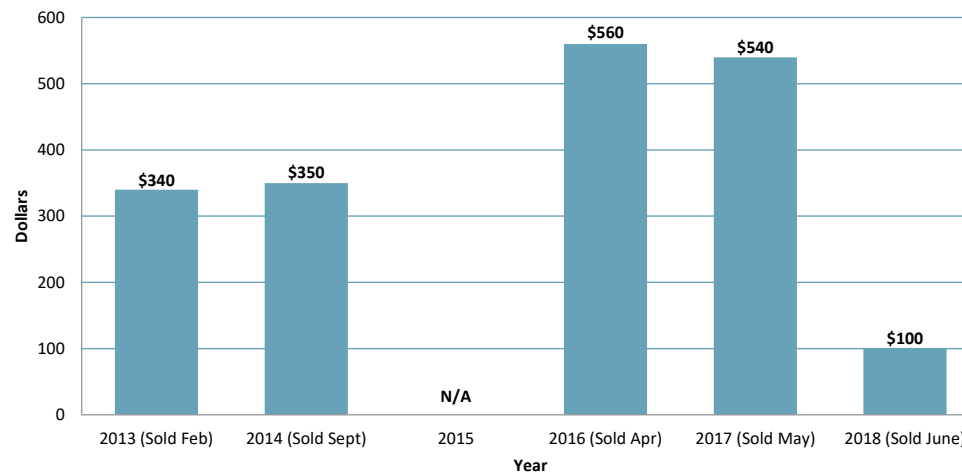

# PROJECT BUDGET/COMMITMENT/ AVAILABLE FUNDS REPORT







## REPORT DESCRIPTIONS

### PROJECT BUDGET/COMMITMENT/AVAILABLE FUNDS REPORT

#### COLUMN 1

##### **Org (Organization)**

Represents the Texas Education Agency (TEA) number assigned to the school or non-school facility.

#### COLUMN 2

##### **Campus**

The school name or non-school facility name – also referred to as “Project.”

#### COLUMN 3

##### **Total Budget**

The original budget totaling \$1.89 billion approved by the voters in December 2012.

#### COLUMN 4

##### **Adjustments**

This column includes supplemental funds and realignment funds, as well as any other adjustments made to the original budget.

#### COLUMN 5

##### **Total Adjusted Plan**

Column 3 plus Column 4.

#### COLUMN 6

##### **Program Reserve, Inflation, Management, & Swing Space**

Includes Program Reserves, Program Management Fees, Program Inflation, and Program Swing Space.

#### COLUMN 7

##### **Construction Budget**

Column 5 – Column 6.

#### COLUMN 8

##### **Pre-Encumbrance**

Requisitions (request to buy) that have been entered into the accounting system and are pending approval/ authorization to convert to a purchase order

#### COLUMN 9

##### **Encumbrance**

Purchase order – also referred to as “commitment.”

#### COLUMN 10

##### **Actual**

Represents total expenditures paid.

#### COLUMN 11

##### **Available to Complete Projects**

Uncommitted funds (the difference between the budget less pre-encumbrance less encumbrance less actual).

## 2012 Bond Program - Project Budget/Commitment/Available Funds Report

As of March 31, 2019

Org	Campus	Total Budget	Adjustments	Total Adjusted Budget	Program Reserve, Inflation, Mgt, & Swing Space	Construction Budget	Pre-Encumb	Encumbrance	Actual	Available to Complete Projects
		\$	\$	\$	(\$)	\$	(\$)	(\$)	(\$)	\$
001	Austin H.S.	68,429,000.00	12,511,679.00	80,940,679.00	3,191,964.00	77,748,715.00		46,134,174.08	26,014,887.35	5,599,653.57
002	Bellaire H.S.	106,724,000.00	34,790,428.00	141,514,428.00	6,726,701.00	134,787,727.00		23,655,792.56	14,044,190.17	97,087,744.27
003	Northside H.S.	46,764,000.00	19,633,657.00	66,397,657.00	4,677,515.00	61,720,142.00	3,889.18	12,140,350.72	45,151,070.63	4,424,831.47
004	Furr H.S.	55,100,000.00	499,287.00	55,599,287.00	2,416,369.00	53,182,918.00	24,549.00	957,676.88	49,884,160.82	2,316,531.30
006	Jones H.S.	1,125,000.00	296,011.00	1,421,011.00	56,551.00	1,364,460.00			531,498.00	832,962.00
007	Kashmere H.S.	17,000,000.00	2,053,729.00	19,053,729.00	813,417.00	18,240,312.00		101,021.37	16,851,368.53	1,287,922.10
008	Lamar H.S.	107,974,000.00	14,927,465.00	122,901,465.00	7,109,726.00	115,791,739.00		40,075,232.33	70,246,890.25	5,469,616.42
009	Wisdom H.S.	73,801,000.00	3,785,865.00	77,586,865.00	4,040,707.00	73,546,158.00		797,899.39	70,752,176.92	1,996,081.69
010	Madison H.S.	82,736,000.00	4,037,444.00	86,773,444.00	3,821,223.00	82,952,221.00	43,001.77	7,788,063.71	67,834,606.14	7,286,549.38
011	Milby H.S.	68,810,000.00	13,114,723.00	81,924,723.00	3,797,736.00	78,126,987.00	6,700.09	2,801,998.30	73,510,355.87	1,807,932.74
014	Sterling H.S.	72,304,000.00	-8,618,325.00	63,685,675.00	3,295,893.00	60,389,782.00	13,546.35	25,918.67	57,556,004.81	2,794,312.17
015	Waltrip H.S.	30,115,000.00	5,123,961.00	35,238,961.00	2,022,545.00	33,216,416.00	1,927.00	537,152.32	29,205,711.73	3,471,624.95
016	Washington H.S.	51,732,000.00	10,847,934.00	62,579,934.00	2,434,397.00	60,145,537.00	40,075.85	3,152,720.39	54,908,783.92	2,043,956.84
017	Westbury H.S.	40,006,000.00	20,257,598.00	60,263,598.00	2,342,551.00	57,921,047.00		7,947,404.82	45,631,149.98	4,342,492.20
019	Worthing H.S.	30,180,000.00	2,897,460.00	33,077,460.00	1,308,688.71	31,768,771.29		412,444.75	30,079,834.05	1,276,492.49
020	Yates H.S.	59,481,000.00	16,124,271.00	75,605,271.00	2,536,557.65	73,068,713.35		7,020,329.10	61,012,044.55	5,036,339.70
023	Sharpstown H.S.	54,944,000.00	5,646,534.00	60,590,534.00	3,176,581.00	57,413,953.00		844,393.16	55,102,179.25	1,467,380.59
024	Scarborough H.S.	12,566,000.00	2,077,625.00	14,643,625.00	281,461.00	14,362,164.00		65,149.92	12,140,281.53	2,156,732.55
025	HSVPA	80,178,000.00	6,587,477.00	86,765,477.00	3,220,456.00	83,545,021.00		430,296.76	82,766,572.46	348,151.78
026	DeBaKey H.S.	64,512,000.00	2,515,113.00	67,027,113.00	3,318,680.00	63,708,433.00	25,790.48	9,493.67	58,877,848.18	4,795,300.67
033	Jordan H.S.	36,693,000.00	331,913.00	37,024,913.00	1,945,515.00	35,079,398.00	3,058.30	4,578,077.97	25,357,324.32	5,140,937.41
068	Tanglewood M.S.	14,825,000.00	96,404.00	14,921,404.00	705,280.00	14,216,124.00			13,618,182.12	597,941.88
075	Lawson M.S.	59,125,000.00	4,081,598.00	63,206,598.00	2,875,782.00	60,330,816.00		1,476,818.96	55,284,148.18	3,569,848.86
081	Sharpstown International	6,125,000.00	808,379.00	6,933,379.00	405,096.00	6,528,283.00	75.00	143,044.45	4,623,725.16	1,761,438.39
157	Garden Oaks K-8	26,678,000.00	4,195,956.00	30,873,956.00	1,402,320.00	29,471,636.00		1,081,389.70	26,223,387.18	2,166,859.12
215	Parker E.S.	29,485,000.00	1,814,820.00	31,299,820.00	1,475,697.27	29,824,122.73	7,304.48	294,077.88	29,374,689.88	148,050.49
218	Pilgrim K-8	7,989,000.00	960,481.00	8,949,481.00	307,200.00	8,642,281.00		219,445.75	7,360,231.90	1,062,603.35
256	Wharton Dual Language	35,603,000.00	2,482,075.00	38,085,075.00	1,794,006.00	36,291,069.00	15,518.95	1,789,865.32	33,698,693.25	786,991.48
259	Wilson Montessori	18,914,000.00	5,808,033.00	24,722,033.00	1,185,125.00	23,536,908.00		570,055.50	21,485,760.20	1,481,092.30
274	Askew E.S.	26,632,000.00	1,254,972.00	27,886,972.00	1,275,267.00	26,611,705.00	59,082.79	565,639.18	24,852,149.31	1,134,833.72
301	Eastwood Academy	10,875,000.00	432,421.00	11,307,421.00		11,307,421.00	130,568.00	23,753.43	10,871,357.46	281,742.11
308	North Houston EC H.S.	13,500,000.00	-2,961,043.00	10,538,957.00	477,201.66	10,061,755.34	3,859.17		10,021,790.38	36,105.79
310	Sam Houston H.S.	101,428,000.00	5,291,029.00	106,719,029.00	4,851,931.00	101,867,098.00	716,978.66	7,156,048.81	86,824,500.62	7,169,569.91
458	Mickey Leland C.P.A.	28,675,000.00	835,976.00	29,510,976.00	1,391,053.00	28,119,923.00		64,340.50	27,849,417.07	206,165.43
460	Mandarin Chinese K-8	32,161,000.00	2,087,906.00	34,248,906.00	1,531,119.00	32,717,787.00	3,622.50		32,088,555.10	625,609.40

\*This report solely reflects 2012 Bond funds

## 2012 Bond Program - Project Budget/Commitment/Available Funds Report

As of March 31, 2019

Org	Campus	Total Budget	Adjustments	Total Adjusted Budget	Program Reserve, Inflation, Mgt, & Swing Space	Construction Budget	Pre-Encumb	Encumbrance	Actual	Available to Complete Projects
		\$	\$	\$	(\$)	\$	(\$)	(\$)	(\$)	\$
463	Young Women's	27,159,000.00	4,009,189.00	31,168,189.00	863,429.00	30,304,760.00	50,000.00	178,713.06	29,246,312.35	829,734.59
483	M. White E.S.	23,417,000.00		23,417,000.00	442,600.00	22,974,400.00		9,129.15	22,669,736.88	295,533.97
486	S. Early College H.S.	13,500,000.00	-2,793,911.00	10,706,089.00	441,479.94	10,264,609.06		31,557.50	9,661,569.38	571,482.18
660	School Athletics	44,675,000.00	1,100,544.00	45,775,544.00	2,094,016.00	43,681,528.00		346,791.46	41,597,570.08	1,737,166.46
1994	Construction Contingency		11,983,987.82	11,983,987.82		11,983,987.82				11,983,987.82
	<b>TOTAL CAMPUSES</b>	<b>1,681,940,000.00</b>	<b>210,930,665.82</b>	<b>1,892,870,665.82</b>	<b>86,053,837.23</b>	<b>1,806,816,828.59</b>	<b>1,149,547.57</b>	<b>173,426,261.52</b>	<b>1,434,810,715.96</b>	<b>197,430,303.54</b>
1998	Middle School Restrooms	35,000,000.00	-8,301,566.82	26,698,433.18		26,698,433.18		155,175.92	25,971,955.48	571,301.78
1997	District-wide Technology	100,000,000.00	0.00	100,000,000.00		100,000,000.00	129,113.00	977,446.65	51,869,858.39	47,023,581.96
1996	District-wide Safety & Security	17,293,000.00	12,058,745.00	29,351,745.00		29,351,745.00	21,058.69		17,527,724.18	11,802,962.13
1995	Land	55,767,000.00	-8,425,744.00	47,341,256.00		47,341,256.00		6,841.19	46,897,159.51	437,255.30
1999	Program & Management Cost		6,187,863.00	6,187,863.00	86,053,837.23	92,241,700.23		3,619,002.43	83,828,162.79	4,794,535.01
	<b>GRAND TOTAL</b>	<b>1,890,000,000.00</b>	<b>212,449,963.00</b>	<b>2,102,449,963.00</b>		<b>2,102,449,963.00</b>	<b>1,299,719.26</b>	<b>178,184,727.71</b>	<b>1,660,905,576.31</b>	<b>262,059,939.72</b>

\*This report solely reflects 2012 Bond funds



# STRATEGIC ENGAGEMENT AND OUTREACH REPORT



Northside High School

**Holly Huffman**  
*Officer, Business Operations  
Strategic Engagement & Outreach*  
3200 Center St., 136A  
Houston, Texas 77007  
[BondInfo@HoustonISD.org](mailto:BondInfo@HoustonISD.org)

A vertical teal-colored bar on the left side of the page, featuring a geometric pattern of overlapping rectangular and triangular shapes, creating a sense of depth and architectural structure.

## EXECUTIVE SUMMARY

With six campuses opening in January, the Strategic Engagement and Outreach team mobilized to highlight students' first day at their new campuses.

On Jan. 7, the team was dispatched throughout the district to provide extensive, on-site communications coverage for each of the six schools that opened for the first day of the spring semester — Kinder High School for the Performing and Visual Arts, Barbara Jordan Career Center, Wharton Dual Language Academy, Sam Houston Math, Science and Technology Center, and Madison and Worthing high schools.

Team members wrote stories that appeared on the district and bond program websites, took photos, and posted updates on social media.

The team also led the planning, promotion, and execution of the building dedication ceremonies for Askew and Parker elementary schools, and Wilson Montessori, the grand opening celebrations for Worthing High School, and Kinder High School for the Performing and Visual Arts. The team also coordinated the groundbreaking ceremony at Bellaire High School — the final groundbreaking ceremony of the 2012 Bond Program. Milestone event scheduling and planning is ongoing for Wharton Dual Language Academy, Barbara Jordan Career Center, Sam Houston Math, Science and Technology Center, and Madison High School.

Team members continue to attend Project Advisory Team meetings and internal strategy meetings, as needed, to assess communications needs and provide guidance to district leadership and project managers on strategies to engage more effectively with stakeholders.

The team also continued to cultivate the following of the @Build\_HISD Twitter account, posting more than 160 tweets, earning more than 303,500 impressions and 842 profile visits, and gaining 53 new followers during the first quarter, bringing the total followership up to 829.

Team members also wrote 17 project updates, which were published on the HISD News Blog, the 2012 Bond website, and respective school project pages. The posts also were circulated to wider audiences via social media.

Additionally, the team published three *Building Excellence* newsletters, which were sent to more than 4,200 subscribers in January, February, and March.

## FIRST QUARTER STRATEGIC ENGAGEMENT AND OUTREACH BY THE NUMBERS



### SOCIAL MEDIA & WEB STORIES

**166** tweets @Build\_HISD

**829** followers

**303,500** impressions

**17** blog posts



### MEDIA ENGAGEMENT

**4** media mentions

**6** videos

**5** press releases/media advisories



### COMMUNITY OUTREACH

**1** Project Advisory  
Team meeting

**3** Building Dedication  
ceremonies

**2** Grand Opening  
celebrations

**1** Groundbreaking  
ceremony

## COMMUNICATIONS AND SCHOOL OUTREACH

### COMMUNITY ENGAGEMENT

- Continued to focus on updating the bond website, writing project updates, and promoting and engaging with 829 followers on the @Build\_HISD twitter account
- Continued monthly production of the eNewsletter, *Building Excellence*, which is distributed to more than 4,200 subscribers
- Continued to monitor and respond to requests for information and questions submitted to Bondinfo@HoustonISD.org
- Attended the Austin Project Advisory Team meeting to assist with communication, provide coverage and review presentation for accuracy

### EVENTS

- Coordinated and covered six milestone celebrations during the first quarter, including building dedication ceremonies for Askew (Jan. 31) and Parker (Feb. 28) elementary schools, and Wilson Montessori (March 1), and grand opening events for Worthing High School (Jan. 25), and Kinder High School for the Performing and Visual Arts (Feb. 4), as well as the final groundbreaking ceremony of the 2012 Bond Program at Bellaire High School (March 26)





Austin High School

# GLOSSARY







# GLOSSARY

## GLOSSARY OF TERMS

### **BAS**

Building Automation System (HVAC and lighting controls)

### **Change order**

A modification to the original construction contract authorizing a change in the work or an adjustment in the amount of the contract or the contract time. The original contract price may not be increased by more than 25 percent by change order.

### **Competitive Bidding**

A procurement method by which a governmental entity contracts with a contractor for the construction, alteration, rehabilitation, or repair of a facility by awarding the contract to the lowest responsible bidder.

### **Competitive Sealed Proposal (CSP)**

A procurement method by which a governmental entity may request proposals and pricing information based on the scope of work provided, rank the offers, negotiate a contract, and then award the project to the contractor that offers the best value to the entity.

### **Construction commissioning**

A collaborative process whose purpose is to ensure that buildings and systems perform according to contract.

### **Commissioning agent**

An independent party, unaffiliated with the design team or contractors, that takes charge of the construction commissioning process.

### **Construction documents**

Extremely detailed drawings and specifications showing and describing all of the details required to construct the building.

### **Construction Manager at Risk (CMAR)**

A construction delivery method by which a governmental entity contracts with an architect or engineer for design and construction phase services and contracts separately with a construction manager-at-risk to serve as the general contractor and to provide consultation during the design and construction, rehabilitation, alteration, or repair of a facility. A CMAR is selected based upon qualifications and price proposal that would provide the best value for the governmental entity.

### **Daylighting**

A planned energy conservation strategy that utilizes illumination from sunlight.

### **Design development**

Process in which schematic design drawings are further developed to include more detail, including: detailed site plan; room layouts; door and window types; interior and exterior elevations; reflected ceiling plans; plumbing, mechanical, structural, and electrical drawings; and kitchen layouts.

### **Design team**

A group of professionals from architectural and engineering firms that is engaged to design a facility.

### **Educational Specifications**

A document that details the number of rooms required, the size of each room, how those rooms should relate to each other (adjacencies), and the elements (sinks, electrical outlets, markerboards, cabinets, etc.) that should be included in each room. Districtwide Educational Specifications will be adapted for the specific needs of the campus.

### **Encumbrance Accounting**

The recognition of commitments that will subsequently become expenditures when goods and services are received.

### **FF&E**

Furniture, fixtures, and equipment. This describes all contents that are not a permanent part of the structure.



**Hard costs**

Expenses associated with direct construction of a project.

**HVAC**

Heating, ventilation, and air-conditioning

**Job Order Contract (JOC)**

A procurement method used for maintenance, repair, alteration, renovation, remediation, or minor construction of a facility when the work is of a recurring nature, but the delivery times, type, and quantities of work required are indefinite.

**Leadership in Energy and Environmental Design (LEED)**

A building certification process developed by the U.S. Green Building Council (USGBC) to enhance environmental awareness among architects and building contractors and to encourage the design and construction of energy-efficient, water-conserving buildings that use sustainable or green resources and materials.

**MEP**

Mechanical/electrical and plumbing systems.

**Program or Concept design**

Single-line drawings that illustrate room adjacencies and scale

**Public Facility Corporation**

The PFC is a non-profit corporation, the creation of which was sponsored by the District pursuant to the Public Facility Corporation Act. The Public Facility Corporation act authorizes the creation and utilization of school district public facility corporations to issue bonds for capital renovation programs. The Houston Independent School District Public Facility Corporation (HISD-PFC) has utilized this structure to issue \$48M for four of the new schools in the 2007 Facilities Capital Program (FCP).

**Schedule of values**

An itemization of costs that comprises the entire contract amount.

**Schematic Design**

The schematic design submission typically includes a simple site plan, floor plans (simple scale drawings that show room sizes, relationships, doors, and windows), simple building cross sections, an outline specification with general information about building systems, a table comparing required square footages from the educational specifications with actual square footages shown on the drawings, a preliminary estimate of cost options, and possibly 3-dimensional depictions of the exterior of the building.

**Scope-to-Budget**

An analytical review conducted by the architectural/engineering team to ensure the proposed scope of work and project requirements are aligned with the established construction budget. The approved findings from this review become the basis for the design and preparation of the construction documents.

**Soft costs**

A construction industry term, but more specifically a contractor accounting term for an expense item that is not considered direct construction cost. Soft costs include architectural, engineering, financing, legal fees, and other pre- and post-construction expenses.

**Swing space**

A school building or a portion of an existing school building or other facility that will house the student population and its teachers and staff during the school-construction process.






Lamar High School



# APPENDIX







## **Bond Oversight Committee Meeting Status Report February 12, 2019**

Bond Oversight Committee Tours Kinder HSPVA, hears bond program update.

HISD's Bond Oversight Committee toured the newly opened Kinder High School for the Performing and Visual Arts on Tuesday at their quarterly meeting to review progress of the 2012 Bond Program.

HSPVA Principal Scott Allen and HISD General Manager of Facilities Design Dan Bankhead led the eight-member committee as they walked through the school's grand entry hall, the 800-seat Denny Theater, the black box theater and the recital hall.

The tour also included a student exhibit in the visual arts wing and visits to the ceramic and sculpture studios, a recording studio, a creative writing lab, two-story high dance studios, the band and orchestra hall, and the choral music room.

After the tour, the committee was briefed on fourth quarter 2018 progress by General Manager of Construction Services Andreas Peebles.

Those schools, which opened in January, include Kinder HSPVA, Barbara Jordan Career Center, Wharton Dual Language Academy, Sam Houston Math Science and Technology Center, and Worthing and Madison high schools.

Peebles noted that with the latest round of openings, school construction is now 85 percent complete, with only four 2012 Bond projects – Lamar, Bellaire, Northside, and Austin high schools – remaining under construction and yet to open.

Looking ahead, Chief Operating Officer Brian Busby reported that the team is currently researching what projects a new bond program would encompass.

Busby said the team is putting together a community engagement strategy and looking toward 2020 for putting forward a new bond referendum.

## MEETING NOTES

MEETING: **Bond Oversight Committee Meeting**  
Bond Oversight Committee Q4 2018 Meeting

LOCATION: Kinder High School for the Performing and Visual Arts  
790 Austin Street  
Houston, TX 77002

DATE: February 12, 2019

TIME: 8:30 A.M.


PRESENT: **Bond Oversight Committee (BOC)**

Mr. Michael G. Davis  
Mr. Craig R. Johnson Sr.  
Mr. Robert M. Eury  
Mr. Gusta Booker III  
Mr. David Quan  
Mr. Gary White  
Ms. Phoebe Tudor  
Mr. D.V. "Sonny" Flores

ABSENT:

**Houston Independent School District (HISD)**

Mr. Brian Busby, Chief Operating Officer  
Mr. Eugene Salazar, Business Operations  
Mr. Derrick Sanders, Construction Services  
Mr. Dan Bankhead, Construction Services  
Mr. Andreas Peeples, Construction Services  
Ms. Mary Rochon, Construction Services  
Ms. Precilla Rivera, Construction Services  
Ms. Veronica Bush, Construction Services  
Ms. Leesa Love, Real Estate  
Ms. Sherrie Robinson, Controller's Office  
Mr. John Gerwin, Construction Services  
Ms. Cheryl Smith, Business Solutions  
Ms. Mary Rochon, Construction Services  
Ms. Yesenia Taylor, Business Solutions  
Ms. Tonya Savoie, Business Solutions  
Mr. James Moore, Capital Project Accounting  
Mr. Scott Allen, Kinder HSPVA Principal  
Ms. Holly Huffman, Strategic Engagement & Outreach  
Ms. Christi Landry, Strategic Engagement & Outreach  
Mr. Alejandro Banegas, Strategic Engagement & Outreach  
Ms. Mariauna Hernandez, Strategic Engagement & Outreach  
Ms. Rebecca Kiest, Strategic Engagement & Outreach  
Ms. Antonia Jones, Strategic Engagement & Outreach  
Ms. Alecea Rush, Strategic Engagement and Outreach  
Ms. Karla Gutierrez Estrada, Strategic Engagement and Outreach  
Ms. Erica Parker, Strategic Engagement & Outreach  
Ms. Estefania Espinosa, Strategic Engagement & Outreach



The general purpose of the meeting was to brief the Bond Oversight Committee on third quarter progress of the new construction and renovation projects funded through the 2012 Facilities Capital Program. Related issues, questions, and activities were also discussed:

**Item 1      Welcome**

Bond Oversight Committee members and other guests met in the first-floor lobby of Kinder HSPVA in preparation for a tour of the school. Construction Services General Manager Andreas Peeples and Facilities Design General Manager Dan Bankhead welcomed the group at 8:45 a.m.

**Item 2      Kinder HSPVA Tour**

Kinder HSPVA Principal Scott Allen led the group on an abbreviated tour of the school, including the 800-seat main theater, multiple secondary theaters, music and dance studios, the creative writing department, the fitness center, flexible learning spaces, and traditional classrooms.

**Item 3      Minutes from October 23 Meeting**

Mr. Peeples began the business portion of the meeting at 9:45 a.m. by asking Bond Oversight Committee members to approve the minutes from the October 23, 2018, meeting. They were approved unanimously.

**Item 4      Video Presentation**

Mr. Peeples remarked on the district's impressive feat of opening 21 schools in 2018 and introduced a video presentation highlighting the six schools that were completed in the fourth quarter, in preparation for January 2019 openings. The presentation featured not only footage of the new facilities, but also student interviews detailing how their surroundings impact their learning experience.

**Item 5      Fourth Quarter Construction Update**

Mr. Peeples reported that Kinder HSPVA, Worthing High School, Barbara Jordan Career Center, Sam Houston Math, Science, and Technology Center, Madison High School, and Wharton Dual Language Academy started the spring semester of the 2018-2019 school year in new facilities, bringing school construction to 85 percent completion.

**Item 6      Looking Ahead**

Mr. Peeples reported that only four schools in the bond program remain under active construction: Bellaire High School, Northside High School, Lamar High School, and Austin High School. He reported that three of the recently opened schools have ongoing demolition and sitework: Barbara Jordan Career Center, Sam Houston Math, Science, and Technology Center, and Madison High School. Mr. Peeples also noted schools with major realignment projects include Wisdom High School, Milby High School, Waltrip High School, Booker T. Washington High School, Yates High School, Pilgrim Academy, and Westbury High School.



Bond Oversight Committee Member Phoebe Tudor asked for further explanation of the word “realignment.” Mr. Peeples explained these projects were not part of the original scope of work, but are funded by surplus bond funds.

Bond Oversight Committee Member David Quan asked whether BOC members would receive progress updates about these ongoing realignment projects. Mr. Peeples assured him those would be provided. Business Operations Chief Operating Officer Brian Busby asked Strategic Engagement and Outreach Interim Officer Holly Huffman to include supporting documents about the realignment Board item and specific project details in the committee workbook.

Bond Oversight Committee Member D.V. “Sonny” Flores inquired about recent flooding at Northside High School. Mr. Bankhead said this issue is addressed in the city’s capital plan. Improvements have been made to the drainage system in the area, but the city’s goal is to raise and regrade the street. Mr. Bankhead also mentioned the part of the building that typically floods is being demolished to make way for an elevated section, matching the rest of the school. Mr. Busby noted that, in the meantime, a pump was installed underneath the auditorium to avoid water retention.

Mr. Busby also briefly discussed the possibility of a future bond program, which could go before voters as early as May 2020 or November 2020. He stated that the district could potentially focus on the Westheimer and 288 South corridors, where new schools might be needed to accommodate student growth. Mr. Busby further explained that any future bond program would be guided by community input and noted that Ms. Huffman would lead an effort to engage community stakeholders in discussions about the 20-year capital plan and gather feedback about potential projects.

Mr. Quan asked how a potential state takeover would affect future bonds. Mr. Busby said the plan for another bond would be presented to either the existing board or any other future board, as well as continue conducting surveys to gauge public opinion. Mr. Busby remarked that no one is talking about the district’s record-breaking number of school openings that occurred this year. He said we must shift the narrative and rebrand our district, meaning the next bond election campaign will have to be different than what has been previously done. He said we must actively involve the community in deciding the scope of the bond, based on what voters would likely support.

Bond Oversight Committee member Craig R. Johnson Sr. said a new bond is needed to avoid having to tear down schools that have deteriorated beyond repair. He suggested offering virtual tours of the 2012 Bond schools, so the community can see first-hand the benefits of supporting a bond.

Ms. Tudor asked when the previously mentioned potential bond polling took place. Mr. Busby clarified the district used a firm approximately six months ago and conducted its own unofficial polling among both supporters and detractors. He also said they engaged the loudest voices at board meetings to better understand their concerns. Ms. Tudor said she thinks the 2012 Bond has gone extremely well but is worried that the public only hears about what’s going on with the board and how difficult it will be to counteract that narrative. Mr.

Busby agreed that now is not the right time for a bond election and stated Dr. Lathan shares this view.

Bond Oversight Committee Member Robert M. Eury asked whether there is a point when it will become cost-prohibitive to wait for the right time. Mr. Busby acknowledged the negative side of waiting is deferred maintenance on schools. However, the positive side of waiting until 2020 is increased property values, barring another hurricane or tropical storm. This increase will mean a larger bond with no tax increase. Mr. Busby reiterated that 2020, either May or November, is the ideal time.

**Item 7**

**Supplier Diversity (M/WBE) Report and Community Outreach**

Business Solutions General Manager Yesenia Taylor told the committee about three M/WBE workshops that were held during the third quarter — “Beyond the Post-It: Communications for Business Today,” “Driving the Narrative: The Importance of Storytelling,” and “Meet HISD’s Purchasing Services.” She highlighted the latter, sharing that Business Logistics Officer Alexis Licata gave a presentation, which was followed by a networking session in which Ms. Licata met one-on-one with potential suppliers and category specialists. She also discussed other outreach activities in which the team participated, including events with the City of Houston, Greater Houston Black Chamber, Greater Houston Business Procurement Forum, HISD Foundation, Houston Minority Supplier Development Council, and Women’s Business Enterprise Alliance. She noted that the M/WBE participation rate — slightly more than 28 percent — continues to exceed board-established goals.

**Item 8**

**Financial Reports**

Senior Manager of Accounting James Moore reported the total budget for the 2012 Bond program was \$2.1 billion, with total commitments through the fourth quarter of \$1,800,675,666, including \$187,522,126 in encumbrances and actual expenditures of \$1,613,153,540. Funds available to complete projects is \$301,774,297.

Mr. White asked whether there would be any funds left over once construction is complete, even after the realignment. Ms. Savoie explained that they do foresee funds remaining, but that it is too early to give an exact figure. Mr. Busby stressed that the financial clock was reset with the March 2017 board item. Ms. Savoie said the extra money will go into the safety and security budget. Mr. White said the district should inform the public of the amount saved. Ms. Savoie said the public tends to pull out their wish list when they learn there is unused money.

Mr. Johnson said the district should proactively train and prepare the emergency response in the case of a school shooting. Mr. Busby noted that HISD is the only school district in the country with an accredited police department. He also shared that when the Parkland, Florida shooting occurred, HISD’s Chief of Police Paul Cordova was called in to help the Parkland Police Department get to implement a system similar to HISD. Mr. Busby also pointed out that we have 36 patrol officers and a cybercrime unit.

Mr. Quan asked for further clarification of the safety and security fund. Ms. Savoie said the district has always had a safety and security fund, but the board item stipulates that any leftover funds from the 2012 Bond will be transferred to the safety and security fund. Mr. Quan asked if there are two separate accounts or just one, with two separate sources. Ms.

Savoie confirmed the sourcing is different. Mr. Quan asked if the committee could obtain information about the current balance of the safety and security fund. Mr. Moore said that can be arranged. Mr. Busby said they could share information about how much was allocated for this purpose in previous bonds — \$90.3 million for the 2007 bond and \$17.2 million for the 2012 bond. Mr. Busby also said Mr. Sanders, as the Superintendent's designee, is able to move funds within line items as needed.

Mr. Quan asked about the districtwide standard of card access to buildings, specifically whether students are issued cards. Mr. Busby said the goal is for the next bond to include universal cards that will provide entry to buildings and serve as transportation cards, lunch cards and student IDs. Mr. Busby said they increased the number of cameras from around 6,000 to over 16,000. He said when CCTV is added, server capability will also need to be addressed.

Mr. Quan asked how visitors can gain entry to schools with the current security system. Mr. Busby explained that visitors push the intercom at the entrance, ringing the front desk. The staff member inside asks, "How can I help you?" and visitors state their business. Then, the staff member buzzes visitors in. Mr. Busby stated most new campuses have a vestibule, or holding area, where visitors are forced to go to the front desk area and sign in.

#### **Item 9 Strategic Engagement and Outreach**


Ms. Huffman reported that the team focused on preparing for the six new schools that opened in January, including working with school administrators to provide transition communications, such as letters, callouts, maps. She said the team also created social media teaser videos in advance of opening day and provided full, on-site opening day coverage to promote the new campuses. Ms. Huffman explained that the team had held four grand openings and one groundbreaking ceremony in the fourth quarter, noting that the team has already held three more milestone events – grand openings for Worthing High School and Kinder HSPVA and a building dedication for Askew Elementary School — during the first quarter of 2019. Ms. Huffman said the team is currently planning about 12 more milestone events, including potential groundbreakings for the four Harvey schools and a groundbreaking for Bellaire, the last 2012 bond school to have such an event. Ms. Huffman also highlighted the team's shift to a new style of videos which physically showcase the new buildings while letting the narrative detail the academic impact. Ms. Huffman also stated the team worked to shift the style of the quarterly Bond Oversight Committee report from traditional binder to spiralbound report, making it less cumbersome and more cost-effective. She stated her ultimate goal is a digital version.

#### **Item 10 Executive Session**

Mr. Sanders thanked attendees participating in the meeting. BOC members then adjourned into Executive Session.

The information outlined above reflects the author's understanding of the key discussions and decisions reached during this meeting. Should there be any additions and/or clarifications to these meeting notes, please notify the author in writing promptly. These notes will be relied upon as the approved record of the





meeting, unless a written notice to the contrary is sent to the author within seven (7) days of the submission of these meeting notes.

Prepared by HISD Business Operations Strategic Engagement and Outreach.
