



BOND OVERSIGHT COMMITTEE WORKBOOK

Meeting April 24, 2018

Bond Oversight Committee Meeting
April 24, 2018 | 8:30 a.m.

Table of Contents

BOND PROGRAM OVERSIGHT COMMITTEE CHARTER	5
EXECUTIVE SUMMARY	13
PROJECT UPDATE REPORT	19
BOND PHASING SCHEDULE	23
PROJECT UPDATE REPORT — GROUP 1	25
PROJECT UPDATE REPORT — GROUP 2	63
PROJECT UPDATE REPORT — GROUP 3	81
PROJECT UPDATE REPORT — GROUP 4	91
DISTRICTWIDE PROJECTS	115
SUPPLIER DIVERSITY (M/WBE) BOND REPORT	121
BOND FINANCIAL REPORTS	133
PROJECT BUDGET/COMMITMENT/AVAILABLE FUNDS REPORT	137
BOND COMMUNICATIONS REPORT	141
GLOSSARY	175
APPENDIX	181



It is the policy of the Houston Independent School District not to discriminate on the basis of age, color, handicap or disability, ancestry, national origin, marital status, race, religion, sex, veteran status, political affiliation, sexual orientation, gender identity and/or gender expression in its educational or employment programs and activities.

Welcome

COMMITTEE MEMBERS

Gary J. White, Chairman

D.V. “Sonny” Flores, Vice Chairman

Gusta Booker III

Michael G. Davis

Robert M. Eury

Craig Johnson

David Quan

Phoebe Tudor



BOC Meeting

Bond Program Oversight Committee Charter

PURPOSE OF CHARTER

The Board of Education ("Board") for the District desires to make continual improvements to existing programs. As a result, the Bond Program Oversight Committee Charter ("Charter") is adopted to explain the mission, purpose, structure, membership, duties, responsibilities, and expectations. This Charter supersedes the previously adopted charter dated August 30, 2010.

COMMITTEE MISSION

The HISD Board, in response to community interest in the effective and efficient use of bond proceeds, has established a mechanism to encourage greater accountability, transparency, public support, and confidence by creating the Committee. The Committee is an independent citizens' Committee that is responsible to the Superintendent, Board, and general public (in that order).

The Committee's charge is to monitor all applicable Bond funded construction projects and help interested Houstonians to stay informed about new construction and renovation projects in the District. Its purpose is to monitor performance and compliance in order to confirm that HISD implements Bond Program work in conformance with the program approved by the Board and make recommendations to maximize available resources to achieve construction goals in the most effective and cost efficient manner. Its focus should be oversight rather than limited to hindsight.

COMMITTEE STRUCTURE AND MEMBERSHIP

- a) The Committee has up to nine voting members, including a Chairperson and Vice Chairperson, who are appointed by the Superintendent. Formal action from the Committee requires a majority vote of the quorum present. Individual members of the Committee shall not exercise authority for the Committee as a whole and shall not act independently of the Committee. Written applications will be reviewed by members of the District's Executive Leadership team for each applicant's experiences and qualifications. The Executive Leadership team will submit recommendations to the Superintendent for approval and appointment to the Committee.
- b) Appointments will be staggered for one year and two year terms. Terms may be extended for additional one or two year terms upon approval by the Superintendent.
- c) The Committee will approve meeting minutes, review and approve the reasonableness of reports from the District, and approve the issuance of status reports and other communications from the Committee.
- d) All meetings will be open to the general public.
- e) Membership on the Committee shall consist of interested persons from the following groups who can remain objective and independent with the District's best interest at heart:
 - 1. Special preference for members with expertise or knowledge in the areas of building design/engineering, construction, construction project management, and/or finance.
 - 2. Members active in a business organization representing the business community located in the District.
 - 3. Members who are parents or guardians of a child enrolled in the District and also active in a parent-teacher organization.
 - 4. Members of the community at-large.

- f) The Committee members receive no direct or indirect compensation from the District for their services as members of the Committee.
- g) The Committee members may not have an active contract or be seeking a contract with the District or with any contractor or sub-contractors associated with the Bond Programs.
- h) The Committee may not include any employee or official of the District, or any vendor, contractor or consultant of the District.
- i) A Committee member serves the general interest of the public as opposed to any personal interest or special interest group.
- j) If a Committee member moves outside of the District's geographic boundaries, resigns, violates the Ethics Policy contained herein, fails to attend two consecutive Committee meetings without reasonable excuse, or otherwise becomes unable to serve on the Committee, the Superintendent may declare the position on the Committee to be vacant and appoint another qualified person to the Committee.

COMMITTEE DUTIES AND RESPONSIBILITIES

The Committee shall inform the Superintendent, Board, and general public (in that order) concerning the District's overall project management of all Bond Programs, including but not limited to:

- a) Review periodic reports produced by the District to verify effective and efficient use of bond proceeds and compliance with the purposes set forth in the Bond Programs as approved by the Board. See reports issued by the District in the "District Duties and Responsibilities" section below.
- b) Ensure that bond revenues are expended for the purpose set forth in the Bond Programs as approved by the Board of Education, and that any deferred proposals or plans where considered necessary are appropriate.
- c) Validate that no bond funds are used for any teacher or administrative salaries or other school operating expense, other than administrative salaries whose primary purpose is to manage the District's Bond Programs.
- d) Review efforts by the District to maximize bond revenues by balancing best value, quality, and efficiency in meeting the District's goals and priorities.
- e) Evaluate risks and related controls associated with the District's Bond Programs, determine focus areas and strategic approach to review, and communicate any findings and recommendations for improvement via a periodic independent report to the Superintendent, Board, and general public. To maximize these efforts, the Committee may recommend the performance of specific audit projects based on its risk assessments and communications to the Board Audit Committee and HISD Office of Inspector General.
- f) Coordinate with the Superintendent's designee to visit District facilities and grounds for which bond proceeds have been or will be expended, in accordance with any necessary access procedures.
- g) Review copies of other bond reports published by the District.
- h) Review any performance audits of the District's Bond Programs to ensure the District is taking appropriate action to remediate any deficiencies identified in such reports.
- i) Review operational audits conducted by the HISD Office of Inspector General to ensure the adequacy of scope, management action plans, and remediation efforts of the District.
- j) Review any financial audits of the District's Bond Programs to ensure the District is taking appropriate action to remediate any deficiencies identified in such reports.
- k) Provide periodic status reports and an annual report regarding the results of its activities, in addition to any Committee findings, recommendations, and management action plans, to the Superintendent and Board. These reports should include the Committee's opinion regarding the District's remediation efforts for any recommendations included in the performance audits, operational audits, or financial audits mentioned above and will be made available to the general public by inclusion on the District's website and other communication avenues.
- l) Perform other reasonable duties requested by the Superintendent.
- m) Disclose and sign an annual conflict of interest statement for existing conflicts and re-submit if any conflicts arise during a Committee member's tenure.

- n) Any perceived allegation of wrongdoing; potential waste, fraud, misuse or abuse; or non-compliance with Local, State, Federal laws/regulations, or District policies that becomes known to the Committee shall be communicated to the Superintendent, who shall refer such matters to the Board, Ethics and Compliance Officer, Office of Inspector General, and outside legal counsel where appropriate.

The Committee provides counsel and input to the administration and the Board, but it does not have management or policy-setting responsibilities. Also, the Committee does not have a fiduciary responsibility to the District or Board, nor are its members personally liable to the District or Board. The Committee is not responsible for:

- a) Approval of construction contracts or change orders;
- b) Appropriation of construction funds;
- c) Handling of legal matters;
- d) Approval of construction plans and schedules;
- e) Approval of the District's maintenance plan;
- f) Approval of the sale of bonds;
- g) Establishment of priorities and order of construction for the bond projects;
- h) Selection of architects, engineers, construction managers, project managers, and such other professional service firms;
- i) Approval of the design for each project including exterior materials, paint color, interior finishes, site plan and construction means or methods;
- j) Selection of independent audit firm(s), performance audit consultants and such other consultants as are necessary to support the performance of the Bond Programs;
- k) Setting or approving schedules of design and construction activities;
- l) Investigations of alleged wrongdoing; potential waste, fraud, misuse or abuse; or non-compliance with Local, State, Federal laws/regulations, or District policies.
- m) Directing the activities of staff or consultants; or
- n) Activities, roles or responsibilities that have been delegated to staff or consultants by the Superintendent or his designee.

COMMITTEE MEETINGS

- a) The Committee shall meet at least quarterly to review the District's Bond Program's status and related information, and to perform other duties as provided herein. The Superintendent, Chairperson, or Vice Chairperson may convene additional meetings, if necessary.
- b) All Committee meetings shall be held within the District's geographic boundaries.
- c) Minutes will be prepared by a representative of the District and will be distributed to the Committee within 15 business days. The minutes will be voted upon for the record at the next scheduled Committee meeting.

DISTRICT DUTIES AND RESPONSIBILITIES

- a) The Chief Operating Officer shall act as the Superintendent's designee to the Committee.
- b) The Superintendent or his designee shall oversee management's action plan to respond to any written report from the Committee with findings or suggestions for improvement within 15 business days. All recommendations and management action plans from inception to date will be tracked and made available to the Committee and Board. The District's website and other communication avenues will also publicize the Committee's report and management's action plan for use by the general public.
- c) The District shall have a commitment to the Committee, provide open communication, and provide necessary technical and administrative assistance in a timely fashion as follows:
 - 1. Provision of a meeting room, including any necessary audio/visual equipment;
 - 2. Preparation and copies of any documentary meeting materials, such as agendas and reports; and distribution of those materials to the Committee in a timely manner;
 - 3. Provision of a quarterly summary progress report covering the Bond Programs;
 - 4. Access to other information to effectively perform its oversight function.
 - 5. Retention of all Committee meeting records, and providing public access to such records on the District's website; and
 - 6. Notify the public of Committee meeting times and locations. The meetings are open to the public.
- d) Summary progress reports will communicate and provide an explanation for the following attributes in a clear concise manner. As part of reporting, HISD will identify projects that experience a significant impact to schedule, budget, or scope of work. Detail reports can be provided upon the Committee's request.
 - 1. Project schedules with anticipated completion dates and current status.
 - 2. Project scope
 - 3. Contingency report (change allowance, encumbrances, and available budget)
 - 4. Expenditure reports
 - 5. Status of Minority/or Woman Owned Business Enterprise (M/WBE)
- e) The appropriate District staff, District consultants, and/or designees shall attend all Committee proceedings in order to provide a status update for their area of responsibility as it relates to the Bond Programs and answer any questions from Committee members.
- f) The Office of Inspector General will consider the input and specific audit requests of the Committee and HISD management during its development of the Annual Audit Plan. Audit projects conducted by the Office of Inspector General will be completed by the issuance of a formal audit report, which will be provided to the Board Audit Committee and made available to the Committee. Such reports will be publicized on the District's website for use by the general public.

- g) The District acknowledges that the Committee may request certain information that is sensitive or legally privileged. The District will use the counsel of its legal advisor to comply with such requests within the limits of Texas law and the best interest of the District.

ETHICS POLICY

This Ethics Policy provides general guidelines for Committee members to follow in carrying out their roles. Not all ethical issues that Committee members face are covered in this Policy. However, this Policy captures some of the critical areas that help define ethical and professional conduct for Committee members. The provisions of this Policy were developed from existing laws, rules, policies and procedures as well as from concepts that define generally accepted good business practices. Committee members are expected to strictly adhere to the provisions of this Ethics Policy.

POLICY

CONFLICT OF INTEREST. A Committee member shall not make or influence a District decision related to: (1) any contract funded by bond proceeds or (2) any construction project that will benefit the Committee member's outside employment, business, or provide a financial benefit to the Committee member or a family member, such as a spouse, child, parent, or sibling.

OUTSIDE EMPLOYMENT. A Committee member shall not use his or her authority over a particular matter to negotiate future employment with any person or organization that relates to: (1) any contract funded by bond proceeds; or (2) any construction project. A Committee member shall not make or influence a District decision related to any construction project involving the interest of a person with whom the member has an agreement concerning current or future employment, or remuneration of any kind. For a period of one (1) year after leaving the Committee, a former Committee member may not represent any person or organization for compensation in connection with any matter pending before the District that, as a Committee member, he or she participated in personally and substantially.

COMMITMENT TO UPHOLD LAW. A Committee member shall uphold the federal and Texas Constitutions, the laws and regulations of the United States and the State of Texas, and the policies, procedures, rules and regulations of the Houston Independent School District.

COMMITMENT TO DISTRICT. A Committee member shall place the interests of the District above any personal or business interest of the member.

MEMBER CERTIFICATION. A Committee member shall certify his or her understanding of Committee's Ethics Policy and disclose and sign an annual conflict of interest statement for existing conflicts and re-submit if any conflicts arise during their tenure.



Executive Summary

EXECUTIVE SUMMARY

The Houston Independent School District Construction Services team has so far this year brought online nine facilities, including three new schools, two renovated schools, one temporary campus, and three new additions.

The openings made for an extremely active first quarter, as the 2012 Bond Program surpassed the halfway mark in terms of school completion rate.

Schools welcoming students to new facilities upon their return from winter break on Jan. 8 include Sharpstown, Scarborough, and North Forest high schools, and Robinson Elementary School. (The construction of North Forest High School and renovation of storm-damaged Robinson Elementary were overseen by the bond team, but not funded with bond dollars.) Also in January, Austin High School opened a temporary campus to house students for the duration of construction on their new building.

Additional openings took place in March after Spring Break, with Parker Elementary School opening its new building, and Westbury High School, Wilson Montessori, and Garden Oaks Montessori opening new additions.

Eighteen more schools are expected to wrap up construction by the end of 2018, making this year one of the busiest for HISD, the 2012 Bond, and the Construction Services team.

Construction on several schools will be wrapping up in the coming months, including Energy Institute High School, High School for Law Enforcement, Washington and Yates high schools, Lawson Middle School, Askew Elementary School, Eastwood, Pilgrim, and Young Women's College Preparatory academies, and Wilson and Garden Oaks Montessori schools.

Additionally, construction on Kinder HSPVA, Jordan High School for Careers, Wharton Dual Language Academy, and Worthing, Northside, and Westbury high schools are all scheduled to wrap up by the end of the year.

Work also continues on schools damaged during Hurricane Harvey. Construction at Hilliard Elementary School, which underwent significant renovation after being damaged by the storm, is wrapping up and the school is on track to re-open in August. Additionally, the four elementary schools — Scarborough, Braeburn, Kolter, and Mitchell — being rebuilt after sustaining significant damage from Hurricane Harvey are now in the design phase.

Harvey rebuild schools are not funded by the bond program, but the projects are being overseen by Bond and Construction Services staff.

In total, Construction Services is managing building programs on 27 campuses, 22 of which are 2012 Bond projects. By the end of the year, the construction completion rate for the 2012 Bond Program will be 80 percent.

With so many schools nearing completion, Construction Services has focused on finishing construction and working with schools to select and order furniture that soon will be delivered to campuses that will be transitioning into new spaces in the coming months.

The team also is working to coordinate tours and celebrations for new schools as they wrap up and come on-line. Project managers and district staff have hosted walk-throughs for project advisory team members and trustees at High School for Law and Justice, Kinder HSPVA, Yates and Madison high schools, and Garden Oaks Montessori.

The team also coordinated milestone celebrations at three schools during the first quarter. Kashmere High School and Codwell Elementary School (non-bond) held grand opening ceremonies, and Northside High School marked its construction progress with a wall signing celebration.

Five more grand opening/building dedication celebrations are planned for the second quarter, including Scarborough High School (April 26), Sharpstown High School (May 3), North Forest High School (May 4), Wisdom High School (May 15), and Furr High School (May 18).

DESIGN MILESTONES

Last April, the Houston Independent School District Board of Education approved a plan allowing nearly \$99.1 million in forecasted bond surplus to be used for outstanding needs at bond campuses across the district. The impact of that realignment has become more evident in the first quarter of 2018. The scope refinements and design work for more than a dozen of these “mini-projects” have been completed and construction has begun.

Additionally, drawings, permitting, and pricing are being finalized so that projects and related enhancements can begin at DeBakey High School for Health Professions, Sharpstown High School, Lawson Middle School, Parker Elementary School, Askew Elementary School, Waltrip High School, Northside High School, and Wilson Montessori. Some of the needed improvements and academic programmatic requests that are being added to the bond projects as a result of the re-aligned funds include additional seating in gymnasiums for student assemblies, enhanced acoustical treatment in common areas, improved fine arts spaces, modernization of an existing cafeteria/kitchen, audiovisual and theatrical equipment upgrades, improvements to interior finishes, and various repairs to the exterior building envelopes.

The Bellaire High School project is continuing to move forward. Design work and drawing development continue to progress, with the first phase of selective demolition and construction scheduled to begin this summer.

Additionally, the Construction Services department continues its push for design excellence and sustainability for all the 2012 Bond Program projects. In the first quarter, the Milby High School project was honored with a 2018 Good Brick Award from Preservation Houston. This project also was awarded a Silver Level L.E.E.D. Certification from the U.S Green Building Council. Milby is the second project in the 2012 Bond Program to achieve L.E.E.D. certification and the first one in the 2012 Bond Program to reach Silver level certification. HISD currently has more than 20 projects registered with the U.S. Green Building Council and awaiting L.E.E.D. certification. Additionally, we have four non-bond projects also seeking L.E.E.D. certification.

Also this quarter, the Condit Elementary School project received the Caudill Award, the highest honor in the annual Exhibit of School Architecture competition, which is facilitated by Texas Association of School Board Administrators and Texas Association of School Boards for projects that exemplify excellence in planning and design of

the learning environment. Condit was recognized for how the compact, two-story, transformational 21st Century learning environment fulfills the desire of the community for a non-traditional school.

M/WBE NETWORKING ACTIVITIES

The Office of Business Assistance held and participated in multiple programs to promote HISD business and bid opportunities during the first quarter. The Supplier Diversity team sponsored three Workshop Wednesday meetings, which are held monthly to provide information to M/WBEs on topics of interest. First quarter workshop topics included how to do business with HISD, how to access capital, and how to create proposals.

The Business Assistance/Supplier Diversity Team also promoted bid opportunities and pre-bid meetings to their extensive contact list of minority companies, participated in 11 outreach events, and continued its partnership with the Interagency Mentor-Protégé Program. The current M/WBE participation rate for 2012 Bond projects is 26.48 percent — above the 20 percent goal originally set by program officials.

COMMUNICATIONS AND COMMUNITY ENGAGEMENT

The Bond Communications Team spent much of the first quarter planning and implementing communications plans for the nine new schools and additions that opened during the first quarter.

Team members worked with school principals to develop communications materials needed to ensure transitions and school openings went smoothly. The team also produced social media teaser videos to generate excitement about the new facilities in advance of their openings and carried out extensive, on-site, first-day coverage — blog posts, project updates, photos, videos, and social media posts.

The team continued to focus on updating the bond website, writing and distributing project updates, and promoting the @Build_HISD twitter account, which has grown to 412 followers, distributed more than 324 tweets, and earned more than half a million impressions during the first quarter.

Bond Communications also led the planning, promotion, and execution of grand opening celebrations at Kashmere High School and Codwell Elementary School (non-bond), and a wall signing celebration at Northside High School. The Northside event, in particular, drew in hundreds of stakeholders.

Planning is now underway for five more milestone events scheduled for the second quarter of 2018

REAL ESTATE

With all purchases complete under the 2012 bond program, the Real Estate department is maintaining and renewing current lease agreements as needed, assisting project managers with land planning issues, and searching for possible sites for future development. The department continues to supplement and maintain the centralized database of key documents for all HISD properties.



Askew Elementary School

Project Update Report

FACILITIES CAPITAL PROGRAM

HISD CAPITAL IMPROVEMENT PROGRAM — 2012 Facilities Capital Program — Page 1 of 1

Project	Scope of Work	Proposed Project Budget
High Schools:		\$
Austin High School	New facility preserving the architecturally significant building structure for a campus accommodating 1,800 – 2,000 students.	68,429,000
Bellaire High School	New 2,800 – 3,100 student school that will incorporate the recently completed science classroom and laboratory wing.	106,724,000
Davis High School	New facility preserving the architecturally significant building structure for a campus accommodating 1,500 – 1,700 students.	46,764,000
DeBaKey High School	New 900 – 1,000 student health professions school.	64,512,000
Eastwood Academy	New facility that will incorporate the new 2 story classroom wing for a campus accommodating 500 students.	10,875,000
Furr High School	New 1,100 – 1,300 student school.	55,100,000
Houston High School	New 2,550 – 2,750 student school that will incorporate the new science classroom and laboratory wing.	101,428,000
HSPVA	New 750 student performing and visual arts school.	80,178,000
Jones High School	Renovations to existing school facilities.	1,125,000
Jordan High School	New 600 – 800 student school.	36,693,000
Kashmere High School	Renovations to existing school facilities and site improvements.	17,000,000
Lamar High School	New facility preserving the architecturally significant building structure for a campus accommodating 2,800 – 3,100 students.	107,974,000
Lee High School	New 1,700 – 1,900 student school.	73,801,000
Madison High School	New 1,900 – 2,100 student school that will incorporate recent science and classroom building renovations.	82,736,000
Milby High school	New facility preserving the architecturally significant building structure for a campus accommodating 1,800 – 2,000 students.	68,810,000
North Early College	New 400 student early college school.	13,500,000
Scarborough High School	Renovations to existing school facilities and site improvements.	12,566,000
Sharpstown High School	New 1,300 – 1,500 student school.	54,944,000
Sharpstown International High School	Renovations to existing school facilities and site improvements.	6,125,000
South Early College	New 400 student early college school.	13,500,000
Sterling High School	New 1,600 – 1,800 student school.	72,304,000
Waltrip High School	Partial replacement and general renovations to accommodate 1,800 – 2,000 students.	30,115,000
Washington High School	New 1,100 – 1,300 student school.	51,732,000
Westbury High School	Partial replacement and general renovations to accommodate 2,300 – 2,500 students.	40,006,000
Worthing High School	New facility that will incorporate the new 2 story classroom wing for a campus accommodating 1,100 – 1,300 students.	30,180,000
Yates High School	New 1,300 – 1,500 student school.	59,481,000
Young Men's College Prep.	Partial replacement and general renovations to complement portions of the Howard Payne Carter Career Center for a campus accommodating 900 – 1,000 students.	28,675,000
Young Women's College Prep.	Partial replacement and general renovations for a campus accommodating 900 – 1,000 students.	27,159,000
	High School Subtotal	\$1,362,436,000
Middle Schools:		
Dowling Middle School	New 1,300 – 1,500 student school.	59,125,000
Grady Middle School	New addition to complete multi-phase master plan for the campus.	14,825,000
	Middle School Subtotal	\$73,950,000
K-8s:		
Garden Oaks Montessori K-8 School	New addition and general renovations of the existing facilities accommodating 750 – 900 students.	26,678,000
Mandarin Chinese Language Immersion School at Gordon K-8	New 750 – 900 student school.	32,161,000
Pilgrim Academy K-8	New addition for a campus accommodating 750 – 900 students.	7,989,000
Wharton Dual Language School K-8	New addition and general renovations of the existing facilities accommodating 750 – 900 students.	35,603,000
Wilson Montessori School K-8	New addition and general renovations of the existing facilities accommodating 750 – 900 students.	18,914,000
	K-8 Subtotal	\$121,345,000
Elementary Schools:		
Askew Elementary School	850 student new school — replacement.	26,632,000
Parker Elementary School	850 student new school — replacement.	29,485,000
Relief Elementary School	750 student new school to be built in the west Houston area.	23,417,000
	Elementary Subtotal	\$79,534,000
All Schools		\$1,637,265,000
Districtwide Projects:		
District Athletic Improvements	Replacement of regional field house(s) and athletic facility improvements.	44,675,000
District Wide Land Acquisition	Districtwide funds to supplement significant site/parking constraints.	55,767,000
Middle School Restroom Renovation	Districtwide middle school restroom renovations.	35,000,000
Districtwide Technology	Districtwide technology improvements.	100,000,000
Districtwide Safety and Security	Districtwide safety and security improvements.	17,293,000
	Districtwide Total	\$252,735,000
	Grand Total	\$1,890,000,000

1. Funding within this bond for North and South Early College will be combined with funds previously allocated from the 2007 bond for these projects to meet the schools programmatic needs.
2. HSPVA moved to district 8 due to a proposed site for the new school located at 1300 Capital.
3. Program costs allocated to each project budget will be separated into various program budgets to provide better oversight and financial management, at a later date.
4. New schools / replacement projects will undergo a school site specific ed-spec development process and all schools will undergo a scope to budget process.
5. Project budgets include allocations for planning, design, construction, administration, and other related costs.
6. The current allocation for the Young Men's College Preparatory Academy (YMCPA) will allow for a demolition of the EO Smith facility, the addition of a smaller facility, and the renovation of the HP Carter facility for use by the YMCPA. An alternate plan for the project to include the demolition of both the EO Smith and HP Carter facilities and the building of a new school would cost an additional \$13,727,000.
7. Condit ES will be rebuilt and funded from surplus bond funds and/or the sale of real estate.
8. High School for Law Enforcement and Criminal Justice will be rebuilt and funded from surplus bond funds and/or the sale of real estate.

2012 BOND PHASING SCHEDULE

GROUP 1

- Planning and Design — Early/Mid 2013
- Anticipated Construction to Begin — Mid/Late 2014
 - Condit Elementary School
 - DeBakey High School for Health Professions
 - Furr High School
 - Tanglewood Middle School
 - Kinder HSPVA
 - Wisdom High School
 - Mandarin Immersion Magnet School
 - Milby High School
 - North Houston Early College High School
 - Mark White Elementary School
 - Sharpstown High School
 - South Early College High School
 - Sterling Aviation High School
 - Waltrip High School
 - Booker T. Washington High School
 - Worthing High School
 - Mickey Leland College Preparatory Academy for Young Men

GROUP 2

- Planning and Design — Early/Mid 2014
- Anticipated Construction to Begin — Mid/Late 2015
 - Bellaire High School
 - Northside High School
 - Lawson Middle School
 - Eastwood Academy
 - High School for Law & Justice
 - Lamar High School
 - Parker Elementary School
 - Yates High School


GROUP 3

- Planning and Design — Late 2014/Early 2015*
- Anticipated Construction to Begin — Mid/Late 2016
 - Askew Elementary School
 - Sam Houston Math, Science, & Technology Center
 - Jordan High School for Careers
 - Young Women’s College Preparatory Academy

GROUP 4

- Planning and Design — Late 2014/Early 2015*
- Anticipated Construction to Begin — Mid 2017
 - Austin High School
 - Garden Oaks Montessori
 - Jones Futures Academy
 - Kashmere High School
 - Madison High School
 - Pilgrim Academy
 - Scarborough High School
 - Sharpstown International School
 - Westbury High School
 - Wharton Dual Language Academy
 - Wilson Montessori School

*The planning and design schedule has been accelerated to give the district the flexibility to start construction earlier should market conditions warrant. The original schedule had planning and design for Group 3 in Early / Mid 2015 and for Group 4 in Late 2015 / Early 2016.

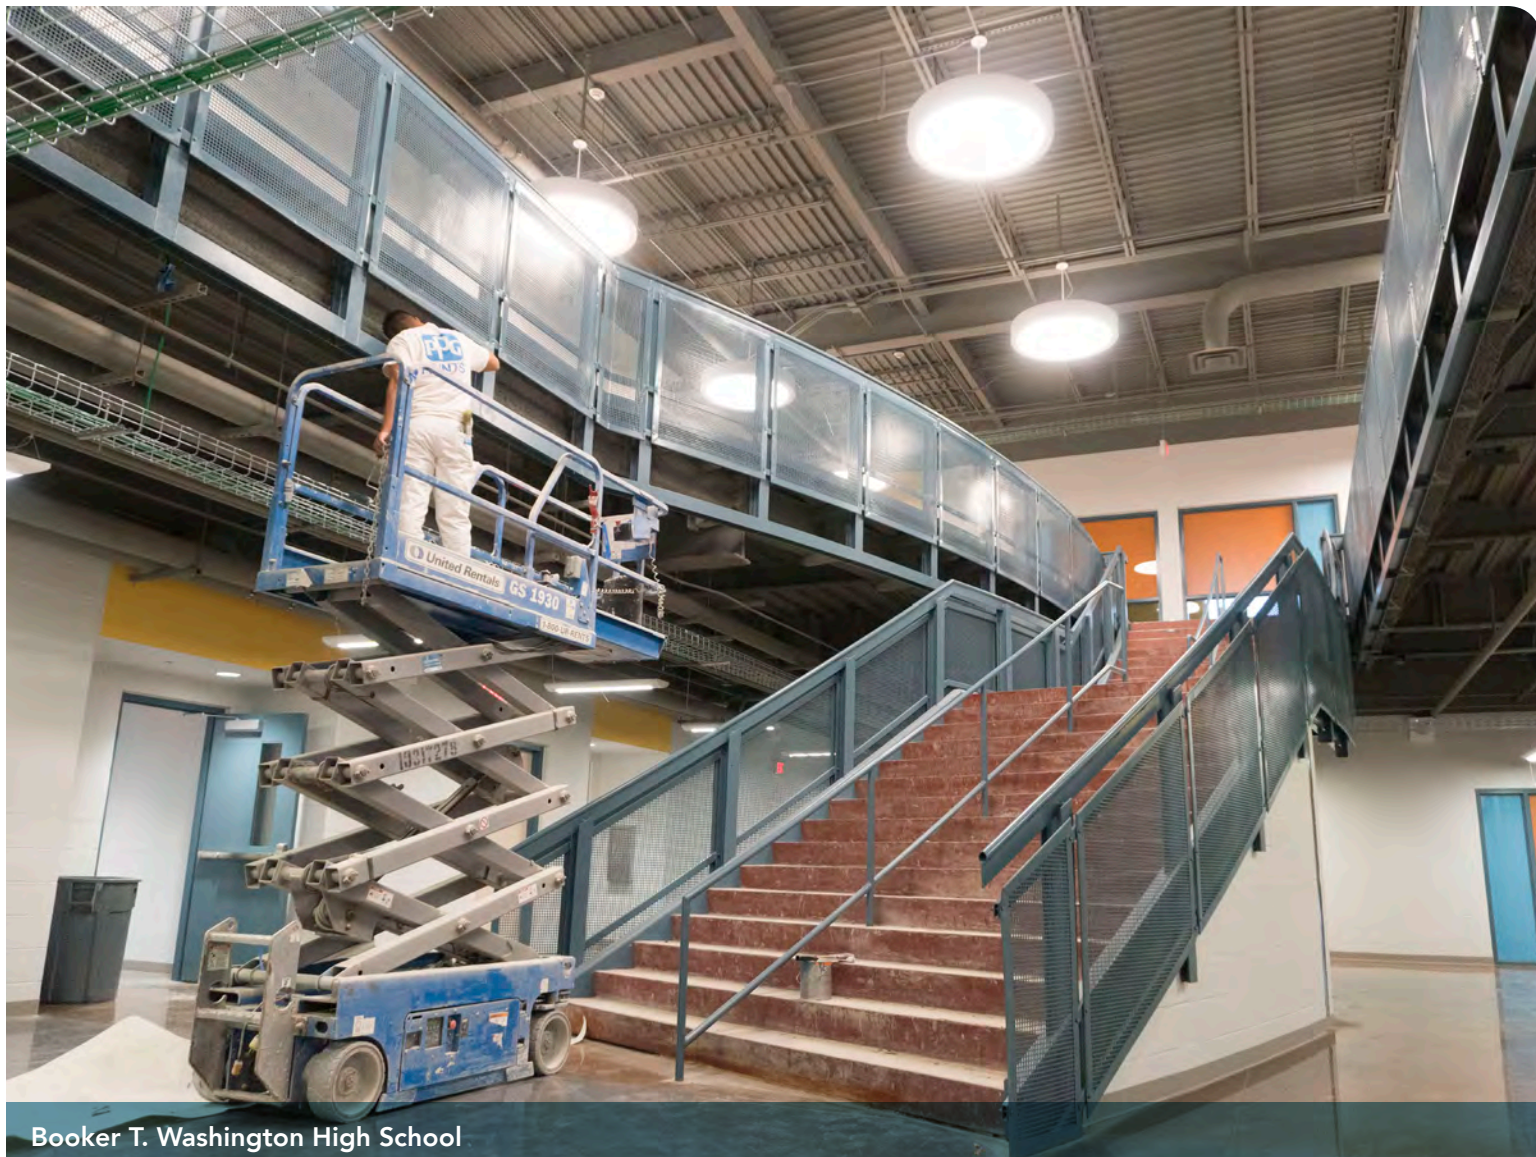

Booker T. Washington High School

Project Update Report — Group 1

Traffic Light Summary



Green light indicates the project is on schedule, on budget, and there are no pending issues of concern.

Yellow light indicates a project may have budget or schedule concerns, and there are issues that bear additional monitoring.

Red light indicates a project has significant budget and/or schedule concerns, and there are issues to be addressed.

*All Projects are currently rated Green

**KEY FACTS**

Budget
\$24,293,919

Trustee
Sue Deigaard

Location
7000 South 3rd St.

CONDIT ELEMENTARY


Condit Elementary School was originally built in 1909. The school moved to its current facility in Bellaire in 1914, with an addition built in 1927. The pre-K – 5 campus offers a Spanish dual language program, as well as a Vanguard neighborhood program.

SCOPE OF WORK

New elementary school for 750 students.


PROJECT STATUS

Project closeout ongoing.

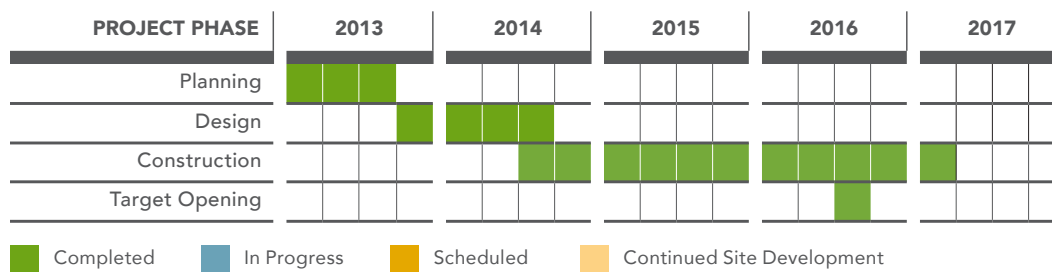TARGET SCHEDULE

Condit Elementary – continued

INFORMATION

Indicator	ID	Project/School/Facility	Budget
	C-130	Condit Elementary	\$24,293,919
	Planning and Design Start		Construction Start
	Early/Mid 2013		Mid/Late 2014
	Phase		% of Phase
	Closeout		95%
Project Team			
HISD Manager		Andreas Peebles	
Architect		VLK Architects	
Contractor		DivisionOne Construction	
Program Manager		Heery International, Inc.	

MILESTONES COMPLETED

Programming/Conceptual Design	✓
Schematic Design Phase	✓
Design Development	✓
Construction Documents	✓
Bid & Award	✓
Construction Start	✓
Construction Complete	✓



**KEY FACTS**

Budget
\$64,512,000

Supplemental Funding
\$2,582,806

Trustee
Sue Deigaard

Location
2545 Pressler St.

DEBAKEY HIGH SCHOOL FOR HEALTH PROFESSIONS

The Michael E. DeBakey High School for Health Professions provides a rigorous and comprehensive pre-college program for students pursuing careers in the health and medical field.


The new school is located on donated land on the western side of the Texas Medical Center. The location provides students with access to some of the best medical facilities in the world.

SCOPE OF WORK

New school for 900 - 1,000 students.


PROJECT STATUS

Project closeout ongoing.

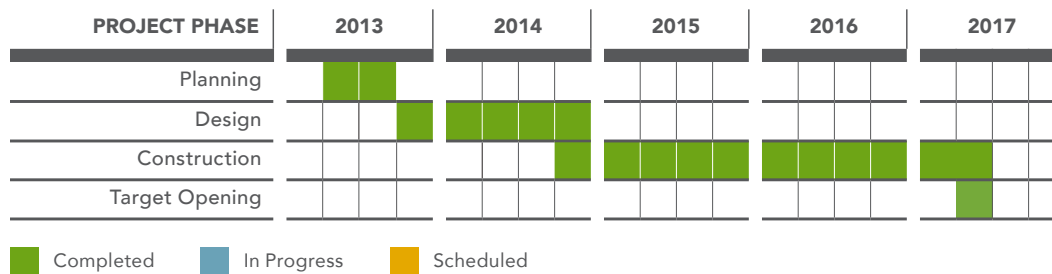TARGET SCHEDULE

DeBakey High School — continued

INFORMATION

Indicator	ID	Project/School/Facility	Budget
	C-026	DeBakey High School	\$64,512,000
	Planning and Design Start		Construction Start
	Early/Mid 2013		Mid/Late 2014
	Phase		% of Phase
	Closeout		99%
Project Team			
HISD Manager		Andreas Peebles	
Architect		WHR Lake-Flato	
Contractor		Tellepsen Builders, L.P.	
Program Manager		Heery International, Inc.	

MILESTONES COMPLETED

Programming/Conceptual Design	✓
Schematic Design Phase	✓
Design Development	✓
Construction Documents	✓
Bid & Award	✓
Construction Start	✓
Construction Complete	✓





KEY FACTS

Budget
\$55,100,000

Supplemental Funding
\$1,258,524

Trustee
Diana Dávila

Location
520 Mercury Drive

FURR HIGH SCHOOL

Furr High School opened in the fall of 1961 on Houston's east side. The campus currently includes nine school buildings and 15 temporary buildings.

The school is home to the Futures Academy of Petroleum Engineering Technology at Furr. It also offers career pathways in energy and mass communications through linked learning, an educational approach that combines rigorous academics with hands-on, real-world experiences.


SCOPE OF WORK

New high school to accommodate 1,000 – 1,300 students.

PROJECT STATUS


Athletic field construction and project closeout ongoing.

TARGET SCHEDULE

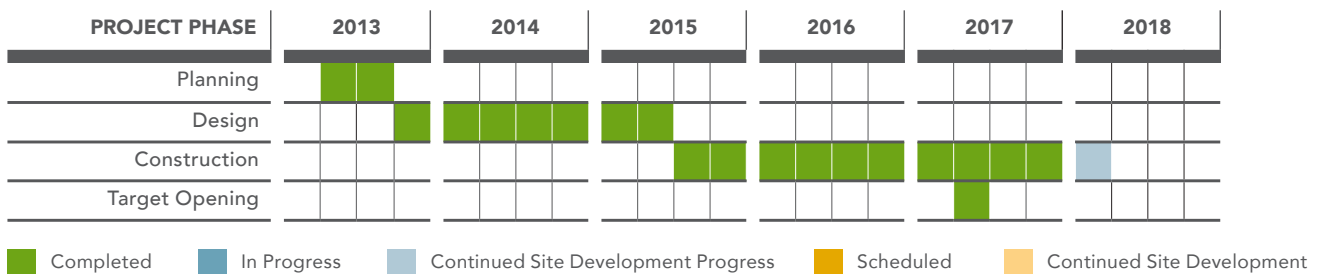

Furr High School — continued

INFORMATION

Indicator	ID	Project/School/Facility	Budget
	C-004	Furr High School	\$55,100,000
	Planning and Design Start		Construction Start
	Early/Mid 2013		Mid/Late 2015
	Phase		% of Phase
	Site Development/Closeout		60%/15%
Project Team			
HISD Manager		Andreas Peebles	
Architect		ERO Architects Inc.	
Contractor		Prime Contractors	
Program Manager		Rice & Gardner Consultants, Inc.	

MILESTONES COMPLETED

Programming/Conceptual Design	✓
Schematic Design Phase	✓
Design Development	✓
Construction Documents	✓
Bid & Award	✓
Construction Start	✓
Construction Complete	✓



**KEY FACTS**

Budget
\$14,825,000

Trustee
Anne Sung

Location
5215 San Felipe St.

TANGLEWOOD MIDDLE SCHOOL

Tanglewood Middle School, located in Houston's Galleria area, was originally built in 1949. It was replaced by a new main school building, which was completed in 2012.

As an International Baccalaureate school, Tanglewood offers a rigorous academic program that aims to develop knowledgeable, caring, inquisitive students who embrace multiculturalism and diversity and want to make the world a better place.

SCOPE OF WORK

New addition to complete multi-phase master plan for the campus.

PROJECT STATUS

Complete.


TARGET SCHEDULE

PROJECT PHASE	2013	2014	2015	2016
Planning	■ ■ ■			
Design		■ ■ ■ ■ ■		
Construction			■ ■ ■ ■ ■	■
Target Opening				■

■ Completed
 ■ In Progress
 ■ Scheduled

Tanglewood Middle School — continued

INFORMATION

Indicator	ID	Project/School/Facility	Budget
	C-068	Tanglewood Middle School	\$14,825,000
	Planning and Design Start		Construction Start
	Early/Mid 2013		Mid/Late 2014
	Phase		% of Phase
	Closeout		100%
Project Team			
HISD Manager		Andreas Peebles	
Architect		Natex Architects Inc.	
Contractor		DivisionOne Construction	
Program Manager		Rice & Gardner Consultants, Inc.	

MILESTONES COMPLETED

Programming/Conceptual Design	✓
Schematic Design Phase	✓
Design Development	✓
Construction Documents	✓
Bid & Award	✓
Construction Start	✓
Construction Complete	✓



**KEY FACTS**

Budget
\$80,178,000

Supplemental Funding
\$8,167,860

Trustee
Diana Dávila

Location
790 Austin St.

KINDER HIGH SCHOOL FOR THE PERFORMING AND VISUAL ARTS (HSPVA)

HSPVA is a performing and visual arts magnet school and national model for combining arts and academics. The current facility was constructed in 1981.


Under the 2012 bond program, a new facility will be built in downtown Houston near other arts and theatrical venues located in the city's Theater District. The new campus will be located on district property that spans a city block.

SCOPE OF WORK

New performing and visual arts school to accommodate 750 students.


PROJECT STATUS

Interior finishes are ongoing.

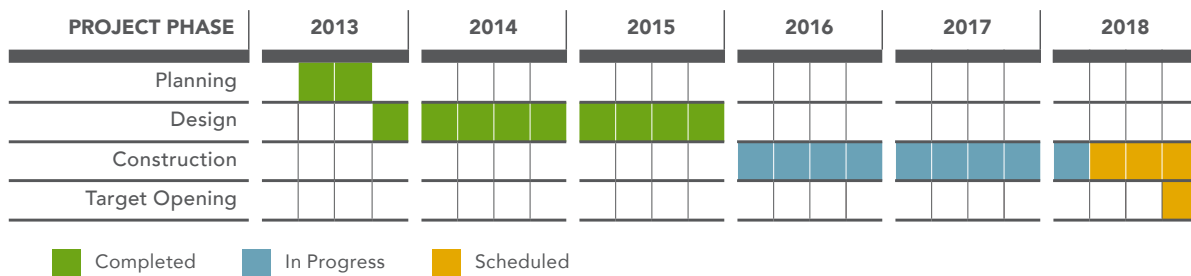TARGET SCHEDULE

Kinder High School for the Performing and Visual Arts — continued

INFORMATION

Indicator	ID	Project/School/Facility	Budget
	C-025	Kinder High School for the Performing and Visual Arts	\$80,178,000
	Planning and Design Start		Construction Start
	Early/Mid 2013		Early/Mid 2016
	Phase		% of Phase
	Construction		84%
Project Team			
HISD Manager		Andreas Peebles	
Architect		Gensler	
Contractor		McCarthy	
Program Manager		Rice & Gardner Consultants, Inc.	

MILESTONES COMPLETED

Programming/Conceptual Design	✓
Schematic Design Phase	✓
Design Development	✓
Construction Documents	✓
Bid & Award	✓
Construction Start	✓
Construction Complete	





KEY FACTS

Budget
\$73,801,000

Supplemental Funding
\$1,066,632

Trustee
Anne Sung

Location
6529 Beverly Hill St.

WISDOM HIGH SCHOOL

Wisdom High School was originally built in 1962 in west Houston. The comprehensive high school offers career pathways in construction and design through linked learning, an educational approach that combines rigorous academics with hands-on, real-world experiences.


SCOPE OF WORK

New school for 1,700 – 1,900 students.

PROJECT STATUS


Project closeout ongoing.

TARGET SCHEDULE

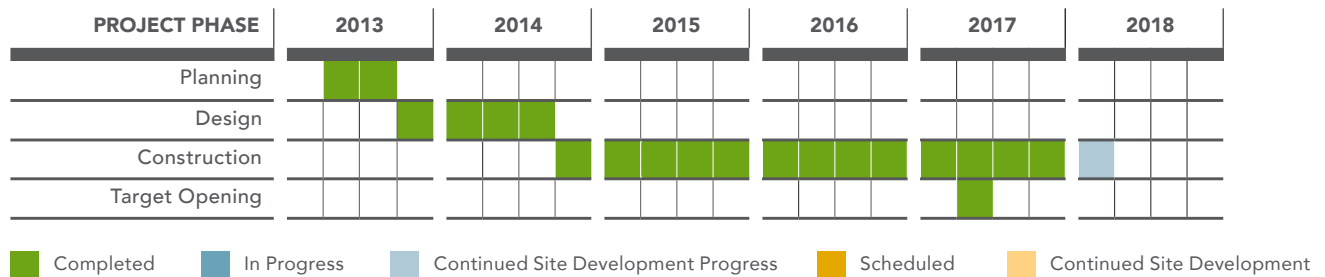

Wisdom High School — continued

INFORMATION

Indicator	ID	Project/School/Facility	Budget
	C-009	Wisdom High School	\$73,801,000
	Planning and Design Start		Construction Start
	Early/Mid 2013		Mid/Late 2014
	Phase		% of Phase
	Closeout		15%
Project Team			
HISD Manager		Andreas Peebles	
Architect		WHR Architects, Inc.	
Contractor		Satterfield and Pontikes Construction, Inc.	
Program Manager		HISD	

MILESTONES COMPLETED

Programming/Conceptual Design	✓
Schematic Design Phase	✓
Design Development	✓
Construction Documents	✓
Bid & Award	✓
Construction Start	✓
Construction Complete	✓



**KEY FACTS**

Budget
\$32,161,000

Trustee
Anne Sung

Supplemental Funding
\$3,610,582

Location
5445 W. Alabama St.

MANDARIN IMMERSION MAGNET SCHOOL

The Mandarin Immersion Magnet School is currently housed in a small elementary school that was built in 1953 in Bellaire.


The school opened in the fall of 2012, becoming one of the first in Texas to offer Mandarin language immersion. The school started with pre-kindergarten through second grades, with plans to add additional grades each year, eventually becoming a K-8 campus.

SCOPE OF WORK

New school for 750 – 900 students.


PROJECT STATUS

Project closeout ongoing.

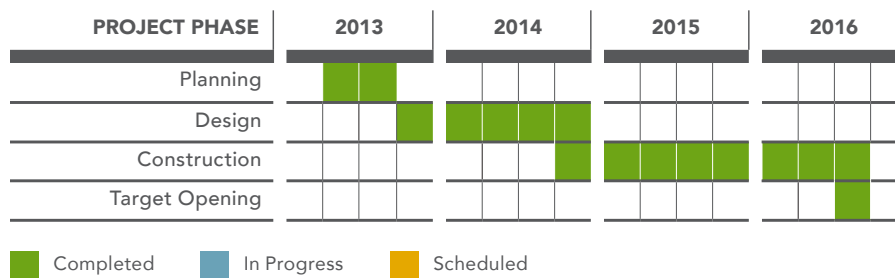TARGET SCHEDULE

Mandarin Immersion Magnet School — continued

INFORMATION

Indicator	ID	Project/School/Facility	Budget
	C-460	Mandarin Immersion Magnet School	\$32,161,000
	Planning and Design Start		Construction Start
	Early/Mid 2013		Mid/Late 2014
	Phase		% of Phase
	Closeout		98%
Project Team			
HISD Manager		Andreas Peebles	
Architect		PBK Architects	
Contractor		Satterfield & Pontikes Construction, Inc.	
Program Manager		Heery International, Inc.	

MILESTONES COMPLETED

Programming/Conceptual Design	✓
Schematic Design Phase	✓
Design Development	✓
Construction Documents	✓
Bid & Award	✓
Construction Start	✓
Construction Complete	✓



**KEY FACTS**

Budget
\$42,402,000

Supplemental Funding
\$1,651,044

Trustee
Rhonda Skillern-Jones

Location
1700 Gregg St..

MICKEY LELAND COLLEGE PREPARATORY ACADEMY FOR YOUNG MEN


Mickey Leland College Preparatory Academy was transformed into an all-male college preparatory academy in 2011. Serving students in grades 6 – 12, the campus offers a small, inclusive environment and rigorous college preparatory curriculum with an emphasis on Advanced Placement and STEM (Science, Technology, Engineering and Math) courses.

SCOPE OF WORK

New facility for a campus accommodating 900 – 1,000 students.


PROJECT STATUS

Athletic field construction and project closeout ongoing.

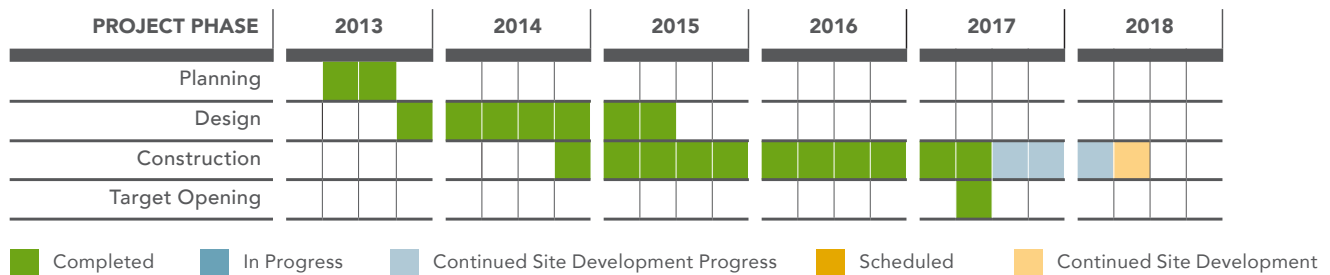TARGET SCHEDULE

Mickey Leland College Preparatory Academy — continued

INFORMATION

Indicator	ID	Project/School/Facility	Budget
	C-067	Mickey Leland College Preparatory Academy	\$42,402,000
	Planning and Design Start		Construction Start
	Early/Mid 2013		Mid/Late 2014
	Phase		% of Phase
	Site Development/Closeout		85%/25%
Project Team			
HISD Manager		Andreas Peebles	
Architect		Harrison Kornberg with Corgan Associates	
Contractor		Prime Contractors	
Program Manager		Rice & Gardner Consultants, Inc.	

MILESTONES COMPLETED

Programming/Conceptual Design	✓
Schematic Design Phase	✓
Design Development	✓
Construction Documents	✓
Bid & Award	✓
Construction Start	✓
Construction Complete	✓



**KEY FACTS**

Budget
\$68,810,000

Supplemental Funding
\$10,234,244

Trustee
Sergio Lira

Location
1601 Broadway St.

MILBY HIGH SCHOOL

Milby High School was constructed in 1926 in east Houston. The campus has seen numerous additions over the years.


The comprehensive high school is home to a STEM (Science, Technology, Engineering and Math) magnet program with three strands — Applied Science Health Professions, Computing Science, and Petroleum Exploration and Engineering. Through linked learning, an approach that combines rigorous academics with real-world experiences, the school also offers career pathways in culinary arts, cosmetology, welding, graphics technology and HVAC heating and cooling systems.

SCOPE OF WORK

New school preserving the architecturally significant building structure and accommodating 1,800 – 2,000 students.


PROJECT STATUS

Project closeout ongoing.

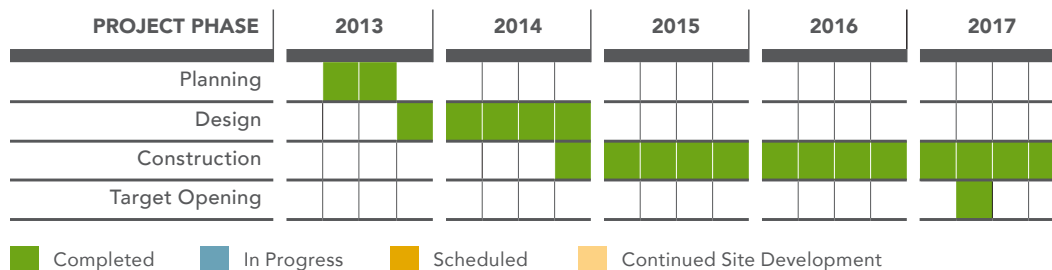TARGET SCHEDULE

Milby High School — continued

INFORMATION

Indicator	ID	Project/School/Facility	Budget
	C-011	Milby High School	\$68,810,000
	Planning and Design Start		Construction Start
	Early/Mid 2013		Mid/Late 2014
	Phase		% of Phase
	Closeout		98%
Project Team			
HISD Manager		Andreas Peebles	
Architect		Kirksey Architecture	
Contractor		Tellepsen Builders, LP	
Program Manager		Heery International, Inc.	

MILESTONES COMPLETED

Programming/Conceptual Design	✓
Schematic Design Phase	✓
Design Development	✓
Construction Documents	✓
Bid & Award	✓
Construction Start	✓
Construction Complete	✓





KEY FACTS

Budget
\$13,500,000

Trustee
Elizabeth Santos

Location
8001 Fulton St.

NORTH HOUSTON EARLY COLLEGE HIGH SCHOOL

North Houston Early College High School is one of five HISD early college campuses offering students the chance to earn both a high school diploma and an associate's degree while still in high school.

Once complete, the new school will feature modern science labs, flexible learning spaces, and a college resource center, where students can obtain scholarship and registration information, as well as access to counselors.


SCOPE OF WORK

New school for 400 students at the Houston Community College – Northline Campus.

PROJECT STATUS


Complete.

TARGET SCHEDULE

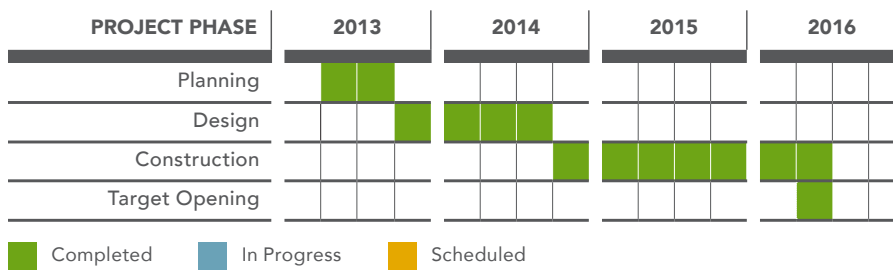

North Houston Early College High School – continued


INFORMATION

Indicator	ID	Project/School/Facility	Budget
	C-308	North Houston Early College High School	\$13,500,000
	Planning and Design Start		Construction Start
	Early/Mid 2013		Mid/Late 2014
	Phase		% of Phase
	Closeout		100%
Project Team			
HISD Manager		Andreas Peebles	
Architect		RdIR Architects	
Contractor		Drymalla	
Program Manager		N/A	

MILESTONES COMPLETED

Programming/Conceptual Design	✓
Schematic Design Phase	✓
Design Development	✓
Construction Documents	✓
Bid & Award	✓
Construction Start	✓
Construction Complete	✓





KEY FACTS

Budget
\$54,944,000

Supplemental Funding
\$7,889,585

Trustee
Holly Maria Flynn Vilaseca

Location
7504 Bissonnet St.

SHARPSTOWN HIGH SCHOOL

Sharpstown High School is located in southwest Houston. It originally opened in 1968 as Sharpstown Junior-Senior High School, but separated from the middle school and moved to its current location the following year.

The comprehensive high school offers a variety of special programs, including Business Management and Administration, Career Development, Finance, Health Science, and Information Technology.


SCOPE OF WORK

New school for 1,300 – 1,500 students.

PROJECT STATUS


Abatement and demo has commenced on old building. Project closeout ongoing.

TARGET SCHEDULE

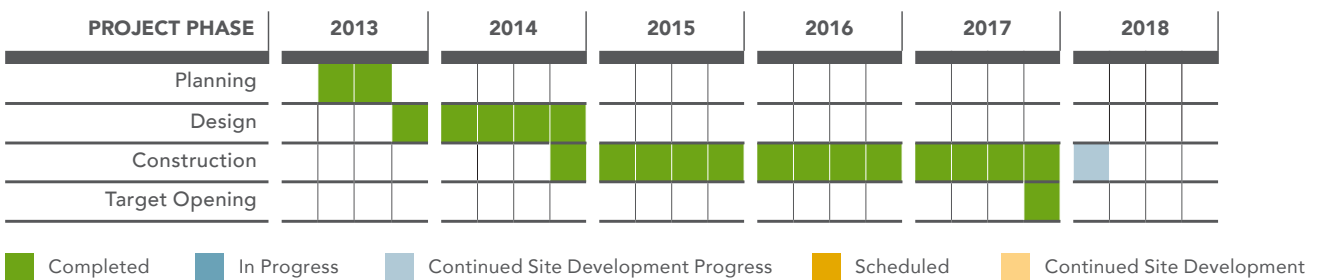

Sharpstown High School — continued

INFORMATION

Indicator	ID	Project/School/Facility	Budget
	C-023	Sharpstown High School	\$54,944,000
	Planning and Design Start		Construction Start
	Early/Mid 2013		Mid/Late 2014
	Phase		% of Phase
	Site Development/Closeout		15%/5%
Project Team			
HISD Manager		Andreas Peebles	
Architect		Kell-Munoz Co.	
Contractor		ICI Construction	
Program Manager		HISD	

MILESTONES COMPLETED

Programming/Conceptual Design	✓
Schematic Design Phase	✓
Design Development	✓
Construction Documents	✓
Bid & Award	✓
Construction Start	✓
Construction Complete	✓



**KEY FACTS**

Budget
\$13,500,000

Trustee
Wanda Adams

Location
1930 Airport Blvd.

SOUTH EARLY COLLEGE HIGH SCHOOL

South Early College High School is one of five HISD early college campuses offering students the chance to earn both a high school diploma and an associate's degree while still in high school.

The new school features flexible learning spaces that accommodate the school's technological programs, including robotics, computer technology, and software engineering.

SCOPE OF WORK

New school for 400 students at the Houston Community College – South Campus.

PROJECT STATUS

Complete.


TARGET SCHEDULE

PROJECT PHASE	2013	2014	2015	2016
Planning	■ ■ ■			
Design		■ ■ ■ ■ ■		
Construction			■ ■ ■ ■ ■ ■ ■	■ ■ ■ ■ ■
Target Opening				■

■ Completed
 ■ In Progress
 ■ Scheduled

South Early College High School – continued

INFORMATION

Indicator	ID	Project/School/Facility	Budget
	C-454	South Early College High School	\$13,500,000
	Planning and Design Start		Construction Start
	Early/Mid 2013		Mid/Late 2014
	Phase		% of Phase
	Closeout		100%
Project Team			
HISD Manager		Andreas Peebles	
Architect		Smith & Co.	
Contractor		Drymalla	
Program Manager		N/A	

MILESTONES COMPLETED

Programming/Conceptual Design	✓
Schematic Design Phase	✓
Design Development	✓
Construction Documents	✓
Bid & Award	✓
Construction Start	✓
Construction Complete	✓



**KEY FACTS**

Budget
\$72,304,000

Trustee
Jolanda Jones

Location
11625 Martindale Road

STERLING AVIATION HIGH SCHOOL


Sterling Aviation High School, constructed in 1965, consists of five main school buildings. The comprehensive high school is home to the Futures Academy of Logistics and Global Supply at Sterling. It also places a strong emphasis on its career pathway in aviation, which is offered through linked learning, an educational approach that combines rigorous academics with real-world experiences.

SCOPE OF WORK

New school for 1,600 – 1,800 students.


PROJECT STATUS

Athletic field construction and project closeout ongoing.

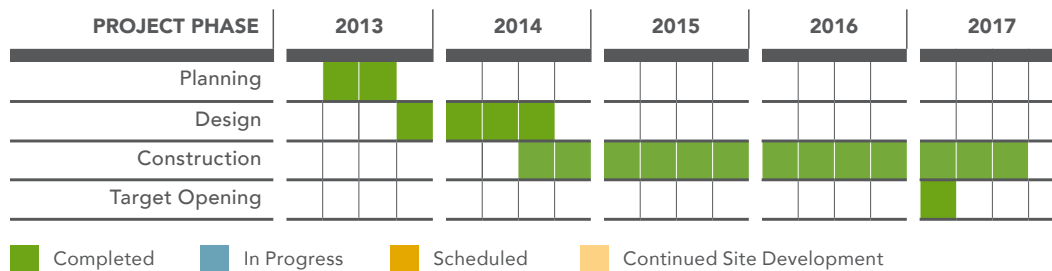TARGET SCHEDULE

Sterling Aviation High School – continued

INFORMATION

Indicator	ID	Project/School/Facility	Budget
	C-014	Sterling Aviation High School	\$72,304,000
	Planning and Design Start		Construction Start
	Early/Mid 2013		Mid/Late 2014
	Phase		% of Phase
	Site Development/Closeout		99%/95%
Project Team			
HISD Manager		Andreas Peebles	
Architect		SHW Group	
Contractor		Cadence McShane Construction, LLC	
Program Manager		Heery International, Inc.	

MILESTONES COMPLETED

Programming/Conceptual Design	✓
Schematic Design Phase	✓
Design Development	✓
Construction Documents	✓
Bid & Award	✓
Construction Start	✓
Construction Complete	✓





KEY FACTS

Budget
\$30,115,000

Supplemental Funding
\$2,123,961

Trustee
Elizabeth Santos

Location
1900 West 34th St.

WALTRIP HIGH SCHOOL

Waltrip High School opened in 1959 in the Oak Forest neighborhood in north Houston. The comprehensive high school offers a magnet program and linked learning career pathway in Research & Technology. Linked Learning is an educational approach that combines rigorous academics and real-world experiences with the goal of readying students for college and careers.


SCOPE OF WORK

Partial replacement and general renovations to accommodate 1,800 – 2,000 students.

PROJECT STATUS


Project closeout ongoing.

TARGET SCHEDULE

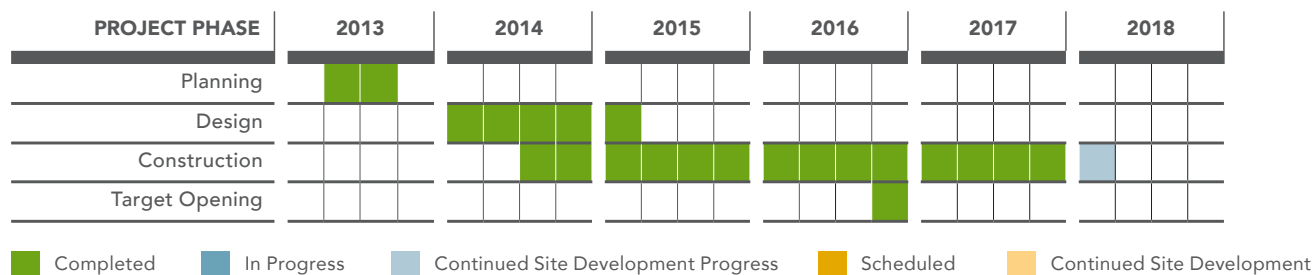

Waltrip High School — continued

INFORMATION

Indicator	ID	Project/School/Facility	Budget
	C-015	Waltrip High School	\$30,115,000
	Planning and Design Start		Construction Start
	Early/Mid 2013		Mid/Late 2014
	Phase		% of Phase
	Closeout		35%
Project Team			
HISD Manager		Andreas Peebles	
Architect		Gensler	
Contractor		Satterfield & Pontikes	
Program Manager		N/A	

MILESTONES COMPLETED

Programming/Conceptual Design	✓
Schematic Design Phase	✓
Design Development	✓
Construction Documents	✓
Bid & Award	✓
Construction Start	✓
Construction Complete	✓





KEY FACTS

Budget
\$51,732,000

Supplemental Funding
\$4,847,934

Trustee
Rhonda Skillern-Jones

Location
119 E. 39th St.

WASHINGTON HIGH SCHOOL

Booker T. Washington High School, named after an education pioneer, was constructed in 1958 in northwest Houston.

The comprehensive high school is home to the Futures Academy of Engineering Sciences at Washington. It also offers career pathways in building and construction through its linked learning program, an approach that combines rigorous academics with real-world experiences.


SCOPE OF WORK

New school for 1,100 – 1,300 students.

PROJECT STATUS


Interior finishes are ongoing.

TARGET SCHEDULE

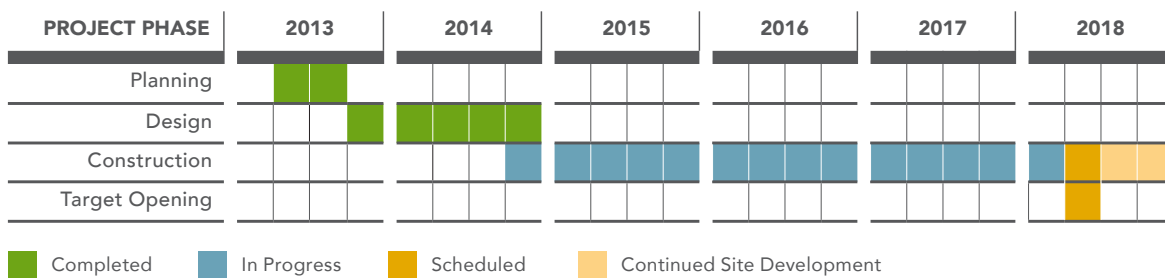

Washington High School — continued

INFORMATION

Indicator	ID	Project/School/Facility	Budget
	C-016	Washington High School	\$51,732,000
	Planning and Design Start		Construction Start
	Early/Mid 2013		Mid/Late 2014
	Phase		% of Phase
	Construction		95%
Project Team			
HISD Manager		Andreas Peebles	
Architect		Fanning-Howey/House Partners	
Contractor		Prime Contractors	
Program Manager		N/A	

MILESTONES COMPLETED

Programming/Conceptual Design	✓
Schematic Design Phase	✓
Design Development	✓
Construction Documents	✓
Bid & Award	✓
Construction Start	✓
Construction Complete	





KEY FACTS

Budget
\$23,417,000

Trustee
Anne Sung

Location
2515 Old Farm Road

MARK WHITE ELEMENTARY

Demographic projections and current student populations indicated a need for a new elementary school in the west Houston area. The campus was built to help address overcrowding in four neighboring schools.

In addition to a standard elementary curriculum, Mark White Elementary also offers a French language immersion program — the first of its kind in Texas.


SCOPE OF WORK

New school for 750 students.

PROJECT STATUS


Project closeout ongoing.

TARGET SCHEDULE

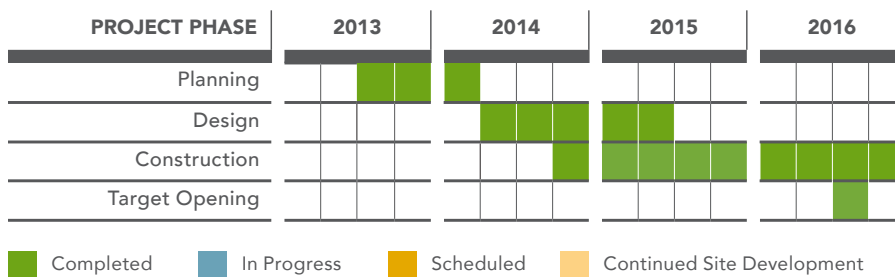

Mark White Elementary— continued

INFORMATION

Indicator	ID	Project/School/Facility	Budget
	TBD	Mark White Elementary	\$23,417,000
	Planning and Design Start		Construction Start
	Early/Mid 2013		Mid/Late 2014
	Phase		% of Phase
	Closeout		65%
Project Team			
HISD Manager		Andreas Peebles	
Architect		English & Associates	
Contractor		DivisionOne Construction	
Program Manager		Rice & Gardner Consultants, Inc.	

MILESTONES COMPLETED

Programming/Conceptual Design	✓
Schematic Design Phase	✓
Design Development	✓
Construction Documents	✓
Bid & Award	✓
Construction Start	✓
Construction Complete	✓





KEY FACTS

Budget
\$30,180,000

Supplemental Funding
\$2,897,460

Trustee
Wanda Adams

Location
9215 Scott St.

WORTHING HIGH SCHOOL

Worthing High School provides a comprehensive academic curriculum, along with career and technology programs, including career pathways in hotel and restaurant management through linked learning, an educational approach that combines rigorous academics with real-world experiences.

The main building at Worthing High School was constructed in 1959.


SCOPE OF WORK

New facility that will incorporate a new two-story classroom wing for a campus accommodating 1,100 – 1,300 students.

PROJECT STATUS


Exterior envelope and overhead MEP are ongoing.

TARGET SCHEDULE

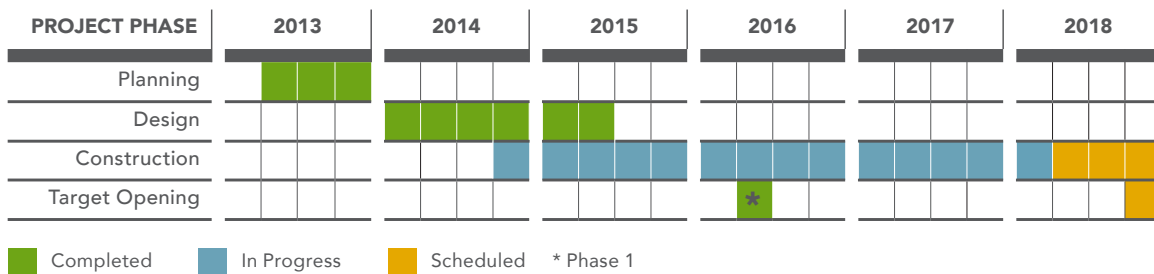

Worthing High School – continued

INFORMATION

Indicator	ID	Project/School/Facility	Budget
	C-019	Worthing High School	\$30,180,000
	Planning and Design Start		Construction Start
	Early/Mid 2013		Mid/Late 2014
	Phase 2		% of Phase 2
	Construction - Phase II		52%
Project Team			
HISD Manager		Andreas Peeples	
Architect		Molina Walker Architects	
Contractor		Prime Contractors	
Program Manager		N/A	

MILESTONES COMPLETED

Programming/Conceptual Design	✓
Schematic Design Phase	✓
Design Development	✓
Construction Documents	✓
Bid & Award	✓
Construction Start	✓
Construction Complete	





Project Update Report — Group 2



KEY FACTS

Budget
\$106,724,000

Supplemental Funding
\$25,290,428

Trustee
Sue Deigaard

Location
5100 Maple St., Bellaire

BELLAIRE HIGH SCHOOL

Bellaire High School serves more than 3,700 students and offers a variety of special programs, including a World Languages magnet program and International Baccalaureate, a rigorous academic program that aims to develop knowledgeable, caring, inquisitive students who embrace multiculturalism and diversity and want to make the world a better place.

The campus consists of one main building (built in 1955 with a 1981 addition) four smaller buildings, and a new science classroom building. The campus also has several temporary buildings.


SCOPE OF WORK

New school for 2,800 – 3,100 students that will incorporate the recently completed science classroom and laboratory wing.

PROJECT STATUS

Design development is ongoing.


TARGET SCHEDULE

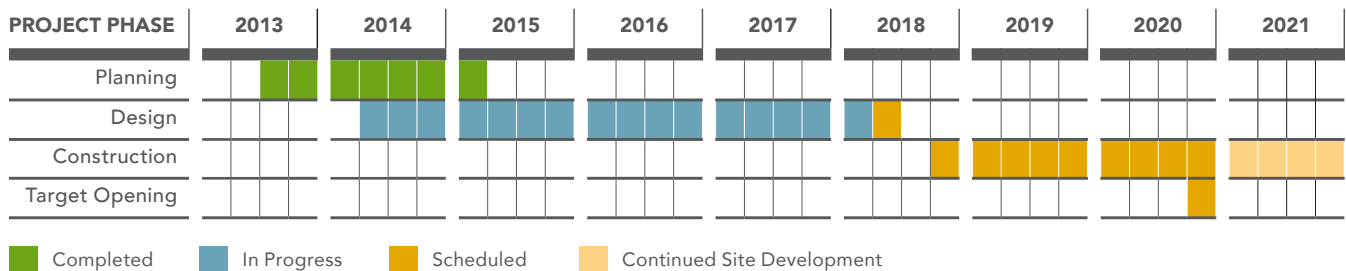

Note: Schedule subject to change.


Bellaire High School – continued

INFORMATION

Indicator	ID	Project/School/Facility	Budget
	C-002	Bellaire High School	\$106,724,000
	Planning and Design Start		Construction Start
	Early/Mid 2014		Late 2018
	Phase		% of Phase
	Design Development		50%
Project Team			
HISD Manager		Dan Bankhead	
Architect		PBK Architects	
Contractor		Turner Construction Company	
Program Manager		Heery International, Inc.	

MILESTONES COMPLETED

Programming/Conceptual Design	✓
Schematic Design Phase	✓
Design Development	
Construction Documents	
Bid & Award	
Construction Start	
Construction Complete	

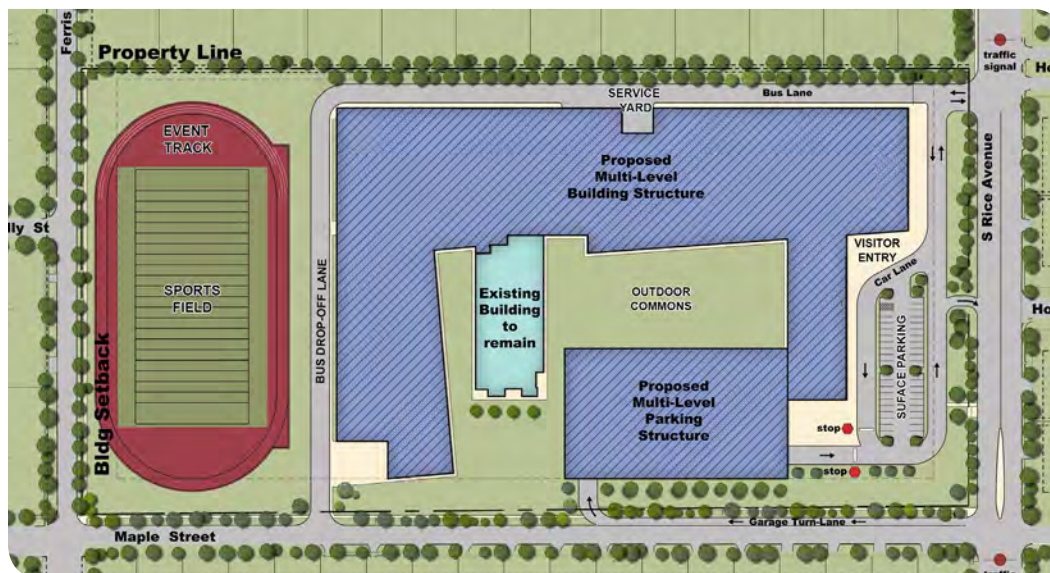



KEY FACTS

Budget
\$46,764,000

Supplemental Funding
\$19,633,657

Trustee
Elizabeth Santos

Location
1101 Quitman St.

NORTHSIDE HIGH SCHOOL

Northside High School was built in 1926 in Houston's Northside. The school features a magnet for Culinary Arts, Hotel Management, and Media. In conjunction with the magnet program, the school also offers career pathways in hospitality and tourism through linked learning, an approach that combines rigorous academics and real-world experiences.

An addition to the school was completed in 1978, and several temporary buildings have been added over the years.


SCOPE OF WORK

New facility preserving the architecturally significant building structure for a school accommodating 1,500 – 1,700 students.

PROJECT STATUS

Exterior envelope, overhead MEP, and drywall are ongoing in the culinary addition.


TARGET SCHEDULE

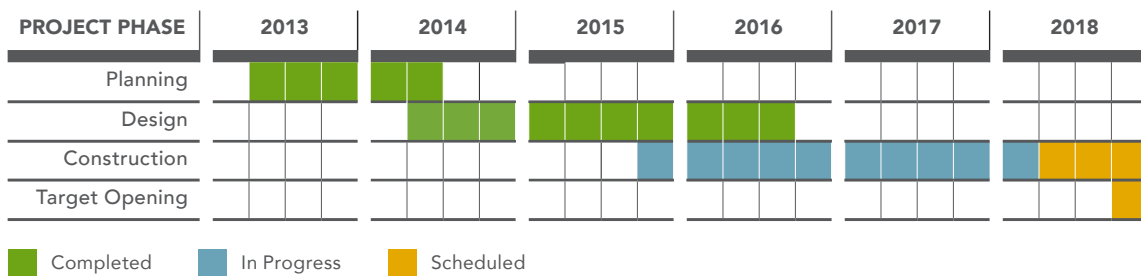

Note: Schedule subject to change.


Northside High School — continued

INFORMATION

Indicator	ID	Project/School/Facility	Budget
	C-003	Northside High School	\$46,764,000
	Planning and Design Start		Construction Start
	Early/Mid 2014		Mid/Late 2015
	Phase		% of Phase
	Construction		50%
Project Team			
HISD Manager		Andreas Peebles	
Architect		Bay-IBI Group Architects	
Contractor		Satterfield & Pontikes	
Program Manager		Heery International, Inc.	

MILESTONES COMPLETED

Programming/Conceptual Design	✓
Schematic Design Phase	✓
Design Development	✓
Construction Documents	✓
Bid & Award	✓
Construction Start	✓
Construction Complete	

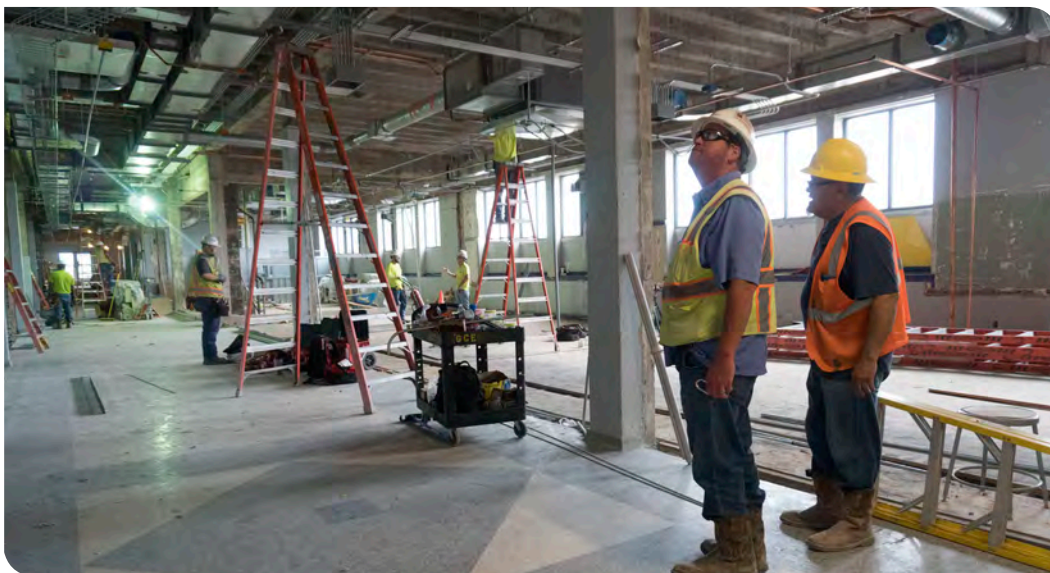



KEY FACTS

Budget
\$59,125,000

Supplemental Funding
\$7,119,857

Trustee
Wanda Adams

Location
14000 Stancliff St.

LAWSON MIDDLE SCHOOL

Lawson Middle School serves students in grades 6 through 8. Located in south Houston, the school offers a performing and visual arts magnet program as part of its academic program.

The main building at Lawson Middle School was constructed in 1966, and over the years the campus has grown to include several small ancillary buildings and 17 temporary classroom buildings.


SCOPE OF WORK

New school for 1,300 – 1,500 students.

PROJECT STATUS

Interior finishes are ongoing.


TARGET SCHEDULE

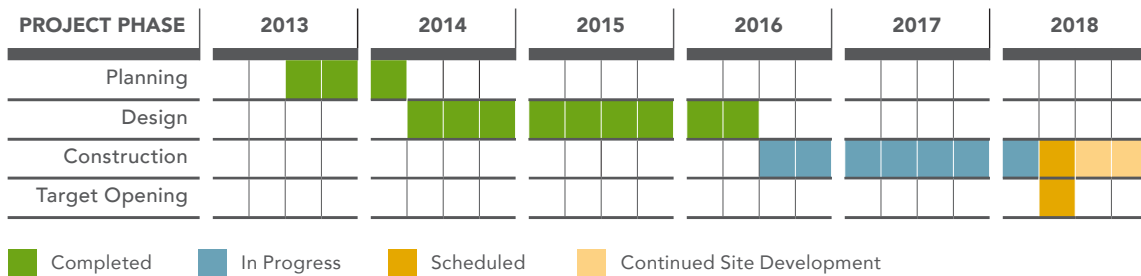

Note: Schedule subject to change.

Lawson Middle School — continued

INFORMATION

Indicator	ID	Project/School/Facility	Budget
	C-075	Lawson Middle School	\$59,125,000
	Planning and Design Start		Construction Start
	Early/Mid 2014		Early/Mid 2016
	Phase		% of Phase
	Construction		82%
Project Team			
HISD Manager		Andreas Peebles	
Architect		Harrison Kornberg	
Contractor		Turner Construction Company	
Program Manager		Rice & Gardner Consultants, Inc.	

MILESTONES COMPLETED

Programming/Conceptual Design	✓
Schematic Design Phase	✓
Design Development	✓
Construction Documents	✓
Bid & Award	✓
Construction Start	✓
Construction Complete	



**KEY FACTS**

Budget
\$10,875,000

Trustee
Diana Dávila

Location
1315 Dumble St.

EASTWOOD ACADEMY


Eastwood Academy is a small college preparatory high school southeast of downtown Houston. All of Eastwood Academy's students take a rigorous college-preparatory curriculum and complete 80 hours of community volunteer work prior to graduation.

SCOPE OF WORK

New facility that will incorporate a new two-story classroom wing for a campus accommodating 500 students.

PROJECT STATUS


Building demo is complete. Library addition work is ongoing.

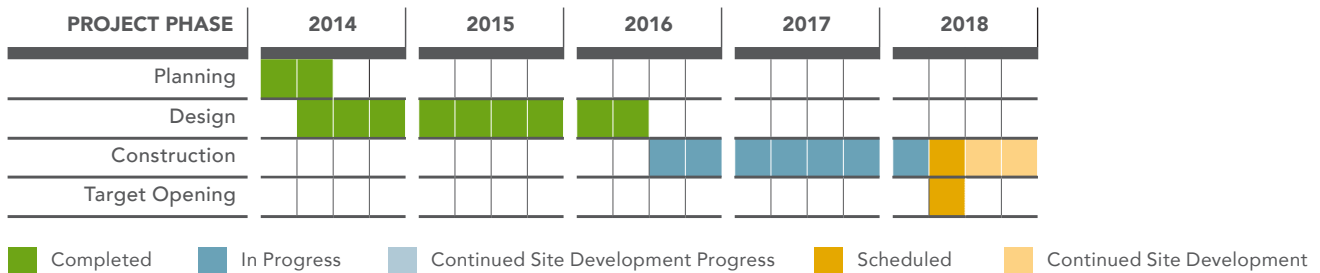TARGET SCHEDULE

Note: Schedule subject to change.

Eastwood Academy – continued

INFORMATION

Indicator	ID	Project/School/Facility	Budget
	C-301	Eastwood Academy	\$10,875,000
	Planning and Design Start		Construction Start
	Early/Mid 2014		Early/Mid 2016
	Phase		% of Phase
	Construction		87%
Project Team			
HISD Manager		Andreas Peebles	
Architect		Prozign	
Contractor		Patriot Contracting, LLC	
Program Manager		Rice & Gardner Consultants, Inc.	

MILESTONES COMPLETED

Programming/Conceptual Design	✓
Schematic Design Phase	✓
Design Development	✓
Construction Documents	✓
Bid & Award	✓
Construction Start	✓
Construction Complete	



**KEY FACTS**

Budget
\$39,998,131

Trustee
Diana Dávila

Location
3505 Coyle St.

HIGH SCHOOL FOR LAW & JUSTICE


The mission of the High School for Law & Justice is to provide students and staff with a safe facility where students receive a strong academic education in conjunction with an in-depth study of law enforcement and criminal justice. The school offers a magnet program in legal studies, law enforcement and fire technology.

SCOPE OF WORK

The school will be rebuilt and funded by real estate sale proceeds.

PROJECT STATUS


Interior finishes are ongoing.

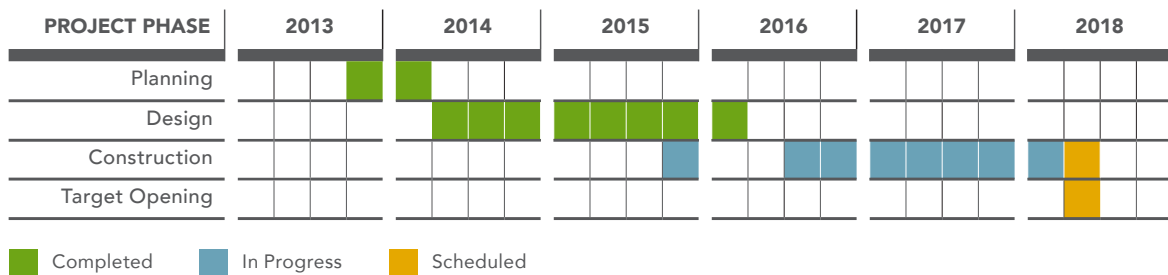TARGET SCHEDULE

Note: Schedule subject to change.

High School for Law & Justice — continued

INFORMATION

Indicator	ID	Project/School/Facility	Budget
	C-034	High School for Law & Justice	\$39,998,131
	Planning and Design Start		Construction Start
	Early/Mid 2014		Early/Mid 2016
	Phase		% of Phase
	Construction		93%
Project Team			
HISD Manager		Andreas Peebles	
Architect		Page DLR	
Contractor		B3Ci	
Program Manager		Rice & Gardner Consultants, Inc.	

MILESTONES COMPLETED

Programming/Conceptual Design	✓
Schematic Design Phase	✓
Design Development	✓
Construction Documents	✓
Bid & Award	✓
Construction Start	✓
Construction Complete	





KEY FACTS

Budget
\$107,974,000

Supplemental Funding
\$14,927,465

Trustee
Anne Sung

Location
3325 Westheimer Road

LAMAR HIGH SCHOOL

Lamar High School offers a Business Administration magnet program and International Baccalaureate, a rigorous academic program that aims to develop knowledgeable, caring, inquisitive students who embrace multiculturalism and diversity and want to make the world a better place.

The campus consists of four main school buildings and several small ancillary buildings. The original main building was constructed in 1937, with additions in 1987.


SCOPE OF WORK

New facility preserving the architecturally significant building structure for a campus accommodating 2,800 – 3,100 students.

PROJECT STATUS

Structural steel is ongoing.


TARGET SCHEDULE

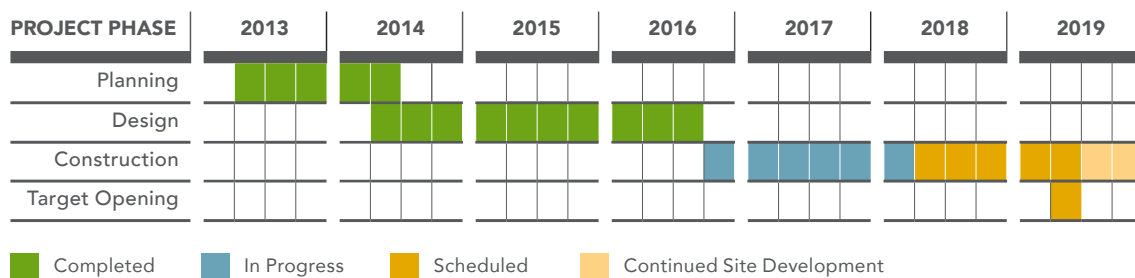

Note: Schedule subject to change.

Lamar High School — continued

INFORMATION

Indicator	ID	Project/School/Facility	Budget
	C-008	Lamar High School	\$107,974,000
	Planning and Design Start		Construction Start
	Early/Mid 2014		Early/Mid 2016
	Phase		% of Phase
	Construction		28%
Project Team			
HISD Manager		Andreas Peebles	
Architect		Perkins + Will	
Contractor		Gilbane Building Company	
Program Manager		Heery International, Inc.	

MILESTONES COMPLETED

Programming/Conceptual Design	✓
Schematic Design Phase	✓
Design Development	✓
Construction Documents	✓
Bid & Award	✓
Construction Start	✓
Construction Complete	



**KEY FACTS**

Budget
\$29,485,000

Supplemental Funding
\$3,525,043

Trustee
Wanda Adams

Location
10626 Atwell Drive

PARKER ELEMENTARY

Parker Elementary in southwest Houston is a music magnet school.


The original campus of Parker Elementary School was constructed in 1959. The campus also includes five temporary classroom buildings.

SCOPE OF WORK

New school for 850 students.

PROJECT STATUS


Punchlist work is underway.

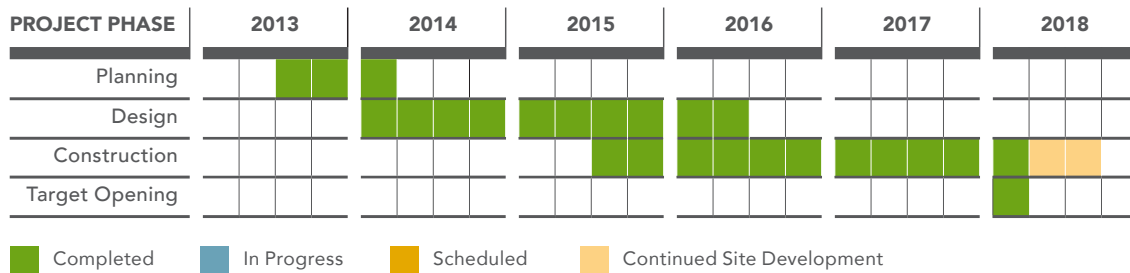TARGET SCHEDULE

Note: Schedule subject to change.

Parker Elementary – continued

INFORMATION

Indicator	ID	Project/School/Facility	Budget
	C-215	Parker Elementary	\$29,485,000
	Planning and Design Start		Construction Start
	Early/Mid 2014		Early/Mid 2016
	Phase		% of Phase
	Construction		99%
Project Team			
HISD Manager		Andreas Peebles	
Architect		Bravé Architecture	
Contractor		Patriot Contracting	
Program Manager		N/A	

MILESTONES COMPLETED

Programming/Conceptual Design	✓
Schematic Design Phase	✓
Design Development	✓
Construction Documents	✓
Bid & Award	✓
Construction Start	✓
Construction Complete	





KEY FACTS

Budget
\$59,481,000

Supplemental Funding
\$5,624,271

Trustee
Jolanda Jones

Location
3703 Sampson St.

YATES HIGH SCHOOL

Yates High School, located in Houston's third ward, is a comprehensive high school that features communications and maritime magnet programs.

The main building at Yates High School was constructed in 1958.


SCOPE OF WORK

New school for 1,300 – 1,500 students.

PROJECT STATUS

Interior finishes are ongoing.


TARGET SCHEDULE

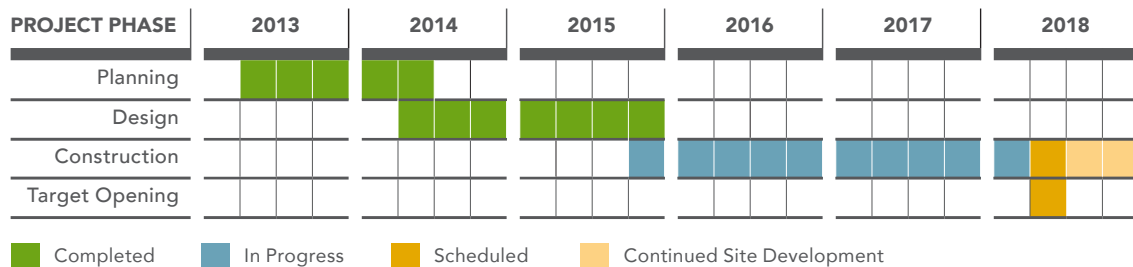

Note: Schedule subject to change.

Yates High School — continued

INFORMATION

Indicator	ID	Project/School/Facility	Budget
	C-020	Yates High School	\$59,481,000
	Planning and Design Start		Construction Start
	Early/Mid 2014		Mid/Late 2015
	Phase		% of Phase
	Construction		80%
Project Team			
HISD Manager		Andreas Peebles	
Architect		Moody Nolan	
Contractor		Turner Construction	
Program Manager		HISD	

MILESTONES COMPLETED

Programming/Conceptual Design	✓
Schematic Design Phase	✓
Design Development	✓
Construction Documents	✓
Bid & Award	✓
Construction Start	✓
Construction Complete	





Sam Houston Math, Science, & Technology Center

Project Update Report — Group 3

**KEY FACTS**

Budget
\$26,632,000

Supplemental Funding
\$4,439,200

Trustee
Holly Maria Flynn Vilaseca

Location
11200 Wood Lodge Drive

ASKEW ELEMENTARY


Askew Elementary School is a pre-K – 5 school with a Vanguard magnet program. The campus includes 22 classrooms in temporary buildings.

SCOPE OF WORK

New school for 850 students.

PROJECT STATUS


Interior finishes are ongoing.

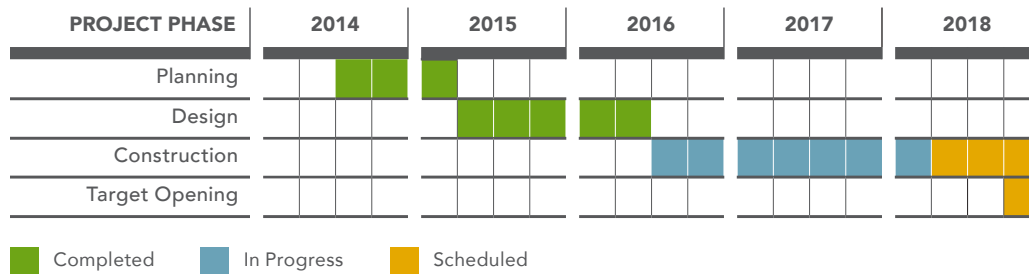TARGET SCHEDULE

Note: Schedule subject to change.

Askew Elementary – continued

INFORMATION

Indicator	ID	Project/School/Facility	Budget
	C-274	Askew Elementary	\$26,632,000
	Planning and Design Start		Construction Start
	Early/Mid 2015		Mid/Late 2016
	Phase		% of Phase
	Construction		84%
Project Team			
HISD Manager		Andreas Peebles	
Architect		Cre8 Architects	
Contractor		Drymalla Construction	
Program Manager		Rice & Gardner Consultants, Inc.	

MILESTONES COMPLETED

Programming/Conceptual Design	✓
Schematic Design Phase	✓
Design Development	✓
Construction Documents	✓
Bid & Award	✓
Construction Start	✓
Construction Complete	





KEY FACTS

Budget
\$36,693,000

Supplemental Funding
\$5,754,548

Trustee
Rhonda Skillern-Jones

Location
5800 Eastex Freeway

BARBARA JORDAN HIGH SCHOOL FOR CAREERS

Barbara Jordan High School for Careers is transitioning from a career magnet school to a regional Career Hub. Located in northeast Houston, the school will provide students from area high schools with real-world experiences in a variety of professions, including Auto/Diesel, Audio/Visual, Construction Management, Cosmetology, Culinary Arts, Marketing/Entrepreneurship, STEM (Electronics), and Welding.

Students will spend half their day at their home school taking required academic classes and the other half at Jordan participating in career curriculum.


SCOPE OF WORK

New school for 600 – 800 students.

PROJECT STATUS

Exterior envelope and overhead MEP are ongoing.


TARGET SCHEDULE

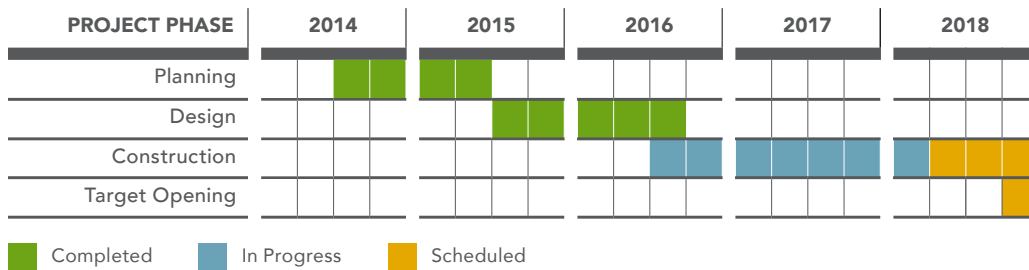

Note: Schedule subject to change.


Jordan High School for Careers — continued

INFORMATION

Indicator	ID	Project/School/Facility	Budget
	C-033	Jordan High School for Careers	\$36,693,000
	Planning and Design Start		Construction Start
	Early/Mid 2015		Mid/Late 2016
	Phase		% of Phase
	Construction		38%
Project Team			
HISD Manager		Dan Bankhead	
Architect		Corgan Associates, Inc. dba Corgan	
Contractor		Cadence McShane	
Program Manager		Heery International, Inc.	

MILESTONES COMPLETED

Programming/Conceptual Design	✓
Schematic Design Phase	✓
Design Development	✓
Construction Documents	✓
Bid & Award	✓
Construction Start	✓
Construction Complete	

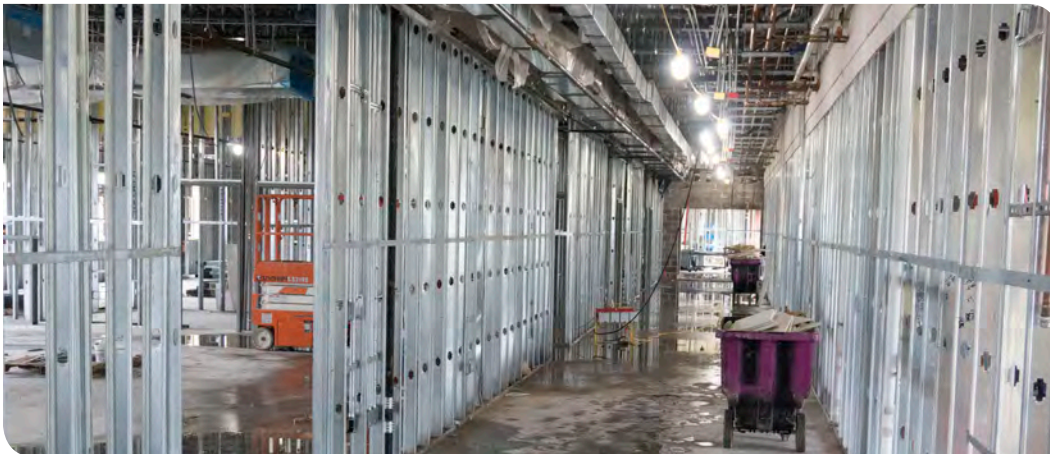

**KEY FACTS**

Budget
\$101,428,000

Supplemental Funding
\$17,175,958

Trustee
Elizabeth Santos

Location
9400 Irvington Blvd.

SAM HOUSTON MATH, SCIENCE AND TECHNOLOGY CENTER

Sam Houston Math, Science and Technology Center High School was built in 1934 in north Houston. The comprehensive high school offers career pathways in Information Technology through linked learning, an approach that combines rigorous academics with real-world experiences.


Over the years, the school has undergone several renovations, most recently the addition of a new science and laboratory building to support the school's mission to prepare students for college and careers.

SCOPE OF WORK

New school that incorporates the new science classroom and laboratory wing to accommodate 2,550 – 2,750 students.

PROJECT STATUS


Exterior envelope and overhead MEP are ongoing.

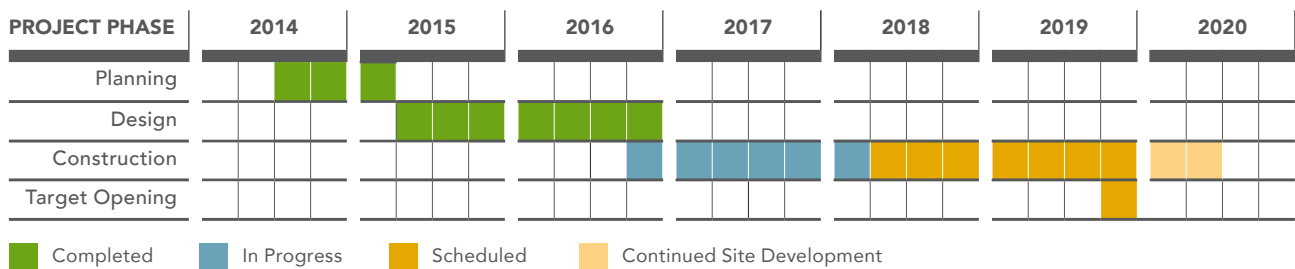TARGET SCHEDULE

Note: Schedule subject to change.


Sam Houston Math, Science and Technology Center — continued

INFORMATION

Indicator	ID	Project/School/Facility	Budget
	C-310	Sam Houston Math, Science and Technology Center High School	\$101,428,000
	Planning and Design Start		Construction Start
	Early/Mid 2015		Mid/Late 2016
	Phase		% of Phase
	Construction		50%
Project Team			
HISD Manager		Dan Bankhead	
Architect		Stantec Architecture, Inc.	
Contractor		Satterfield & Pontikes	
Program Manager		HISD	

MILESTONES COMPLETED

Programming/Conceptual Design	✓
Schematic Design Phase	✓
Design Development	✓
Construction Documents	✓
Bid & Award	✓
Construction Start	✓
Construction Complete	

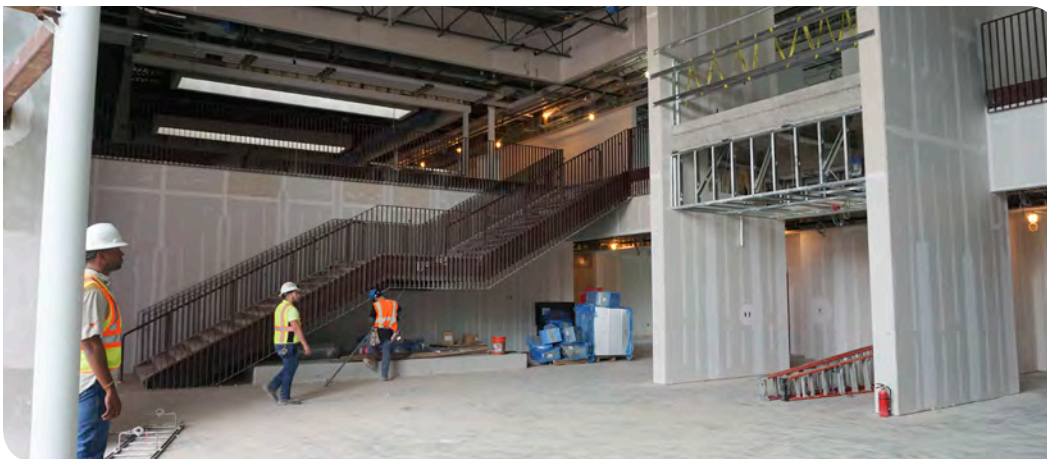

**KEY FACTS**

Budget
\$27,159,000

Supplemental Funding
\$4,009,189

Trustee
Jolanda Jones

Location
1906 Cleburne St.

YOUNG WOMEN'S COLLEGE PREPARATORY ACADEMY (YWCPA)

YWCPA opened in the fall of 2011 in midtown to allow young women to experience a small and inclusive environment enriched with a rigorous college preparatory curriculum.


Serving students in grades 6 – 12, the campus places a strong emphasis on Advanced Placement and STEM (Science, Technology, Engineering and Math) courses.

SCOPE OF WORK

Partial replacement and general renovations accommodating 900 - 1,000 students.

PROJECT STATUS


Overhead MEP and interior drywall framing are ongoing.

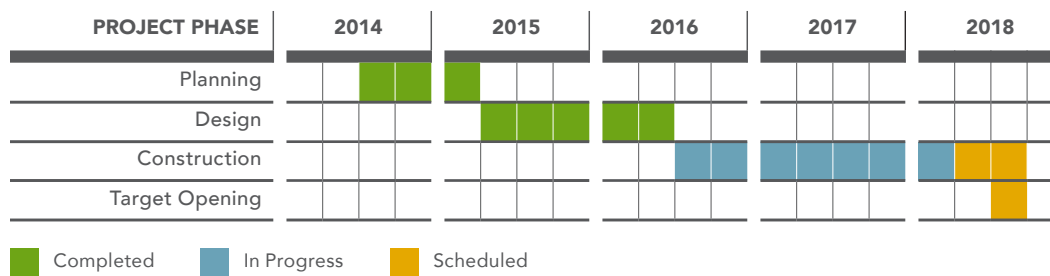TARGET SCHEDULE

Note: Schedule subject to change.

Young Women's College Preparatory Academy – continued


INFORMATION

Indicator	ID	Project/School/Facility	Budget
	C-029	Young Women’s College Preparatory Academy	\$27,159,000
	Planning and Design Start		Construction Start
	Early/Mid 2015		Mid/Late 2016
	Phase		% of Phase
	Construction		88%
Project Team			
HISD Manager		Andreas Peebles	
Architect		Natex Corporation	
Contractor		Satterfield & Pontikes	
Program Manager		Heery International, Inc.	

MILESTONES COMPLETED

Programming/Conceptual Design	✓
Schematic Design Phase	✓
Design Development	✓
Construction Documents	✓
Bid & Award	✓
Construction Start	✓
Construction Complete	



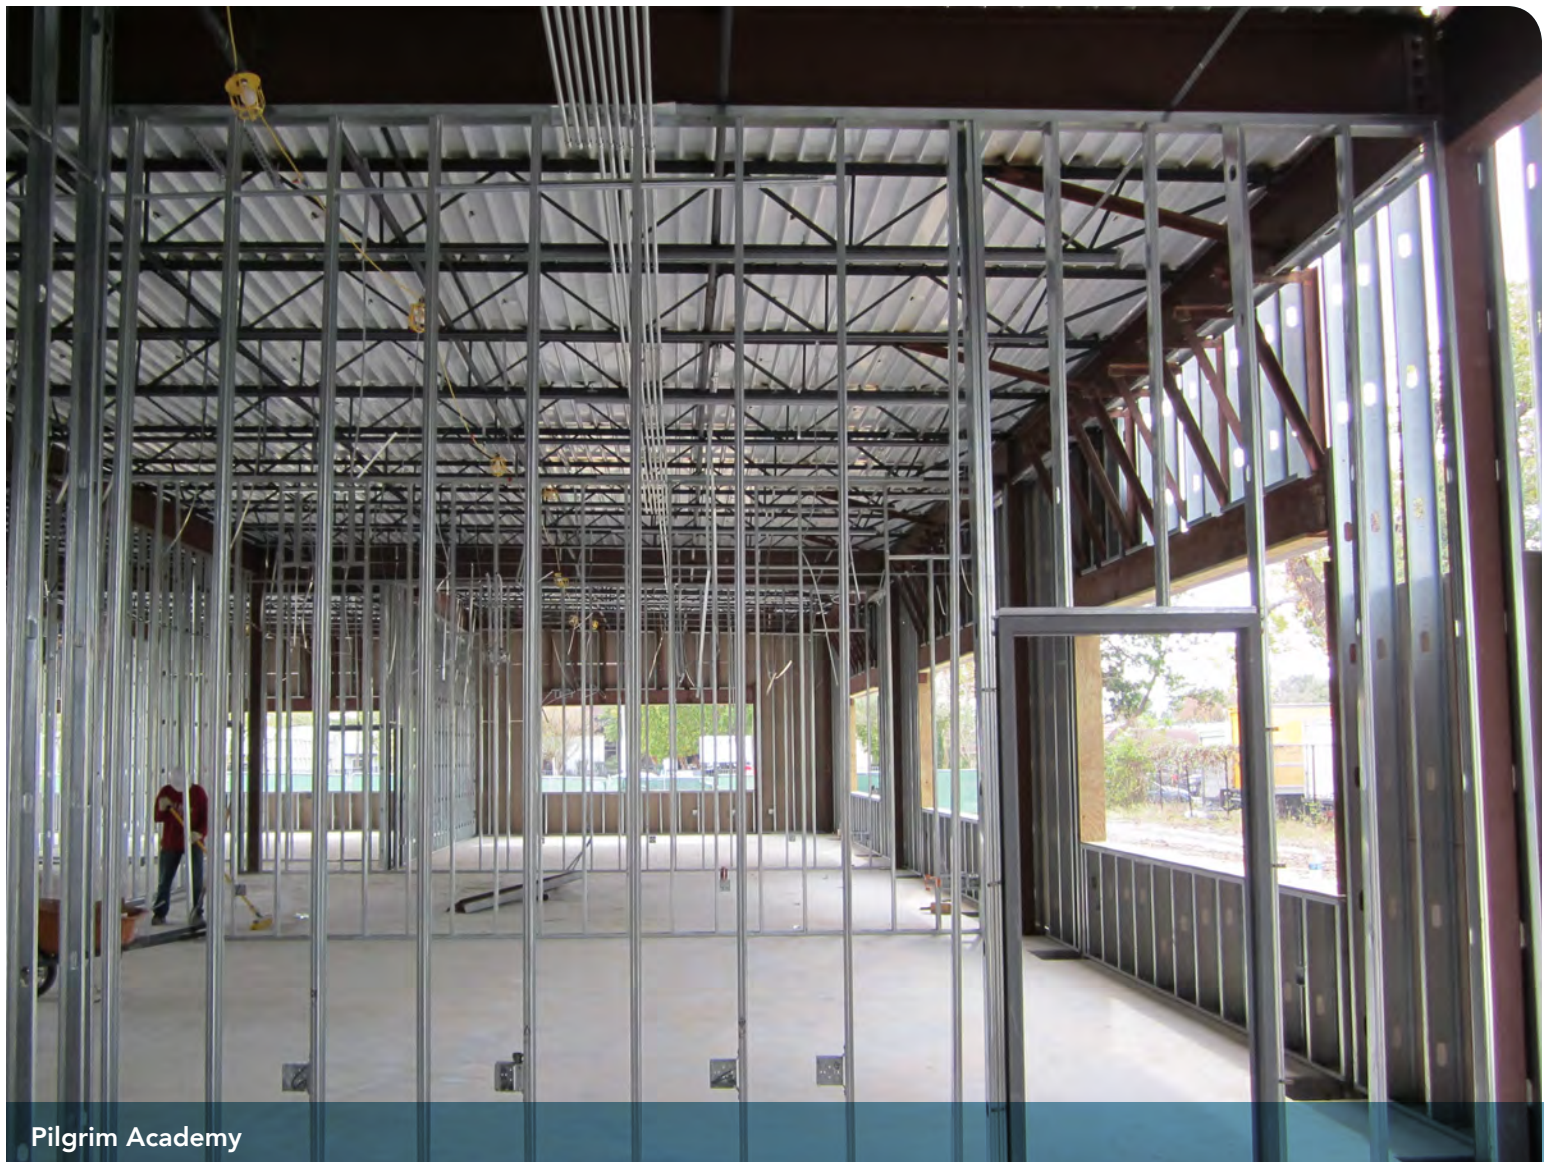

Pilgrim Academy

Project Update Report — Group 4



KEY FACTS

Budget
\$68,429,000

Supplemental Funding
\$11,161,679

Trustee
Diana Dávila

Location
1700 Dumble St.

AUSTIN HIGH SCHOOL

Stephen F. Austin High School is located in Houston's East End. The comprehensive high school features career magnet programs in maritime and the teaching professions.

The school's main building was built in 1937.


SCOPE OF WORK

New facility preserving the architecturally significant building structure for a campus accommodating 1,800 – 2,000 students.

PROJECT STATUS

Abatement is ongoing.


TARGET SCHEDULE

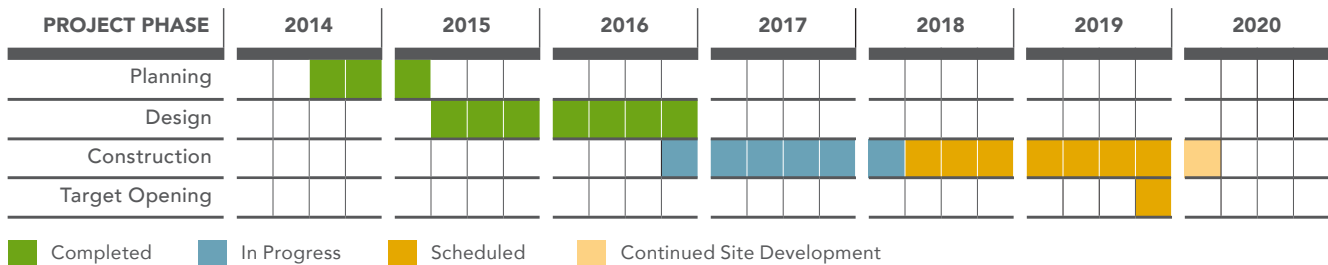

Note: Schedule subject to change.

Austin High School — continued

INFORMATION

Indicator	ID	Project/School/Facility	Budget
	C-001	Austin High School	\$68,429,000
	Planning and Design Start		Construction Start
	Late 2015/Early 2016		Late 2016
	Phase		% of Phase
	Construction		22%
Project Team			
HISD Manager		Dan Bankhead	
Architect		ERO Architects	
Contractor		Webber, LLC	
Program Manager		Heery International, Inc.	

MILESTONES COMPLETED

Programming/Conceptual Design	✓
Schematic Design Phase	✓
Design Development	✓
Construction Documents	✓
Bid & Award	✓
Construction Start	✓
Construction Complete	





KEY FACTS

Budget
\$26,678,000

Supplemental Funding
\$4,195,956

Trustee
Elizabeth Santos

Location
901 Sue Barnett Drive

GARDEN OAKS MONTESSORI

Garden Oaks Montessori is located in Houston's Garden Oaks neighborhood, north of Interstate 610. The school features a Montessori magnet with an emphasis on environmental sciences.

The original school was built in 1979 with an addition built in 1981. The school was last renovated in 2005. Currently, the campus relies on eight temporary buildings, as well as a temporary restroom.


SCOPE OF WORK

New addition and general renovations of the existing facilities to accommodate 750 – 900 students.

PROJECT STATUS

Phase 2 worked was completed over Spring Break. Phase 3 work has commenced.


TARGET SCHEDULE

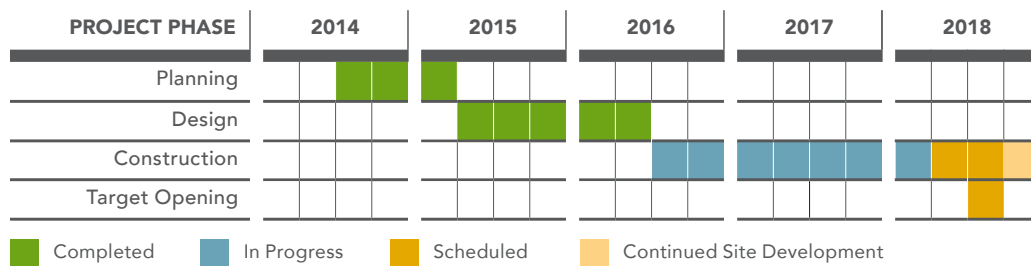

Note: Schedule subject to change.

Garden Oaks Montessori — continued

INFORMATION

Indicator	ID	Project/School/Facility	Budget
	C-157	Garden Oaks Montessori	\$26,678,000
	Planning and Design Start		Construction Start
	Late 2015/Early 2016		Mid/Late 2016
	Phase		% of Phase
	Construction		80%
Project Team			
HISD Manager		Andreas Peebles	
Architect		Hill Swart Chu Architects, LLC	
Contractor		B3CI	
Program Manager		Rice & Gardner Consultants, Inc.	

MILESTONES COMPLETED

Programming/Conceptual Design	✓
Schematic Design Phase	✓
Design Development	✓
Construction Documents	✓
Bid & Award	✓
Construction Start	✓
Construction Complete	



**KEY FACTS**

Budget
\$1,125,000

Supplemental Funding
\$296,011

Trustee
Jolanda Jones

Location
7414 St. Lo Road

JONES FUTURES ACADEMY

Jones Futures Academy was constructed in 1956 in southeast Houston. The campus was repurposed into a speciality school in 2014. It now is home to Futures Academy programs in Allied Health and Construction Technology.

SCOPE OF WORK

Renovations to existing school facilities.

PROJECT STATUS

Complete.

TARGET SCHEDULE


PROJECT PHASE	2014	2015	2016
Planning			
Design			
Construction			
Target Opening			

■ Completed
 ■ In Progress
 ■ Scheduled
 ■ Continued Site Development

Note: Schedule subject to change.

Jones Futures Academy — continued

INFORMATION

Indicator	ID	Project/School/Facility	Budget
	C-006	Jones Futures Academy	\$1,125,000
	Planning and Design Start		Construction Start
	Late 2015/Early 2016		Mid 2016
	Phase		% of Phase
	Closeout		100%
Project Team			
HISD Manager		Dan Bankhead	
Architect		N/A	
Contractor		P2MG/ Aries	
Program Manager		N/A	

MILESTONES COMPLETED

Programming/Conceptual Design	✓
Schematic Design Phase	✓
Design Development	✓
Construction Documents	✓
Bid & Award	✓
Construction Start	✓
Construction Complete	✓



**KEY FACTS**

Budget
\$17,000,000

Supplemental Funding
\$2,053,729

Trustee
Rhonda Skillern-Jones

Location
6900 Wileyvale Road

KASHMERE HIGH SCHOOL

Kashmere High School is located on Houston's northeast side. It is home to the Futures Academy of Computer Engineering Technology at Kashmere. It also offers a Chemical and Process Technology Institute STEM (Science, Technology, Engineering and Math) magnet, as well as a performing and visual arts magnet.

The school was constructed in 1969 and was last renovated in 2000.

SCOPE OF WORK

Renovations to existing school facilities and site improvements.

PROJECT STATUS

Closeout is ongoing.

TARGET SCHEDULE


PROJECT PHASE	2014	2015	2016	2017
Planning	<div></div> <div></div> <div></div>	<div></div> <div></div> <div></div>	<div></div> <div></div> <div></div>	<div></div> <div></div> <div></div>
Design	<div></div> <div></div> <div></div>	<div></div> <div></div> <div></div> <div></div>	<div></div> <div></div> <div></div>	<div></div> <div></div> <div></div>
Construction	<div></div> <div></div> <div></div>	<div></div> <div></div> <div></div> <div></div>	<div></div> <div></div> <div></div> <div></div>	<div></div> <div></div> <div></div> <div></div>
Target Opening	<div></div> <div></div> <div></div>	<div></div> <div></div> <div></div>	<div></div> <div></div> <div></div>	<div></div> <div></div> <div></div>

Completed In Progress Scheduled

Note: Schedule subject to change.

Kashmere High School — continued

INFORMATION

Indicator	ID	Project/School/Facility	Budget
	C-007	Kashmere High School	\$17,000,000
	Planning and Design Start		Construction Start
	Late 2015/Early 2016		Early/Mid 2016
	Phase		% of Phase
	Closeout		5%
Project Team			
HISD Manager		Andreas Peebles	
Architect		Natex Corporation	
Contractor		DT Construction	
Program Manager		HISD	

MILESTONES COMPLETED

Programming/Conceptual Design	✓
Schematic Design Phase	✓
Design Development	✓
Construction Documents	✓
Bid & Award	✓
Construction Start	✓
Construction Complete	✓





KEY FACTS

Budget
\$82,736,000

Supplemental Funding
\$11,193,118

Trustee
Wanda Adams

Location
13719 White Heather Drive

MADISON HIGH SCHOOL

James Madison High School is a comprehensive high school offering career pathways in environmental science professions and robotics through linked learning, an approach that combines rigorous academics with real-world experiences.

The campus, located in southwest Houston, consists of five school buildings and 21 temporary buildings.


SCOPE OF WORK

New school for 1,900 – 2,100 students that will incorporate recent science and classroom building renovations.

PROJECT STATUS

Exterior envelope, overhead MEP, and roof installation are ongoing.


TARGET SCHEDULE

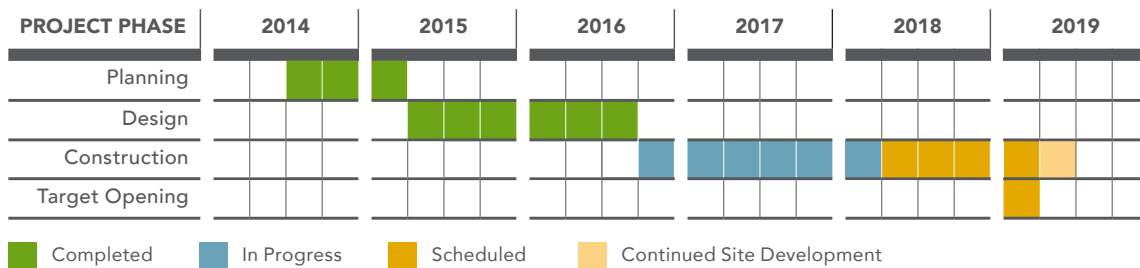

Note: Schedule subject to change.


Madison High School — continued

INFORMATION

Indicator	ID	Project/School/Facility	Budget
	C-010	Madison High School	\$82,736,000
	Planning and Design Start		Construction Start
	Late 2015/Early 2016		Late 2016
	Phase		% of Phase
	Construction		55%
Project Team			
HISD Manager		Andreas Peebles	
Architect		Morris Architects, Inc.	
Contractor		Satterfield and Pontikes Construction, Inc.	
Program Manager		Heery International, Inc.	

MILESTONES COMPLETED

Programming/Conceptual Design	✓
Schematic Design Phase	✓
Design Development	✓
Construction Documents	✓
Bid & Award	✓
Construction Start	✓
Construction Complete	

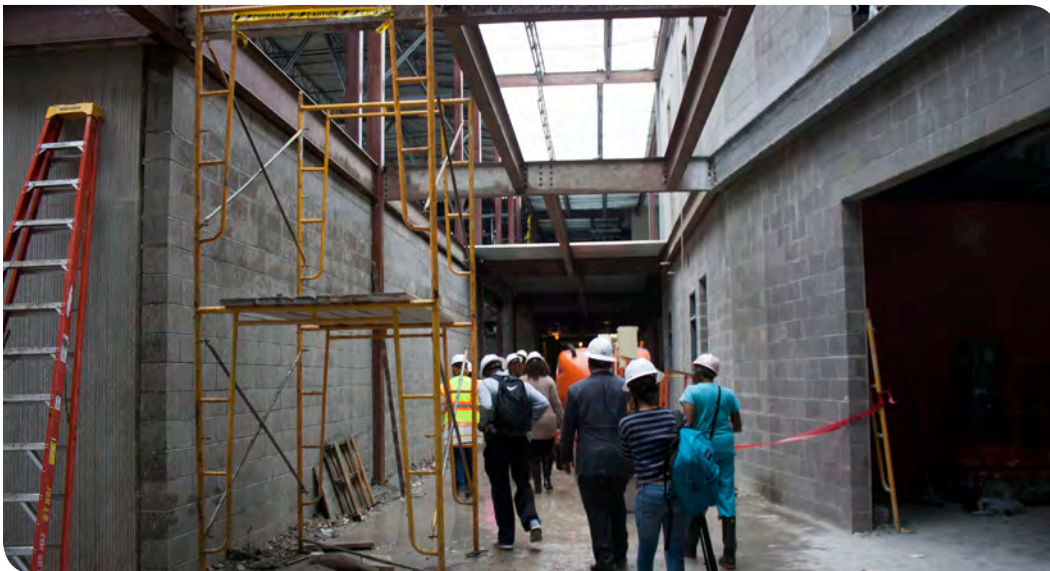



KEY FACTS

Budget
\$7,989,000

Supplemental Funding
\$960,481

Trustee
Anne Sung

Location
6302 Skyline Drive

PILGRIM ACADEMY

Pilgrim Academy was built in 2007 as a neighborhood elementary school in the Galleria area. It that has since expanded to include a middle school program.

The school is currently using temporary classrooms for middle school students.


SCOPE OF WORK

New addition for a campus accommodating 750 – 900 students.

PROJECT STATUS

Exterior envelope, overhead MEP, and drywall framing are ongoing.


TARGET SCHEDULE

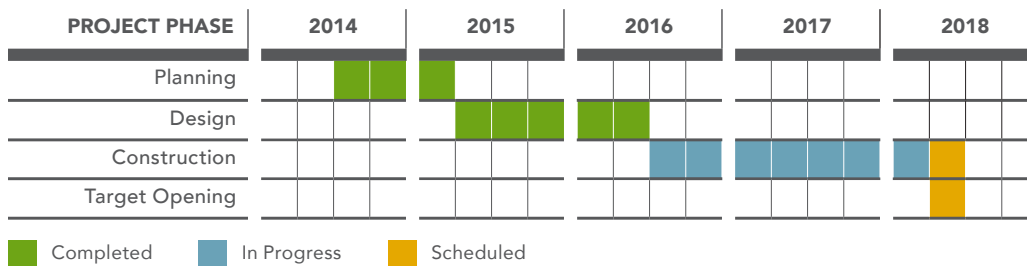

Note: Schedule subject to change.

Pilgrim Academy – continued

INFORMATION

Indicator	ID	Project/School/Facility		Budget
	C-218	Pilgrim Academy		\$7,989,000
	Planning and Design Start		Construction Start	
	Late 2015/Early 2016		Mid 2016	
	Phase		% of Phase	
	Construction		80%	
Project Team				
HISD Manager		Andreas Peebles		
Architect		RDC Architects, PLLC		
Contractor		DT Construction		
Program Manager		Heery International, Inc.		

MILESTONES COMPLETED

Programming/Conceptual Design	✓
Schematic Design Phase	✓
Design Development	✓
Construction Documents	✓
Bid & Award	✓
Construction Start	✓
Construction Complete	



**KEY FACTS**

Budget
\$12,566,000

Supplemental Funding
\$2,077,625

Trustee
Elizabeth Santos

Location
4141 Costa Rica Road

SCARBOROUGH HIGH SCHOOL

Scarborough High School is a comprehensive high school located in northwest Houston. The school is home to the Futures Academy for Network & Computer Administration at Scarborough, and also offers career pathways in retail management through linked learning, an approach that combines rigorous academics with real-world experiences.

The original buildings at the school were constructed in 1966.

SCOPE OF WORK

Renovations to existing school facilities and site improvements.

PROJECT STATUS

Punchlist work is wrapping up.

TARGET SCHEDULE


PROJECT PHASE	2014	2015	2016	2017	2018
Planning	<div></div> <div></div> <div></div>	<div></div> <div></div> <div></div>	<div></div> <div></div> <div></div>	<div></div> <div></div> <div></div>	<div></div> <div></div> <div></div>
Design	<div></div> <div></div> <div></div>	<div></div> <div></div> <div></div> <div></div>	<div></div> <div></div> <div></div>	<div></div> <div></div> <div></div>	<div></div> <div></div> <div></div>
Construction	<div></div> <div></div> <div></div>	<div></div> <div></div> <div></div> <div></div>	<div></div> <div></div> <div></div>	<div></div> <div></div> <div></div> <div></div>	<div></div> <div></div> <div></div>
Target Opening	<div></div> <div></div> <div></div>	<div></div> <div></div> <div></div>	<div></div> <div></div> <div></div>	<div></div> <div></div> <div></div>	<div></div> <div></div> <div></div>

■ Completed
 ■ In Progress
 ■ Scheduled

Note: Schedule subject to change.

Scarborough High School – continued

INFORMATION

Indicator	ID	Project/School/Facility		Budget
	C-024	Scarborough High School		\$12,566,000
	Planning and Design Start		Construction Start	
	Late 2015/Early 2016		Mid/Late 2016	
	Phase		% of Phase	
	Construction		99%	
Project Team				
HISD Manager		Andreas Peebles		
Architect		Randall - Porterfield Architects, Inc.		
Contractor		DT Construction		
Program Manager		HISD		

MILESTONES COMPLETED

Programming/Conceptual Design	✓
Schematic Design Phase	✓
Design Development	✓
Construction Documents	✓
Bid & Award	✓
Construction Start	✓
Construction Complete	



**KEY FACTS**

Budget
\$6,125,000

Supplemental Funding
\$808,379

Trustee
Holly Maria Flynn Vilaseca

Location
8330 Triola Lane

SHARPSTOWN INTERNATIONAL SCHOOL

Sharpstown International School was created through the 2011-2012 consolidation of Sharpstown Middle School and the International High School at Sharpstown, a partnership between the district and the Asia Society's International Studies Schools Network.

Located on the city's southwest side, the school offers an international studies magnet program, and was the first in HISD to offer a magnet program for students in grades 6-12.

SCOPE OF WORK

Renovations to existing school facilities and site improvements.

PROJECT STATUS

Project closeout ongoing.

TARGET SCHEDULE


PROJECT PHASE	2014	2015	2016	2017
Planning	<div></div> <div></div> <div></div>	<div></div> <div></div> <div></div>	<div></div> <div></div> <div></div>	<div></div> <div></div> <div></div>
Design	<div></div> <div></div> <div></div>	<div></div> <div></div> <div></div> <div></div>	<div></div> <div></div> <div></div>	<div></div> <div></div> <div></div>
Construction	<div></div> <div></div> <div></div>	<div></div> <div></div> <div></div> <div></div>	<div></div> <div></div> <div></div> <div></div>	<div></div> <div></div> <div></div> <div></div>
Target Opening	<div></div> <div></div> <div></div>	<div></div> <div></div> <div></div>	<div></div> <div></div> <div></div>	<div></div> <div></div> <div></div>

Completed In Progress Scheduled

Note: Schedule subject to change.

Sharpstown International — continued

INFORMATION

Indicator	ID	Project/School/Facility	Budget
	C-081	Sharpstown International	\$6,125,000
	Planning and Design Start		Construction Start
	Late 2015/Early 2016		Early/Mid 2016
	Phase		% of Phase
	Closeout		90%
Project Team			
HISD Manager		Andreas Peebles	
Architect		Autoarch Architects, Inc.	
Contractor		DT Construction	
Program Manager		Rice & Gardner Consultants, Inc.	

MILESTONES COMPLETED

Programming/Conceptual Design	✓
Schematic Design Phase	✓
Design Development	✓
Construction Documents	✓
Bid & Award	✓
Construction Start	✓
Construction Complete	✓



**KEY FACTS**

Budget
\$40,006,000

Supplemental Funding
\$6,257,598

Trustee
Wanda Adams

Location
11911 Chimney Rock Road

WESTBURY HIGH SCHOOL

Westbury High School consists of five main school buildings. The original campus was constructed in 1961, and additions to the main school building were constructed in 1983, 1995, and 2004.


Westbury is a comprehensive high school with a performing and visual arts magnet program, and career pathways in public safety through linked learning, an approach that combines rigorous academics with real-world experiences.

SCOPE OF WORK

Partial replacement and general renovations to accommodate 2,300 – 2,500 students.

PROJECT STATUS


Phase 2 work was completed over spring break. Phase 3 work has commenced.

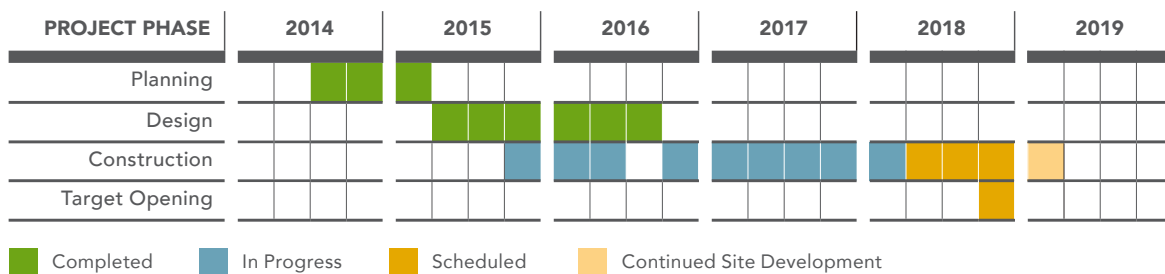TARGET SCHEDULE

Note: Schedule subject to change.

Westbury High School — continued

INFORMATION

Indicator	ID	Project/School/Facility	Budget
	C-017	Westbury High School	\$40,006,000
	Planning and Design Start		Construction Start
	Late 2015/Early 2016		Late 2016
	Phase		% of Phase
	Construction		92%
Project Team			
HISD Manager		Andreas Peebles	
Architect		Joiner Partnership, Inc.	
Contractor		Satterfield & Pontikes	
Program Manager		Rice & Gardner Consultants, Inc.	

MILESTONES COMPLETED

Programming/Conceptual Design	✓
Schematic Design Phase	✓
Design Development	✓
Construction Documents	✓
Bid & Award	✓
Construction Start	✓
Construction Complete	



**KEY FACTS**

Budget
\$35,603,000

Supplemental Funding
\$3,621,734

Trustee
Diana Dávila

Location
900 West Gray St.

WHARTON DUAL LANGUAGE ACADEMY

Wharton Dual Language Academy features a Spanish dual language magnet program, as well as an International Baccalaureate Primary Years Programme, which encourages younger students to become inquisitive, lifelong learners. It serves students in pre-K through 8th grade.


Located in the Montrose area, Wharton was originally built as a small elementary school in 1929. It currently has seven temporary classroom buildings.

SCOPE OF WORK

New addition and general renovations of existing facilities to accommodate 750 – 900 students.

PROJECT STATUS

Exterior envelope, overhead MEP, and drywall framing are ongoing.

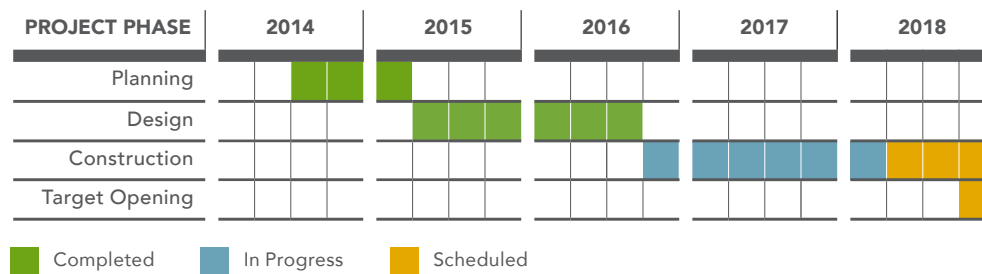TARGET SCHEDULE

Note: Schedule subject to change.

Wharton Dual Language Academy – continued

INFORMATION

Indicator	ID	Project/School/Facility	Budget
	C-256	Wharton Dual Language Academy	\$35,603,000
	Planning and Design Start		Construction Start
	Late 2015/Early 2016		Late 2016
	Phase		% of Phase
	Construction		60%
Project Team			
HISD Manager		Dan Bankhead	
Architect		H. Munoz & Company, Inc.	
Contractor		Division One	
Program Manager		Heery International, Inc.	

MILESTONES COMPLETED

Programming/Conceptual Design	✓
Schematic Design Phase	✓
Design Development	✓
Construction Documents	✓
Bid & Award	✓
Construction Start	✓
Construction Complete	



**KEY FACTS**

Budget
\$18,914,000

Supplemental Funding
\$5,808,033

Trustee
Anne Sung

Location
2100 Yupon St.

WILSON MONTESSORI

Wilson Montessori, located in the Montrose area, was constructed as a small elementary school in 1924 and renovated in 2004. In February 2005, HISD and the Friends of Montessori non-profit organization joined together to create HISD's first all-Montessori school.


The Montessori magnet serves students in grades K – 8. It has six temporary classroom buildings.

SCOPE OF WORK

New addition and general renovations to accommodate 750 – 900 students.

PROJECT STATUS


Phase 1 work was completed over spring break. Phase 2 work has commenced.

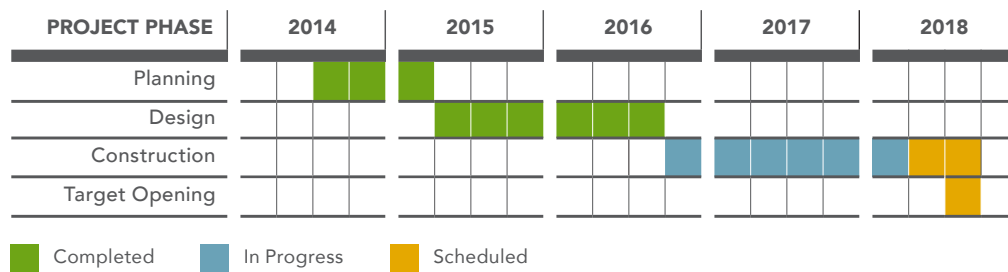TARGET SCHEDULE

Note: Schedule subject to change.


Wilson Montessori — continued


INFORMATION

Indicator	ID	Project/School/Facility	Budget
	C-259	Wilson Montessori	\$18,914,000
	Planning and Design Start		Construction Start
	Late 2015/Early 2016		Late 2016
	Phase		% of Phase
	Construction		92%
Project Team			
HISD Manager		Andreas Peebles	
Architect		Smith & Company Architects, Inc.	
Contractor		Drymalla Construction Co.	
Program Manager		Rice & Gardner Consultants, Inc.	

MILESTONES COMPLETED

Programming/Conceptual Design	✓
Schematic Design Phase	✓
Design Development	✓
Construction Documents	✓
Bid & Award	✓
Construction Start	✓
Construction Complete	

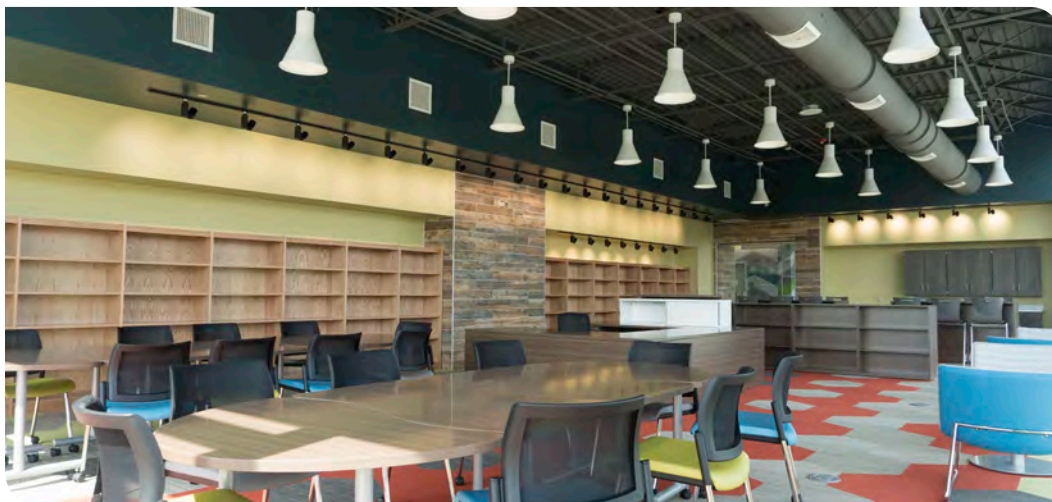

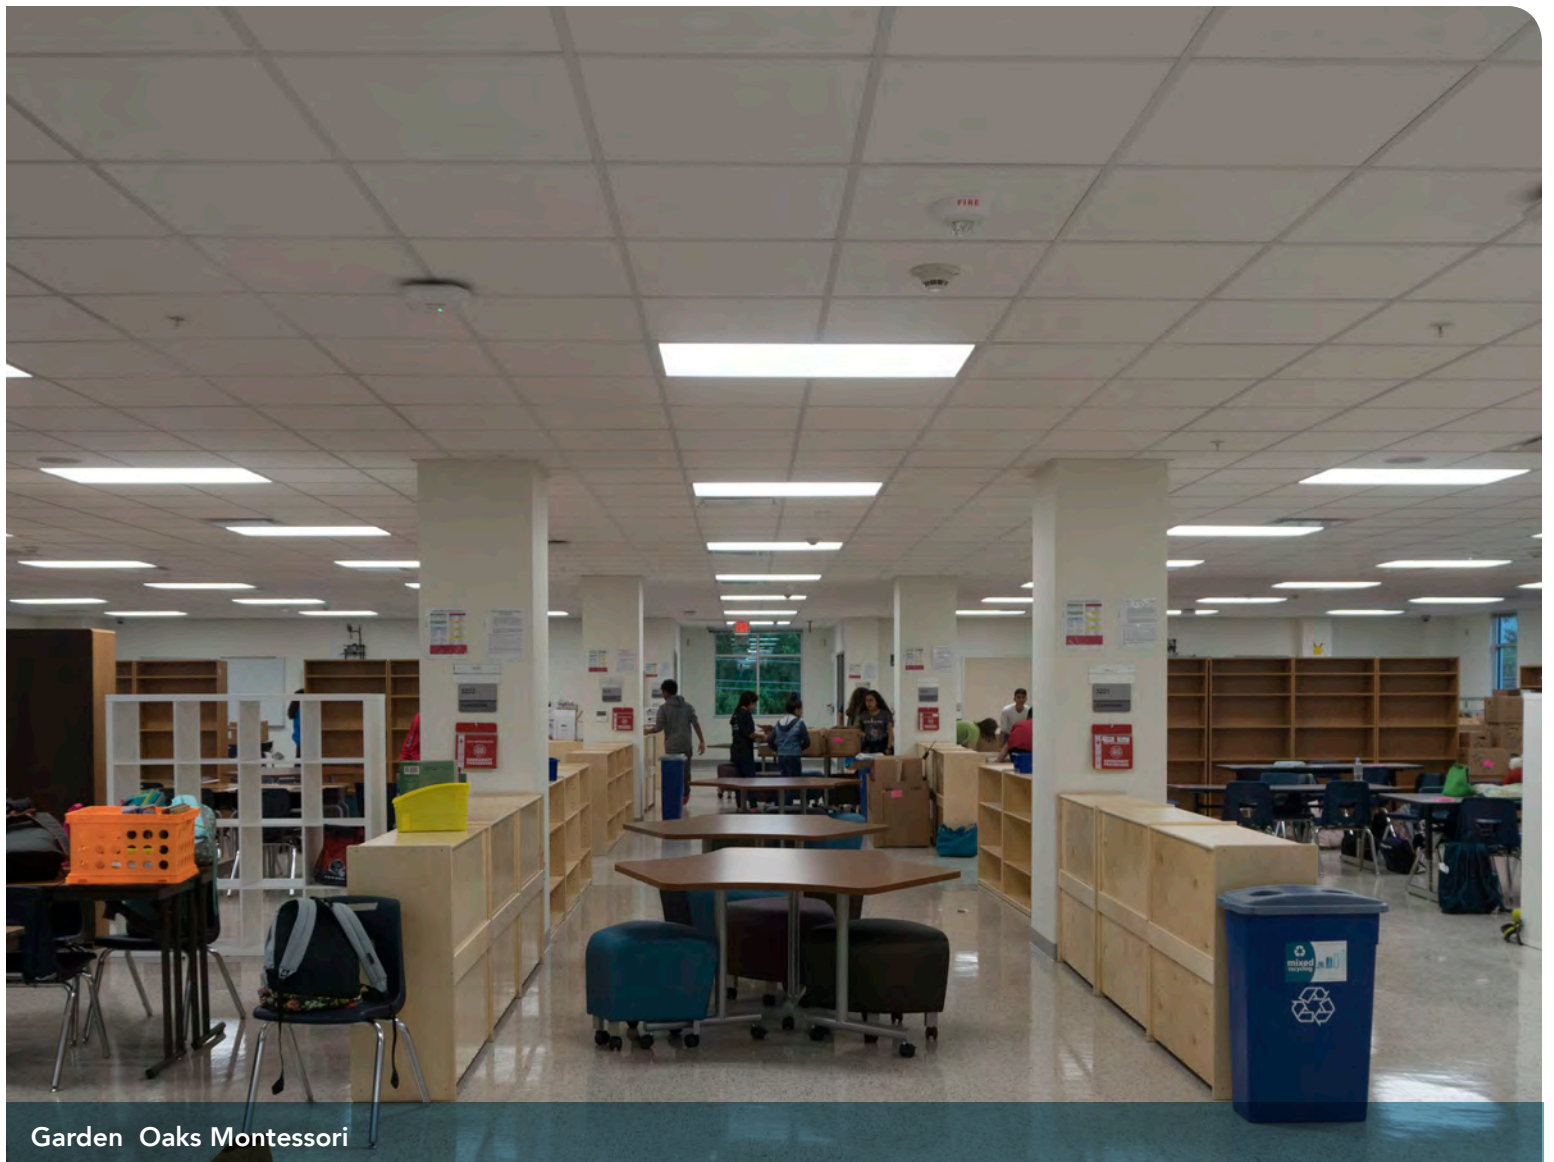

Garden Oaks Montessori

Districtwide Projects

DISTRICTWIDE PROJECTS

2012 Project Update Report

TECHNOLOGY UPGRADES AT ALL HISD SCHOOLS: \$100 MILLION

The 2012 Bond allocated funding for network improvements and wireless expansion.

Project Status

The 2012 Bond Program allocated \$100 million in funding for technology upgrades, network improvements, and wireless expansion at schools across the district. All technology work covered by this portion of the bond has now been completed.

The scope of the work included the addition of wireless access points, cabling, and other infrastructure equipment, such as network switches and Voice over Internet Protocol (VoIP). These improvements allow for the expansion of digital instruction, as well as safety and security improvements like telephones in classrooms.

For more information, please visit HoustonISD.org/voip.

MIDDLE SCHOOL RESTROOM RENOVATIONS: \$35 MILLION

Renovations of the restrooms in middle schools across HISD.

Project Status

All projects are complete, and there are no funds remaining for middle school restrooms. The projects are now in closeout.

SAFETY AND SECURITY IMPROVEMENTS: \$17.3 MILLION

Improvements include fencing, security cameras, and access control.

Project Status

All projects have been completed, and there are no funds remaining for safety and security improvements. The following projects have been completed with 2012 Safety & Security funds:

- Controlled Access - 285 campuses completed, 4 access control upgrades
- Security Camera upgrades - 6 CCTV upgrades
- Fire Alarm upgrades - 1 fire alarm upgrade

LAND ACQUISITION: \$55.8 MILLION

Funds to supplement significant site/parking constraints.

Project Status

With all purchases complete under the 2012 bond program, the Real Estate department is maintaining and renewing current lease agreements as needed, assisting project managers with land planning issues, and searching for possible sites for future development. The department continues to supplement and maintain the centralized database of key documents for all HISD properties.

**KEY FACTS**

Budget
\$4,804,255

Location
6800 Fairway Drive

BARNETT ATHLETIC COMPLEX

Barnett Athletic Complex is a multipurpose facility, including an 8,000-seat football stadium, baseball fields, and fieldhouse.


SCOPE OF WORK

Regional field house(s) and athletic facility improvements.

PROJECT STATUS

Complete.

Information

Indicator	ID	Project/School/Facility		Budget
	C-661	Barnett Fieldhouse		\$4,804,255
	Target Construction Start		Target Construction Completion	
	4th Qtr. 2014		2nd Qtr. 2016	
	Phase		% of Phase	
	Closeout		100%	
Project Team				
Manager		Andreas Peebles		
Architect		PBK Architects		
Contractor		Prime Contractors		
CMPA		N/A		

**KEY FACTS**

Budget
\$4,591,811

Location
13755 South Main St.

BUTLER ATHLETIC COMPLEX

Butler Athletic Complex is a multipurpose facility, including an 8,000-seat football stadium, baseball fields, and fieldhouse.


SCOPE OF WORK

Regional field house(s) and athletic facility improvements.

PROJECT STATUS

Complete.

INFORMATION

Indicator	ID	Project/School/Facility		Budget
	C-662	Butler Fieldhouse		\$4,591,811
	Target Construction Start		Target Construction Completion	
	4th Qtr. 2014		1st Qtr. 2016	
	Phase		% of Phase	
	Closeout		100%	
Project Team				
Manager		Andreas Peeples		
Architect		PBK Architects		
Contractor		Prime Contractors		
CMPA		N/A		

**KEY FACTS**

Budget
\$35,278,934

Location
2020 Mangum Road

DELMAR FIELDHOUSE

Delmar Fieldhouse is a multipurpose facility, including a 12,000-seat football stadium, baseball fields, and a fieldhouse.


SCOPE OF WORK

Replacement of regional field house(s) and athletic facility improvements.

PROJECT STATUS

Closeout underway.

INFORMATION

Indicator	ID	Project/School/Facility		Budget
	C-663	Delmar Fieldhouse		\$35,278,934
	Target Construction Start		Target Construction Completion	
	1st Qtr. 2014		4th Qtr. 2016	
	Phase		% of Phase	
	Closeout		75%	
Project Team				
Manager		Andreas Peeples		
Architect		PBK Architects		
Contractor		DivisionOne Construction		
CMPA		Rice & Gardner Consultants, Inc.		



Northside High School

Supplier Diversity (M/WBE) Bond Report

Alexis Licata
Officer, Business Logistics
4400 W. 18th Street, Level 1 South
Houston, Texas 77092
BusinessAssistance@HoustonISD.org

HISD WORKSHOPS

WORKSHOP WEDNESDAY

- January – **"How to do Business with HISD."** Presenter: HISD Supplier Diversity Department
- February – **"Access to Capital."** Presenter: Nini Gutierrez, Senior Loan Officer, PeopleFund Houston
- March – **"Better Proposals Equal More Wins."** Presenter: Julie Irvin Hartman, CF APMP, Certified Proposal Manager and Trainer

M/WBE HISD EVENTS

- CMAR Supplier Outreach - Project Announcement Event
- CMAR Supplier Outreach - Network Meet & Greet

M/WBE OUTREACH EVENTS

EAST END CHAMBER OF COMMERCE

- 2018 Vision Luncheon
- Business Over Breakfast

FIFTH WARD CHAMBER OF COMMERCE

- The Nickel Connection Breakfast

GREATER HOUSTON BLACK CHAMBER

- Programs Committee Meeting
- Doing Business with HISD Presentation

GREATER HOUSTON BUSINESS PROCUREMENT FORUM

- Procurement Breakfast Exhibitor

HOUSTON MINORITY SUPPLIER DEVELOPMENT COUNCIL (HMSDC)

- Supplier Diversity Advisory Committee Meeting (SDAC)
- Procurement Marketing Luncheon Exhibitor

WOMEN'S BUSINESS ENTERPRISE ALLIANCE (WBEA)

- Corporate Advisory Committee Meeting (CAC)
- Thought Leadership Luncheon Exhibitor

WOMEN CONTRACTORS ASSOCIATION

- Annual Forecast of the Houston Construction Marketplace, March Luncheon


2012 BOND CONSTRUCTION M/WBE BREAKDOWN BY PROJECT TYPE

Calculations based on numbers reported as of March 31, 2018

ARCHITECT PROJECTS

TOTAL AWARDED: \$70,838,521


TOTAL COMMITTED: \$37,191,631

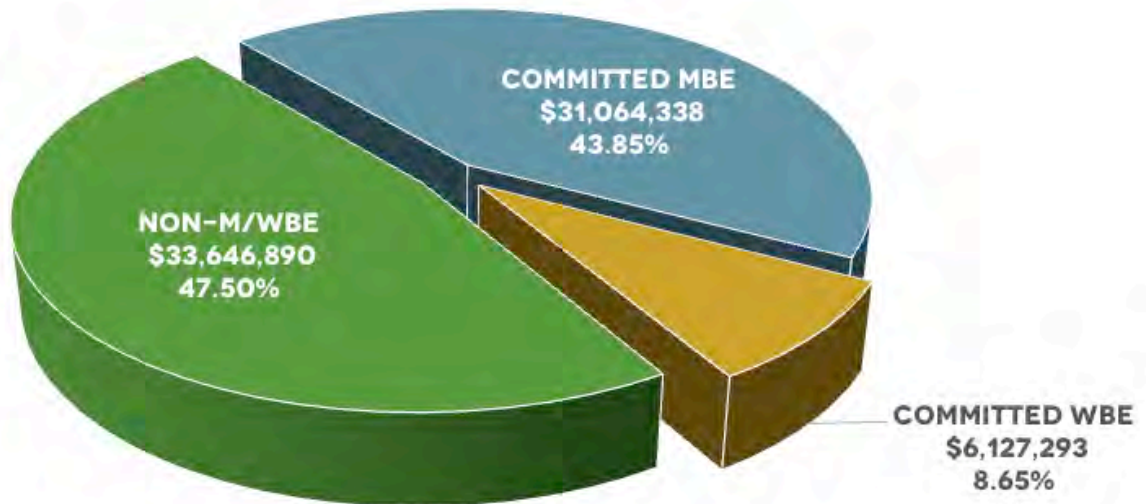

CONSTRUCTION FIRM PROJECTS

TOTAL AWARDED: \$1,174,640,302

TOTAL COMMITTED: \$297,412,467

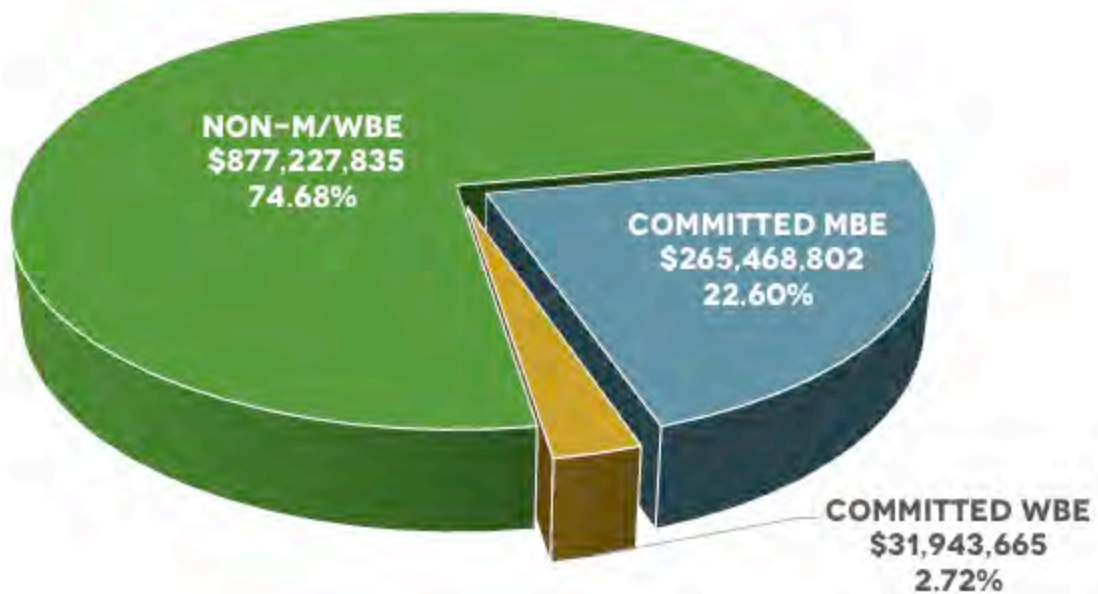


2012 BOND CONSTRUCTION M/WBE BREAKDOWN BY PROJECT TYPE

Calculations based on numbers reported as of March 31, 2018

PROGRAM MANAGEMENT FIRM PROJECTS

TOTAL AWARDED: \$52,276,179

TOTAL COMMITTED: \$23,342,543

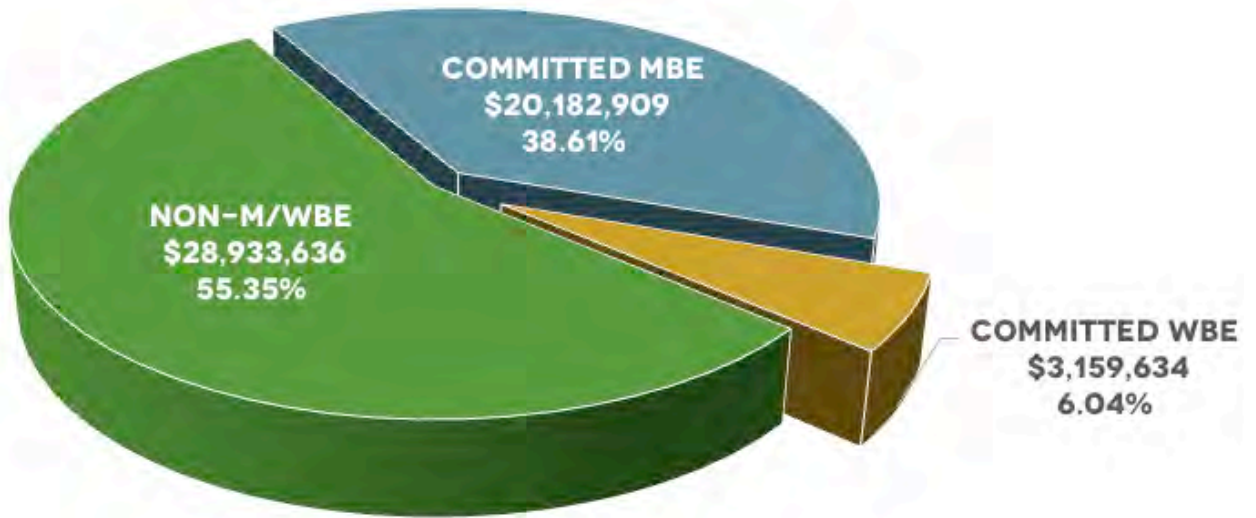


OTHER PROJECTS/VARIOUS VENDOR COSTS

(INCLUDING OTHER PROGRAM MANAGEMENT FEES & COSTS)

TOTAL AWARDED: \$411,177,439

TOTAL COMMITTED: \$119,528,909

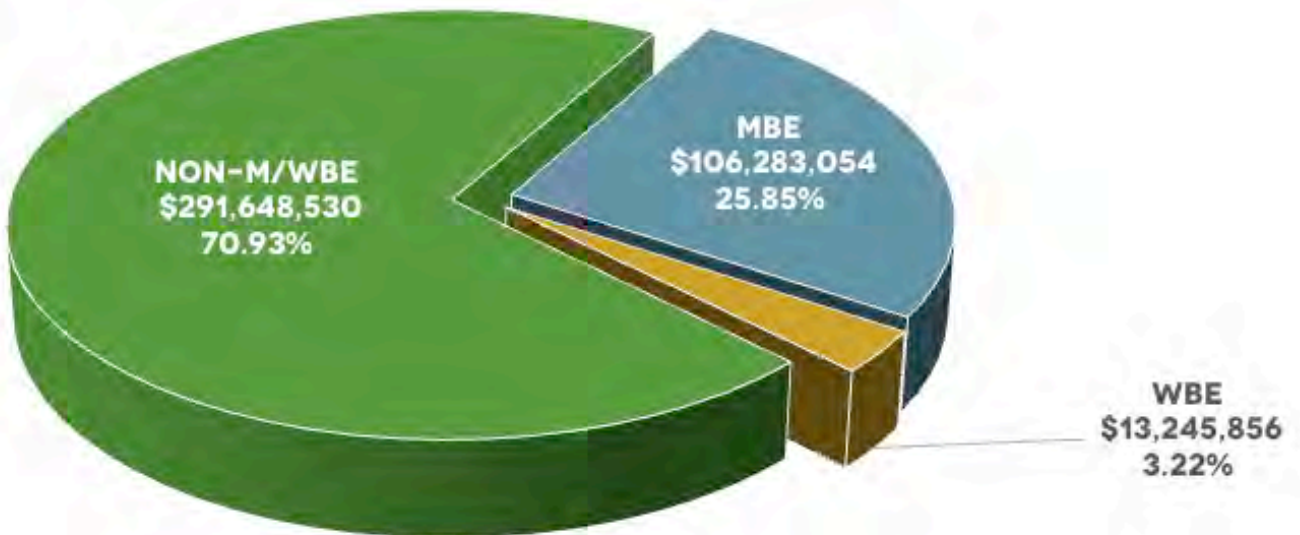


2012 BOND CONSTRUCTION M/WBE BREAKDOWN BY PROJECT TYPE

Calculations based on numbers reported as of March 31, 2018

TOTAL COMBINED PROJECTS

TOTAL AWARDED: \$1,708,932,441

TOTAL COMMITTED: \$477,475,550

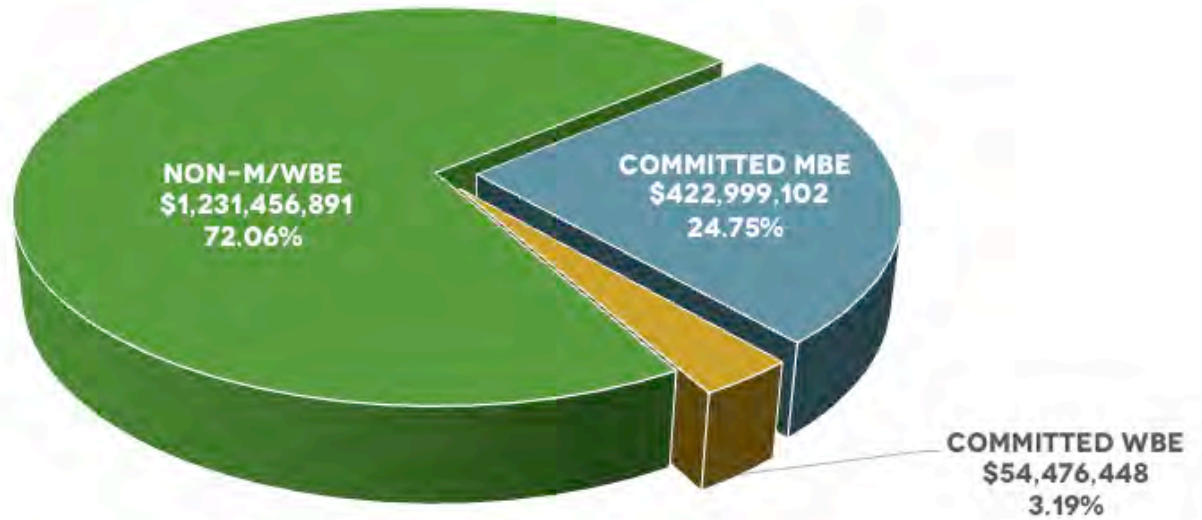

M/WBE BOND REPORT

School Name	Vendor / Project Type	Vendor Name	Contracted Amount	Payments to Date	"First Tier MBE Spend"	"First Tier WBE Spend"	Additional MBE Spend	Additional WBE Spend	Second Tier MBE Spend	Second Tier WBE Spend	Actual M/WBE Spend Amount	Actual M/WBE Spend Percentage
DEBAKEY H S H P	Architect	WHR Architects	\$2,536,210.98	\$2,537,460.32	\$0.00	\$0.00	\$0.00	\$0.00	\$106,570.00	\$491,436.00	\$598,006.00	23.58%
	CMAR	Telepsen Builders, L. P.	\$48,632,154.76	\$37,076,099.20	\$0.00	\$0.00	\$0.00	\$0.00	\$9,361.30	\$0.00	\$9,361.30	0.02%
	Other	Various Vendors	\$8,039,743.27	\$18,752,370.85	\$1,918,723.07	\$237,565.89	\$0.00	\$0.00	\$0.00	\$0.00	\$2,156,288.96	26.82%
	Total		\$59,208,109.01	\$58,365,930.37								
TANGLEWOOD (FORMERLY GRADY) MIDDLE SCHOOL	Architect	Natex	\$645,211.83	\$642,877.83	\$0.00	\$645,211.83	\$0.00	\$0.00	\$0.00	\$0.00	\$645,211.83	100.00%
	CMAR	DivisionOne Construction, LLC	\$10,394,436.33	\$10,394,436.33	\$0.00	\$0.00	\$0.00	\$0.00	\$3,194,907.38	\$24,243.04	\$3,219,150.42	30.38%
	Other	Various Vendors	\$2,494,452.61	\$2,584,888.36	\$1,049,080.29	\$142,537.70	\$0.00	\$0.00	\$0.00	\$0.00	\$1,191,627.99	47.77%
	Total		\$13,736,378.84	\$13,622,202.52								
WISDOM (FORMERLY LEE) HIGH SCHOOL	Architect	WHRLake Flato	\$2,838,836.18	\$2,585,353.13	\$0.00	\$0.00	\$0.00	\$0.00	\$137,818.75	\$416,463.00	\$554,281.75	19.52%
	CMAR	Satterfield & Pontikes Construction Co.	\$55,293,188.14	\$32,254,996.81	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
	Other	Various Vendors	\$10,015,645.09	\$31,350,490.95	\$1,443,050.77	\$1,328,599.60	\$0.00	\$0.00	\$0.00	\$0.00	\$2,771,850.37	27.67%
	Total		\$68,147,669.41	\$66,190,840.89								
MANDARIN CHINESE LANGUAGE IMMERSION MAGNET SCHOOL	Architect	PBK Architects	\$1,285,560.23	\$1,202,171.45	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
	CMAR	Satterfield & Pontikes Construction Co.	\$26,863,589.62	\$24,281,635.43	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
	Other	Various Vendors	\$4,495,467.94	\$6,554,521.48	\$1,438,906.45	\$114,207.61	\$0.00	\$0.00	\$0.00	\$0.00	\$1,553,114.06	34.55%
	Total		\$32,624,617.79	\$32,038,328.36								
MARK WHITE ELEMENTARY SCHOOL	Architect	English & Associates	\$874,156.43	\$743,349.64	\$0.00	\$874,156.43	\$0.00	\$0.00	\$0.00	\$0.00	\$874,156.43	100.00%
	CMAR	DivisionOne Construction, LLC	\$17,227,501.40	\$10,044,929.87	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
	Other	Various Vendors	\$4,706,066.00	\$11,752,905.04	\$2,552,377.69	\$173,846.93	\$0.00	\$0.00	\$0.00	\$0.00	\$2,726,224.62	0.00%
	Total		\$22,807,723.83	\$22,541,184.55								
MICKEY LELAND COLLEGE PREPARATORY ACADEMY (YMCPA)	Architect	Harrison Korbarg	\$1,391,575.08	\$1,138,023.82	\$1,391,575.08	\$0.00	\$147,111.00	\$24,336.83	\$0.00	\$0.00	\$1,391,575.08	100.00%
	CSP	Prime Contractors	\$24,484,992.94	\$12,413,267.93	\$0.00	\$0.00	\$0.00	\$0.00	\$436,598.93	\$3,319,213.64	\$3,755,812.57	0.00%
	Other	Various Vendors	\$1,273,960.84	\$13,479,952.92	\$2,320,307.42	\$245,345.73	\$0.00	\$0.00	\$0.00	\$0.00	\$2,565,653.15	201.39%
	Total		\$27,150,528.86	\$27,031,244.37								
MILBY HIGH SCHOOL	Architect	Kirksey Architecture	\$2,783,576.96	\$2,541,693.85	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
	CMAR	Telepsen Builders, L. P.	\$57,117,634.13	\$37,696,841.54	\$0.00	\$0.00	\$0.00	\$0.00	\$181,926.99	\$3,990.00	\$185,916.99	0.33%
	Other	Various Vendors	\$13,515,367.28	\$32,307,717.53	\$5,730,882.53	\$1,025,179.44	\$0.00	\$0.00	\$0.00	\$0.00	\$6,755,881.97	49.99%
	Total		\$73,416,578.37	\$72,546,252.92								
NORTH HOUSTON EARLY COLLEGE HIGH SCHOOL	Architect	RDLR Architects	\$664,989.29	\$655,581.29	\$664,989.29	\$0.00	\$39,971.00	\$12,000.00	\$0.00	\$0.00	\$664,989.29	100.00%
	CMAR	Dymalla Construction Company Inc.	\$11,541,996.35	\$11,415,118.11	\$0.00	\$0.00	\$0.00	\$0.00	\$2,341,368.61	\$107,588.95	\$2,448,957.56	21.22%
	Other	Various Vendors	-\$2,128,845.51	-\$2,087,675.69	\$595,903.74	\$122,128.31	\$0.00	\$0.00	\$0.00	\$0.00	\$718,032.05	-33.73%
	Total		\$10,078,139.13	\$9,983,023.71								
SHARPSTOWN HIGH SCHOOL	Architect	Manoz & Company	\$2,161,935.24	\$1,726,231.82	\$2,161,935.24	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$2,161,935.24	100.00%
	CMAR	ICI Construction	\$11,300,000.00	\$26,365,111.58	\$0.00	\$0.00	\$0.00	\$0.00	\$647,838.46	\$156,149.03	\$803,985.49	7.11%
	Other	Various Vendors	\$40,530,935.93	\$22,627,318.97	\$2,644,566.54	\$154,476.85	\$0.00	\$0.00	\$0.00	\$0.00	\$2,799,043.39	6.91%
	Total		\$53,992,871.17	\$50,518,662.37								
SOUTH EARLY COLLEGE HIGH SCHOOL (EMPOWERMENT)	Architect	Smith & Company Architects, Inc.	\$642,300.00	\$466,363.00	\$642,300.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$642,300.00	100.00%
	CMAR	Dymalla Construction Company Inc.	\$10,494,819.91	\$8,687,122.43	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
	Other	Various Vendors	-\$1,307,291.14	\$573,503.60	\$951,583.98	\$60,290.36	\$0.00	\$0.00	\$0.00	\$0.00	\$1,011,874.34	0.00%
	Total		\$9,829,828.77	\$9,726,989.03								

M/WBE BOND REPORT

School Name	Vendor / Project type	Vendor Name	Contracted Amount	Payments to Date	"First Tier MBE Spend"	"First Tier WBE Spend"	Additional MBE Spend	Additional WBE Spend	Second Tier MBE Spend	Second Tier WBE Spend	Actual MWBE Spend Amount	Actual MWBE Spend Percentage
STERLING HIGH SCHOOL	Architect	STANTEC ARCHITECTURE INC.	\$614,777.62	\$388,860.62	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
	CMMR	Cadence McShane Construction, Inc.	\$48,211,392.81	\$40,827,960.39	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
	Other	Various Vendors	\$9,295,200.83	\$15,118,936.51	\$2,465,636.25	\$154,917.97	\$0.00	\$0.00	\$0.00	\$0.00	\$2,620,554.22	28.19%
		Total	\$58,121,371.26	\$56,335,757.52								
WALTRIP HIGH SCHOOL	Architect	Gensler	\$1,900,840.89	\$1,076,129.05	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
	CMMR	Satterfield & Pontikes Construction Co.	\$34,028,969.54	\$27,167,460.32	\$0.00	\$0.00	\$0.00	\$0.00	\$927,062.39	\$0.00	\$927,062.39	2.72%
	Other	Various Vendors	\$6,474,179.58	\$309,999.48	\$556,994.73	\$399,262.61	\$0.00	\$0.00	\$0.00	\$0.00	\$956,257.34	-14.77%
		Total	\$29,455,630.85	\$28,553,588.85								
WASHINGTON HIGH SCHOOL	Architect	Fanning-Howey House Partners, LLC	\$2,434,138.29	\$2,320,686.76	\$0.00	\$0.00	\$0.00	\$0.00	\$212,219.44	\$433,386.00	\$645,605.44	26.52%
	CMMR	Comer Rock Construction, LLC	\$396,802.20	\$390,135.55	\$0.00	\$396,802.20	\$0.00	\$0.00	\$0.00	\$0.00	\$396,802.20	100.00%
	CMMR	Prime Contractors	\$42,800,000.00	\$30,110,555.73	\$0.00	\$0.00	\$4,071,629.07	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
	Other	Various Vendors	\$5,730,157.19	\$11,284,759.41	\$1,488,170.12	\$1,173,306.44	\$0.00	\$0.00	\$0.00	\$0.00	\$2,631,476.56	45.92%
		Total	\$51,361,097.68	\$44,106,137.45								
WORTHING HIGH SCHOOL	Architect	Melina Walker Architects, Inc.	\$560,627.39	\$560,627.39	\$0.00	\$560,627.39	\$0.00	\$0.00	\$0.00	\$0.00	\$560,627.39	100.00%
	CMMR	BalfourSCJ (A Joint Venture-BSCJ)	\$18,942,052.27	\$18,942,052.27	\$0.00	\$0.00	\$0.00	\$0.00	\$10,182,829.49	\$1,648,556.77	\$11,831,386.26	62.46%
	CSP	Prime Contractors	\$22,212,789.09	\$12,109,928.26	\$0.00	\$0.00	\$0.00	\$0.00	\$608,712.08	\$2,185,949.46	\$2,794,661.54	12.58%
	Other	Various Vendors	\$-12,881,118.88	\$-13,127,657.63	\$161,730.66	\$9,405.00	\$0.00	\$0.00	\$0.00	\$0.00	\$171,135.66	-1.33%
		Total	\$28,834,349.87	\$18,484,950.29								
BELLAIRE HIGH SCHOOL	Architect	PBK Architects	\$7,413,011.48	\$1,598,323.64	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
	CMMR	Turner Construction Company	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
	Other	Various Vendors	\$-60,742.71	\$293,750.28	\$164,350.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$164,350.00	-270.57%
		Total	\$7,352,268.77	\$1,882,073.92								
NORTHSIDE (FORMERLY DAVIS) HIGH SCHOOL	Architect	BAY/BI	\$2,950,799.43	\$1,144,979.36	\$0.00	\$0.00	\$0.00	\$0.00	\$92,037.93	\$439,321.99	\$531,359.92	18.01%
	CMMR	SATTERFIELD & PONTIKES CONST.	\$43,833,775.43	\$20,709,997.22	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
	Other	Various Vendors	\$5,315,836.69	\$4,355,618.46	\$3,330,616.77	\$417,216.96	\$0.00	\$0.00	\$0.00	\$0.00	\$3,747,833.73	70.50%
		Total	\$52,100,411.55	\$26,210,595.04								
LAWSON (FORMERLY DOWLING) MIDDLE SCHOOL	Architect	Harrison Kornberg	\$2,208,552.06	\$1,727,952.20	\$2,208,552.06	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$2,208,552.06	100.00%
	CMMR	Turner Construction Company	\$48,174,529.00	\$40,094,920.47	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
	Other	Various Vendors	\$4,237,938.39	\$854,838.56	\$724,406.13	\$10,482.43	\$0.00	\$0.00	\$0.00	\$0.00	\$734,888.56	17.34%
		Total	\$54,621,019.45	\$42,677,711.23								
EASTWOOD ACADEMY HIGH SCHOOL	Architect	Prozign	\$462,949.00	\$410,994.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
	Other	Various Vendors	\$10,180,700.24	\$8,063,850.10	\$418,103.36	\$31,570.34	\$0.00	\$0.00	\$0.00	\$0.00	\$449,673.70	4.42%
		Total	\$10,643,649.24	\$8,474,844.10								
	Architect	Perkins+Will	\$4,803,209.91	\$1,769,517.66	\$0.00	\$0.00	\$0.00	\$0.00	\$387,527.72	\$537,307.90	\$924,835.62	19.25%
LAMAR HIGH SCHOOL	CMMR	Gilbane Building Company	\$103,811,590.20	\$18,801,284.11	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
	Other	Various Vendors	\$2,141,555.50	\$2,627,208.63	\$507,687.31	\$32,000.00	\$0.00	\$0.00	\$0.00	\$0.00	\$539,687.31	25.20%
		Total	\$110,756,355.61	\$23,197,010.40								

M/WBE BOND REPORT

School Name	Vendor / Project Type	Vendor Name	Contracted Amount	Payments to Date	"First Tier MBE Spend"	"First Tier WBE Spend"	Additional MBE Spend	Additional MBE Spend	Second Tier MBE Spend	Second Tier WBE Spend	Actual M/WBE Spend Percentage
PARKER ELEMENTARY SCHOOL	Architect	Brave Architecture	\$1,082,397.11	\$919,181.05	\$1,082,397.11	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	100.00%
	CMAR	Patriot Contracting, LLC	\$22,700,000.00	\$16,106,833.15	\$0.00	\$0.00	\$0.00	\$0.00	\$359,053.29	\$1,246,022.32	0.00%
	Other	Various Vendors	\$4,354,960.18	\$6,568,903.00	\$2,363,598.25	\$206,981.46	\$0.00	\$0.00	\$0.00	\$0.00	59.03%
		Total	\$28,137,357.29	\$23,594,917.20							
YATES HIGH SCHOOL	Architect	Moody-Noian/Huerta Associates	\$2,397,235.71	\$1,576,999.30	\$2,397,235.71	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	100.00%
	CMAR	Turner Construction Company	\$0.00	\$32,613,335.28	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
	Other	Various Vendors	\$53,882,164.27	\$11,471,144.84	\$1,636,877.86	\$31,863.60	\$0.00	\$0.00	\$0.00	\$0.00	3.10%
		Total	\$56,279,399.98	\$45,661,479.42							
ASKEW ELEMENTARY SCHOOL	Architect	Cre8 Architects	\$940,427.45	\$665,723.45	\$940,427.45	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	100.00%
	CMAR	Drymalla Construction Company Inc.	\$19,230,254.00	\$14,529,158.00	\$0.00	\$0.00	\$0.00	\$0.00	\$503,595.05	\$0.00	2.62%
	Other	Various Vendors	\$2,876,158.92	\$2,494,628.99	\$594,948.39	\$67,450.00	\$0.00	\$0.00	\$0.00	\$0.00	23.03%
		Total	\$23,046,840.37	\$17,689,510.44							
FURR HIGH SCHOOL	Architect	ERO International LLP	\$1,670,868.57	\$1,426,126.99	\$1,670,868.57	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	100.00%
	CSP	Prime Contractors	\$43,185,427.74	\$26,080,432.03	\$0.00	\$0.00	\$0.00	\$0.00	\$2,491,746.08	\$3,688,164.83	0.00%
	Other	Various Vendors	\$4,633,977.12	\$19,744,569.71	\$1,406,388.11	\$1,098,989.88	\$0.00	\$0.00	\$0.00	\$0.00	54.07%
		Total	\$49,490,273.43	\$47,251,128.73							
HIGH SCHOOL FOR PERFORMING & VISUAL ARTS	Architect	Gensler	\$3,328,769.89	\$2,676,432.08	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
	CMAR	McCarthy Building Companies	\$7,529,738.17	\$46,350,782.92	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
	Other	Various Vendors	-\$739,834.17	\$15,206,561.03	\$881,152.45	\$0.00	\$0.00	\$0.00	\$4,994.00	\$0.00	-119.78%
		Total	\$80,118,673.89	\$64,233,776.03							
JORDAN HIGH SCHOOL	Architect	Corgan Associates, Inc. DBA Corgan	\$1,235,247.39	\$904,085.39	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
	CSP	Cadence McShane Construction, Inc.	\$27,642,063.30	\$8,119,281.47	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
	Other	Various Vendors	\$777,672.36	\$483,545.07	\$174,295.98	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	22.41%
		Total	\$29,654,983.05	\$9,505,911.93							
SAM HOUSTON MATH SCIENCE AND TECHNOLOGY CENTER	Architect	Stantec Architecture Inc.	\$3,687,899.62	\$2,170,927.21	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
	CMAR	Satterfield & Pontikes Construction Co.	\$79,902,331.00	\$37,084,625.81	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
	Other	Various Vendors	\$2,898,517.98	\$1,214,129.32	\$1,528,065.63	\$113,763.00	\$0.00	\$0.00	\$0.00	\$0.00	56.64%
		Total	\$86,488,748.60	\$40,469,682.34							
YOUNG WOMEN'S COLLEGE PREPARATORY ACADEMY (YWCPA)	Architect	Natlex	\$1,152,642.18	\$926,399.34	\$0.00	\$1,152,642.18	\$0.00	\$0.00	\$0.00	\$0.00	100.00%
	CMAR	SATTERFIELD & PONTIKES CONST.	\$716,542.96	\$14,809,174.66	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
	Other	Various Vendors	\$26,318,521.69	\$10,378,180.88	\$1,044,377.48	\$293,146.30	\$0.00	\$0.00	\$0.00	\$0.00	5.08%
		Total	\$28,187,706.83	\$26,113,754.88							
AUSTIN HIGH SCHOOL	Architect	ERO International LLP	\$2,785,215.03	\$1,199,847.03	\$2,785,215.03	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	100.00%
	CMAR	Pepper-Lawson Construction, L.P.	\$59,616,278.70	\$6,156,920.86	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
	Other	Various Vendors	\$4,274,660.00	\$2,204,310.33	\$963,751.28	\$69,160.25	\$0.00	\$0.00	\$0.00	\$0.00	21.82%
		Total	\$66,676,153.73	\$9,561,078.22							
GARDEN OAKS MONTESSORI	Architect	Hill Swart Chu Architects	\$918,298.61	\$699,423.70	\$0.00	\$918,298.61	\$0.00	\$0.00	\$0.00	\$0.00	100.00%
	CMAR	BalfourSCl (A Joint Venture-BSCl)	\$22,257,513.00	\$15,627,923.01	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
	Other	Various Vendors	\$3,832,201.09	\$2,486,185.94	\$1,353,400.22	\$435,902.92	\$0.00	\$0.00	\$0.00	\$0.00	46.69%
		Total	\$27,008,012.70	\$18,823,532.65							

M/WBE BOND REPORT

School Name	Vendor / Project Type	Vendor Name	Contracted Amount	Payments to Date	*First Tier MBE Spend*	*First Tier WBE Spend*	Additional MBE Spend	Second Tier MBE Spend	Second Tier WBE Spend	Actual M/WBE Spend Amount	Actual M/WBE Spend Percentage
JONES FUTURES ACADEMY	Other	Various Vendors	\$522,474.75	\$522,474.75	\$200,759.29	\$64,296.84	\$0.00	\$0.00	\$0.00	\$265,056.13	0.00%
		Total	\$522,474.75	\$522,474.75							
KASHMERE HIGH SCHOOL	Architect	Natex	\$800,455.48	\$659,530.61	\$0.00	\$800,455.48	\$0.00	\$0.00	\$0.00	\$800,455.48	100.00%
		DT CONSTRUCTION	\$13,060,000.00	\$4,040,149.76	\$0.00	\$0.00	\$0.00	\$175,116.90	\$2,290,561.52	\$2,465,678.42	18.88%
KASHMERE HIGH SCHOOL	Other	Various Vendors	\$2,240,290.52	\$11,183,406.62	\$735,024.27	\$146,471.11	\$0.00	\$0.00	\$0.00	\$881,485.38	39.35%
		Total	\$16,100,746.00	\$15,883,086.99							
MADISON HIGH SCHOOL	Architect	Morris Architects, Inc.	\$2,826,827.42	\$2,094,035.42	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
MADISON HIGH SCHOOL	CMAR	Satterfield and Pontikes Construction, Inc.	\$59,526,905.23	\$31,338,730.76	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
MADISON HIGH SCHOOL	Other	Various Vendors	\$6,848,701.58	\$6,314,604.43	\$430,783.20	\$0.00	\$0.00	\$0.00	\$0.00	\$430,783.20	6.29%
		Total	\$69,202,434.23	\$39,747,370.61							
PILGRIM ACADEMY	Architect	RDC Architects	\$282,840.18	\$187,440.18	\$282,840.18	\$0.00	\$0.00	\$0.00	\$0.00	\$282,840.18	100.00%
PILGRIM ACADEMY	CSP	DT CONSTRUCTION	\$5,570,330.23	\$4,004,665.34	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
PILGRIM ACADEMY	Other	Various Vendors	\$1,343,394.00	\$935,144.45	\$490,195.20	\$19,651.98	\$0.00	\$0.00	\$0.00	\$509,847.18	37.95%
		Total	\$7,196,564.41	\$5,127,249.97							
SCARBOROUGH HIGH SCHOOL	Architect	Randall-Porterfield	\$626,292.00	\$504,058.61	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
SCARBOROUGH HIGH SCHOOL	CSP	DT CONSTRUCTION	\$9,809,576.00	\$9,299,528.26	\$0.00	\$0.00	\$0.00	\$145,221.75	\$0.00	\$145,221.75	1.48%
SCARBOROUGH HIGH SCHOOL	Other	Various Vendors	\$1,652,621.70	\$1,386,202.56	\$729,938.52	\$441,916.56	\$0.00	\$0.00	\$0.00	\$1,171,855.08	70.91%
		Total	\$12,088,489.70	\$11,199,789.43							
SHARPSTOWN INTERNATIONAL SCHOOL	Architect	Aubarch Architects	\$238,508.61	\$169,148.81	\$0.00	\$238,508.61	\$0.00	\$0.00	\$0.00	\$238,508.61	100.00%
SHARPSTOWN INTERNATIONAL SCHOOL	CSP	DT CONSTRUCTION	\$3,810,064.59	\$918,606.17	\$0.00	\$0.00	\$0.00	\$523,616.75	\$275,411.04	\$799,027.79	20.97%
SHARPSTOWN INTERNATIONAL SCHOOL	Other	Various Vendors	\$562,401.72	\$3,573,543.64	\$147,642.00	\$49,123.63	\$0.00	\$0.00	\$0.00	\$196,766.63	34.99%
		Total	\$4,610,974.92	\$4,561,298.42							
WESTBURY HIGH SCHOOL	Architect	Joiner Partnership, Inc.	\$1,195,078.00	\$910,009.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
WESTBURY HIGH SCHOOL	CMAR	Satterfield & Pontikes Construction Co.	\$5,035,486.00	\$31,825,957.96	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
WESTBURY HIGH SCHOOL	Other	Various Vendors	\$38,603,892.73	\$7,646,173.09	\$792,863.78	\$956,576.09	\$0.00	\$0.00	\$0.00	\$1,749,239.87	4.53%
		Total	\$44,834,456.73	\$40,382,140.05							
WHARTON K-8 DUAL LANGUAGE ACADEMY	Architect	Munoz & Company	\$1,135,716.00	\$925,211.66	\$1,135,716.00	\$0.00	\$0.00	\$0.00	\$0.00	\$1,135,716.00	100.00%
WHARTON K-8 DUAL LANGUAGE ACADEMY	CMAR	DivisionOne Construction	\$26,671,326.75	\$14,481,877.92	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
WHARTON K-8 DUAL LANGUAGE ACADEMY	Other	Various Vendors	\$4,390,047.24	\$3,913,648.00	\$426,267.03	\$0.00	\$0.00	\$0.00	\$0.00	\$426,267.03	9.71%
		Total	\$32,197,069.99	\$19,020,737.58							
WILSON MONTESSORI	Architect	Smith & Company Architects, Inc.	\$753,556.30	\$659,771.83	\$753,556.30	\$0.00	\$0.00	\$0.00	\$0.00	\$753,556.30	100.00%
WILSON MONTESSORI	CMAR	Drymalla Construction Company Inc.	\$14,935,700.00	\$13,256,845.41	\$0.00	\$0.00	\$0.00	\$1,251,821.16	\$107,866.30	\$1,359,687.46	9.10%
WILSON MONTESSORI	Other	Various Vendors	\$2,843,043.01	\$2,353,324.71	\$894,276.75	\$173,001.24	\$0.00	\$0.00	\$0.00	\$1,067,277.99	37.54%
		Total	\$18,532,299.31	\$16,069,941.95							
BARNETT FIELD HOUSE	Architect	PBK Architects	\$216,082.79	\$192,607.82	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
BARNETT FIELD HOUSE	CSP	Prime Contractors	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
BARNETT FIELD HOUSE	Other	Various Vendors	-\$15,832.64	\$7,086.59	\$21,209.52	\$0.00	\$0.00	\$0.00	\$0.00	\$21,209.52	-133.96%
		PBK Architects	\$367,377.81	\$189,811.41	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%

M/WBE BOND REPORT

School Name	Vendor / Project Type	Vendor Name	Contracted Amount	Payments to Date	"First Tier MBE Spend"	"First Tier WBE Spend"	Additional MBE Spend	Second Tier WBE Spend	Actual M/WBE Spend Amount	Actual M/WBE Percentage
BUTLER FIELD HOUSE	CSP	Prime Contractors	\$858,703.44	\$858,703.44	\$0.00	\$0.00	\$0.00	\$63,829.22	\$63,829.22	0.00%
	Other	Various Vendors	\$60,113.05	\$207,146.71	\$55,085.00	\$14,184.31	\$0.00	\$0.00	\$69,269.31	115.23%
	Architect	PBK Architects	\$2,039,458.36	\$1,817,372.78	\$0.00	\$0.00	\$0.00	\$9,450.40	\$86,123.62	4.69%
	CMAR	DivisionOne Construction	\$36,141,441.77	\$31,689,198.59	\$0.00	\$0.00	\$0.00	\$9,515,752.58	\$95,384.75	26.59%
	Other	Various Vendors	\$2,131,746.19	\$6,466,704.64	\$1,365,959.01	\$121,214.41	\$0.00	\$0.00	\$1,487,173.42	68.76%
		Total	\$41,799,090.77	\$41,438,631.98						
MIDDLE SCHOOL RESTROOMS	Architect	Robert Adams, Inc.	\$523,443.00	\$473,912.11	\$523,443.00	\$0.00	\$0.00	\$0.00	\$523,443.00	100.00%
MIDDLE SCHOOL RESTROOMS	Architect	Courney Harper + Partners, Inc.	\$626,053.67	\$580,811.16	\$0.00	\$626,053.67	\$0.00	\$0.00	\$626,053.67	100.00%
MIDDLE SCHOOL RESTROOMS	Architect	English & Associates	\$311,339.19	\$262,815.07	\$0.00	\$311,339.19	\$0.00	\$0.00	\$311,339.19	100.00%
MIDDLE SCHOOL RESTROOMS	Architect	VCS	\$543,233.53	\$466,097.99	\$0.00	\$0.00	\$0.00	\$0.00	\$63,554.00	11.70%
MIDDLE SCHOOL RESTROOMS	CSP	DTCONSTRUCTION	\$3,312,000.00	\$3,227,268.79	\$0.00	\$0.00	\$0.00	\$747,339.66	\$0.00	22.56%
MIDDLE SCHOOL RESTROOMS	CSP	Prime Contractors	\$7,164,127.04	\$9,843,931.38	\$0.00	\$0.00	\$0.00	\$3,331,000.78	\$45,323.55	47.13%
MIDDLE SCHOOL RESTROOMS	Other	Various Vendors	\$13,788,323.57	\$10,993,910.80	\$2,695,466.35	\$55,293.46	\$0.00	\$216,720.26	\$0.00	21.55%
		Total	\$26,248,520.00	\$25,848,747.30						
TECHNOLOGY	Other	Various Vendors	\$35,211,137.10	\$34,200,027.84	\$33,662,922.49	\$659,249.27	\$0.00	\$0.00	\$34,321,071.76	97.47%
SAFETY & SECURITY	Other	Various Vendors	\$17,050,898.44	\$16,293,819.52	\$7,618,328.27	\$2,148,807.80	\$0.00	\$0.00	\$9,767,137.07	57.28%
LAND	Other	Various Vendors	\$46,904,000.70	\$46,892,395.60	\$1,401,738.32	\$157,218.61	\$0.00	\$0.00	\$1,558,956.93	3.32%
		Total	\$99,166,036.24	\$97,386,243.06						
HEERY INTERNATIONAL, INC.	PMF	HEERY INTERNATIONAL, INC.	\$27,475,077.46	\$14,078,878.57	\$0.00	\$0.00	\$0.00	\$2,918,177.37	\$192,120.00	11.32%
		Total	\$27,475,077.46	\$14,078,878.57						
JACOBS PROJECT MANAGEMENT CO.	PMF	JACOBS PROJECT MANAGEMENT CO.	\$1,933,367.48	\$1,398,731.48	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
		Total	\$1,933,367.48	\$1,398,731.48						
KWAME BUILDING GROUP, INC.	PMF	KWAME BUILDING GROUP, INC.	\$2,829,520.93	\$2,932,751.71	\$2,829,520.93	\$0.00	\$64,911.23	\$109,133.25	\$0.00	100.00%
		Total	\$2,829,520.93	\$2,932,751.71						
RICE & GARDNER CONSULTANTS	PMF	RICE & GARDNER CONSULTANTS	\$16,116,266.00	\$8,737,757.49	\$0.00	\$0.00	\$0.00	\$834,837.25	\$2,989,174.30	23.73%
		Total	\$16,116,266.00	\$8,737,757.49						
URS CORPORATION	PMF	URS CORPORATION	\$3,921,947.00	\$4,284,377.00	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	0.00%
		Total	\$3,921,947.00	\$4,284,377.00						
Other Program Management Fees & Costs	Other	Various Vendors	\$34,830,335.93	\$47,403,617.21	\$12,114,435.91	\$90,252.70	\$0.00	\$0.00	\$12,204,688.61	35.04%
		Total	\$34,830,335.93	\$47,403,617.21						
		Design & Construction Total	\$1,245,478,823.30	\$839,940,740.85	\$18,641,050.02	\$6,524,095.59	\$4,258,711.07	\$36,336.83	\$39,520,491.87	6.54%
		Technology, Safety & Security and Land Total	\$99,166,036.24	\$97,386,243.06	\$42,682,890.08	\$2,964,275.68	\$0.00	\$0.00	\$0.00	46.03%
		Other Project Cost Total (Various Vendors)	\$277,181,066.84	\$295,252,827.91	\$51,265,013.38	\$10,191,327.21	\$0.00	\$220,714.26	\$0.00	22.25%
		Other Project Cost Total (Various Vendors, Tech., Land and S&S)	\$376,347,103.08	\$392,639,070.97	\$93,947,903.46	\$13,155,602.89	\$0.00	\$220,714.26	\$0.00	28.52%
		Other Program Management Fees & Costs	\$34,830,335.93	\$47,403,617.21	\$12,114,435.91	\$90,252.70	\$0.00	\$0.00	\$0.00	35.04%
		Program Management Firms	\$52,276,176.87	\$31,432,496.25	\$2,829,520.93	\$0.00	\$64,911.23	\$109,133.25	\$3,181,294.30	18.68%
		Grand Total*	\$1,708,932,441.18	\$1,311,415,925.28	\$127,532,910.32	\$19,769,951.18	\$4,323,622.30	\$145,470.08	\$20,907,141.23	12.33%

CERTIFIED MINORITY/WOMEN OWNED BUSINESSES BREAKDOWN BY PROJECT TYPE

Calculations based on numbers reported as of March 31, 2018

2012 CMAR PROJECTS*

Project	Awarded CMAR	M/WBE Commitment
Askew Elementary School	Drymalla Construction Company, Inc.	28.00%
Austin High School	Pepper-Lawson Construction, L. P.	22.00%
Barnett Fieldhouse (CSP)	Prime Contractors Inc.	22.72%
Bellaire High School	Turner Construction Company	20.00%
Butler Fieldhouse (CSP)	Prime Contractors Inc.	24.68%
Condit Elementary School	DivisionOne Construction, LLC	30.00%
DeBaKey High School	Tellepsen Builders, L. P.	20.00%
Delmar Tusa Fieldhouse	DivisionOne Construction, LLC	30.00%
Eastwood Academy (CSP)	Patriot Contracting, LLC	20.13%
Furr High School (CSP)	Prime Contractors Inc.	23.67%
Garden Oaks Montessori	Balfour/3Ci a Joint Venture (B3Ci)	30.00%
Golfcrest Elementary School (CSP)	Amerian Construction	10.00%
HS for Law Enforcement & Criminal Justice	Balfour/3Ci a Joint Venture (B3Ci)	30.00%
HSPVA	McCarthy Building Companies	20.00%
Jordan High School (CSP)	Cadence McShane Construction, LLC	23.50%
Kashmere High School	DT Construction, LP	20.00%
Lamar High School	Gilbane Building Company	30.00%
Lawson (Formerly Dowling) Middle School	Turner Construction Company	20.00%
Madison High School (CSP)	Satterfield & Pontikes Const., Inc.	20.00%
Mandarin Chinese Language Immersion	Satterfield & Pontikes Const., Inc.	20.00%
Mark White Elementary School	DivisionOne Construction, LLC	30.00%
Mickey Leland College Preparatory Academy (CSP)	Prime Contractors Inc.	20.76%
Milby High School	Tellepsen Builders, L. P.	20.00%
North Houston Early College High School	Drymalla Construction Company, Inc.	20.00%
Northside (Formerly Davis) High School	Satterfield & Pontikes Const., Inc.	20.00%
Parker Elementary School (CSP)	Patriot Contracting, LLC	20.04%
Pilgrim Academy	DT Construction, LP	20.00%
Sam Houston Math, Science, and Technology Center	Satterfield & Pontikes Const., Inc.	20.00%
Scarborough High School (CSP)	DT Construction, LP	20.19%
Sharpstown High School (CSP)	ICI Construction	23.50%
Sharpstown International School (CSP)	DT Construction, LP	20.00%
South Early College High School	Drymalla Construction Company, Inc.	20.00%
Sterling High School	Cadence McShane Const., LLC	21.00%
Tanglewood (Formerly Grady) Middle School	DivisionOne Construction, LLC	30.00%
Waltrip High School	Satterfield & Pontikes Const., Inc.	20.00%
Washington High School (CSP)	Prime Contractors Inc.	20.38%
Westbury High School	Satterfield & Pontikes Const., Inc.	20.00%
Wharton Dual Language School	DivisionOne Construction, LLC	25.00%
Wilson Montessori School	Drymalla Construction Company, Inc.	20.14%
Wisdom (Formerly Lee) High School	Satterfield & Pontikes Const., Inc.	20.00%
Worthing High School (CSP)	Primer Contractors Inc.	20.40%
Yates High School	Turner Construction Company	20.00%
Young Women's College Preparatory Academy	Satterfield & Pontikes Const., Inc.	20.00%
*M/WBE Percentage reflects contractor's commitment.		



Madison High School

Bond Financial Reports

Sherrie Robinson
Controller


Office of the Controller, 3 Northeast
4400 W. 18th St.
Houston, Texas 77092

2012 BOND FINANCIAL REPORT

The total budget for the 2012 Bond Program, approved by voters in December 2012, is \$1.89 billion. The Board approved an additional \$212.4 million in supplemental funding in October 2015, bringing the total to \$2.102 billion. Of that, \$1,708,932,441 is committed, including encumbrances of \$397,429,517 and actual expenditures of \$1,311,502,924. There is \$393,517,522 available to complete projects.


TOTAL BUDGET, COMMITMENTS & AVAILABLE FUNDING TO DATE

TOTAL BUDGET \$2.1 BILLION

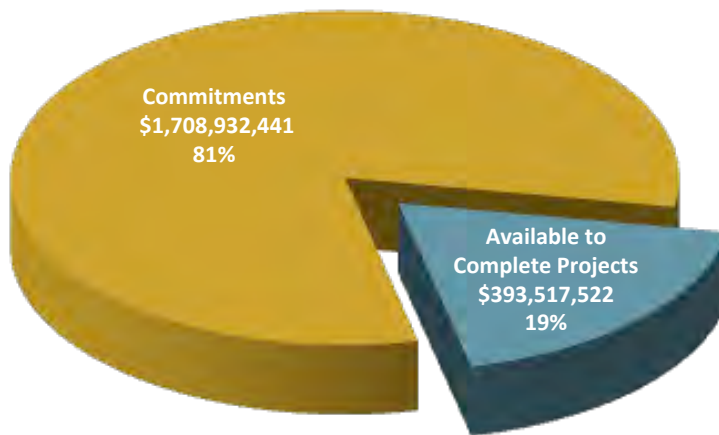

TOTAL BOND REFERENDUM \$1.89 BILLION

(ISSUANCE SALES IN MILLIONS)

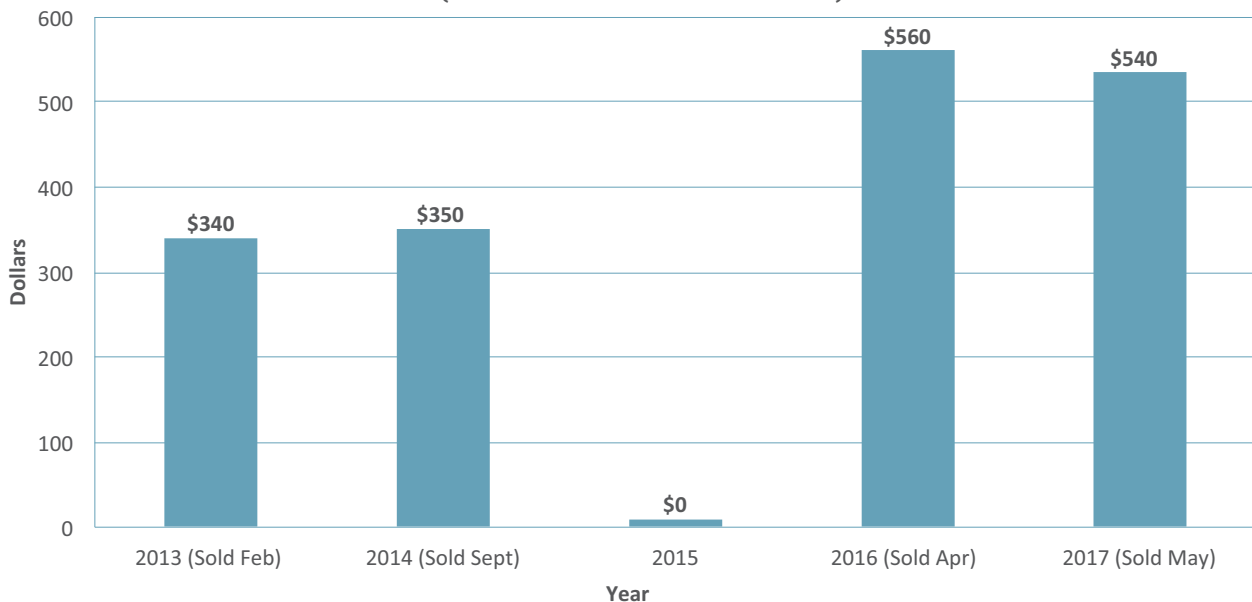



High School for Law & Justice

Project Budget/Commitment/ Available Funds Report

Report Descriptions

PROJECT BUDGET/COMMITMENT/AVAILABLE FUNDS REPORT

COLUMN 1

Org (Organization)

Represents the Texas Education Agency (TEA) number assigned to the school or non-school facility.

COLUMN 2

Campus

The school name or non-school facility name – also referred to as “Project.”

COLUMN 3

Original Plan

The original budget totaling \$1.89 billion approved by the voters in December 2012.

COLUMN 4

Supplemental Funding

Represents a total of \$212.4 million in additional funding approved October 2015 at the board workshop that could be needed to complete project budgets as originally proposed when the 2012 bond program was approved.

COLUMN 5

Total Adjusted Plan

Column 3 plus Column 4.

COLUMN 6

Program Reserve, Inflation, Management, & Swing Space

Includes Program Reserves, Program Management Fees, Program Inflation, and Program Swing Space.

COLUMN 7

Budget Plan

Column 5 – Column 6.

COLUMN 8

Pre-Encumbrance

Requisitions (request to buy) that have been entered into the accounting system and are pending approval/authorization to convert to a purchase order

COLUMN 9

Encumbrance

Purchase order – also referred to as “commitment.”

COLUMN 10

Actual

Represents total expenditures paid.

COLUMN 11

Available to Complete Projects

Uncommitted funds (the difference between the budget less pre-encumbrance less encumbrance less actual).

BOND FINANCIAL REPORT

2012 Bond Program - Project Budget/Commitment/Available Funds Report

As of March 31, 2018

Org	Campus	Total Budget	Supplemental Funding	Total Adjusted Budget	Program Reserve, Inflation, Mgt, & Swing Space	Construction Budget	Pre-Encumb	Encumbrance	Actual	Available to Complete Projects
		\$	\$	\$	(\$)	\$	(\$)	(\$)	(\$)	\$
001	Austin H.S.	68,429,000.00	11,161,679.00	79,590,679.00	12,521,549.00	67,069,130.00	60,718.18	57,049,882.43	9,565,553.12	392,976.27
002	Bellaire H.S.	106,724,000.00	25,290,428.00	132,014,428.00	17,505,908.00	114,508,520.00		5,470,194.85	1,882,073.92	107,156,251.23
003	Northside H.S.	46,764,000.00	19,633,657.00	66,397,657.00	8,136,745.00	58,260,912.00	135,774.00	25,754,042.51	26,210,595.04	6,160,500.45
004	Furr H.S.	55,100,000.00	1,258,524.00	56,358,524.00	4,873,066.00	51,485,458.00	145.95	2,214,127.38	47,276,000.10	1,995,184.57
006	Jones H.S.	1,125,000.00	296,011.00	1,421,011.00		1,421,011.00			522,474.75	898,536.25
007	Kashmere H.S.	17,000,000.00	2,053,729.00	19,053,729.00	2,699,674.00	16,354,055.00		217,659.01	15,883,086.99	253,309.00
008	Lamar H.S.	107,974,000.00	14,927,465.00	122,901,465.00	7,460,649.30	115,440,815.70		87,559,345.21	23,197,010.40	4,684,460.09
009	Wisdom H.S.	73,801,000.00	1,066,632.00	74,867,632.00	2,947,953.00	71,919,679.00	1,961.08	1,954,867.44	66,190,840.89	3,772,009.59
010	Madison H.S.	82,736,000.00	11,193,118.00	93,929,118.00	17,478,349.00	76,450,769.00		29,455,063.62	39,747,370.61	7,248,334.77
011	Milby H.S.	68,810,000.00	10,234,244.00	79,044,244.00	3,213,016.00	75,831,228.00	1,319.00	869,006.45	72,546,252.92	2,414,649.63
014	Sterling H.S.	72,304,000.00		72,304,000.00	12,942,809.17	59,361,190.83	14,214.35	1,802,509.77	56,304,647.14	1,239,819.57
015	Waltrip H.S.	30,115,000.00	2,123,961.00	32,238,961.00	1,561,860.00	30,677,101.00	1,927.00	900,115.00	28,553,588.85	1,221,470.15
016	Washington H.S.	51,732,000.00	4,847,934.00	56,579,934.00	3,896,860.00	52,683,074.00		7,254,960.23	44,106,137.45	1,321,976.32
017	Westbury H.S.	40,006,000.00	6,257,598.00	46,263,598.00		46,263,598.00	124,773.44	4,327,543.24	40,382,140.05	1,429,141.27
019	Worthing H.S.	30,180,000.00	2,897,460.00	33,077,460.00	1,482,170.98	31,595,289.02		10,349,399.58	18,484,950.29	2,760,939.15
020	Yates H.S.	59,481,000.00	5,624,271.00	65,105,271.00	5,149,707.74	59,955,563.26	37,283.24	10,580,637.32	45,661,479.42	3,676,163.28
023	Sharpstown H.S.	54,944,000.00	7,889,585.00	62,833,585.00	4,221,638.00	58,611,947.00	10,830.00	3,463,378.80	50,518,662.37	4,619,075.83
024	Scarborough H.S.	12,566,000.00	2,077,625.00	14,643,625.00	281,461.00	14,362,164.00	3,430.21	885,270.06	11,199,789.43	2,273,674.30
025	Kinder HSVPA	80,178,000.00	8,167,860.00	88,345,860.00	3,871,764.00	84,474,096.00		15,884,897.86	64,233,776.03	4,355,422.11
026	DeBakey H.S.	64,512,000.00	2,582,806.00	67,094,806.00	6,945,149.58	60,149,656.42	25,790.48	816,388.16	58,365,930.37	941,547.41
033	Jordan H.S.	36,693,000.00	5,754,548.00	42,447,548.00	7,142,414.00	35,305,134.00	7,953.00	20,141,118.12	9,505,911.93	5,650,150.95
068	Tanglewood M.S.	14,825,000.00	262,740.00	15,087,740.00		15,087,740.00		114,176.32	13,622,202.52	1,351,361.16
075	Lawson M.S.	59,125,000.00	7,119,857.00	66,244,857.00	7,088,980.25	59,155,876.75	2,373,368.72	9,569,939.50	42,677,711.23	4,534,857.30
081	Sharpstown International	6,125,000.00	808,379.00	6,933,379.00	999,035.00	5,934,344.00	75.00	46,039.84	4,564,860.08	1,323,369.08
157	Garden Oaks K-8	26,678,000.00	4,195,956.00	30,873,956.00	2,085,145.00	28,788,811.00	46,628.14	8,137,851.91	18,823,532.65	1,780,798.30
215	Parker E.S.	29,485,000.00	3,525,043.00	33,010,043.00	4,668,106.00	28,341,937.00	60,342.13	4,482,097.96	23,594,917.20	204,579.71
218	Pilgrim K-8	7,989,000.00	960,481.00	8,949,481.00	1,598,840.00	7,350,641.00		2,069,314.44	5,127,249.97	154,076.59
256	Wharton Dual Language	35,603,000.00	3,621,734.00	39,224,734.00	6,573,227.34	32,651,506.66		13,176,352.41	19,020,737.58	454,416.67
259	Wilson Montessori	18,914,000.00	5,808,033.00	24,722,033.00	1,063,810.00	23,658,223.00	85,032.91	2,377,324.45	16,069,941.95	5,125,923.69
274	Askew E.S.	26,632,000.00	4,439,200.00	31,071,200.00	4,749,517.00	26,321,683.00	30,392.50	5,326,937.43	17,689,510.44	3,274,842.63
301	Eastwood Academy	10,875,000.00		10,875,000.00		10,875,000.00		2,168,805.14	8,474,844.10	231,350.76
308	North Houston EC H.S.	13,500,000.00		13,500,000.00		13,500,000.00	3,859.17	70,248.58	10,004,031.38	3,421,860.87
310	Sam Houston H.S.	101,428,000.00	17,175,958.00	118,603,958.00	18,380,687.00	100,223,271.00	667,019.35	45,352,046.91	40,469,682.34	13,734,522.40
458	Mickey Leland C.P.A.	28,675,000.00	1,651,044.00	30,326,044.00		30,326,044.00		119,284.49	27,031,244.37	3,175,515.14
460	Mandarin Immersion Magnet	32,161,000.00	3,610,582.00	35,771,582.00	1,531,119.00	34,240,463.00	3,622.50	582,666.93	32,038,328.36	1,615,845.21
463	Young Women's	27,159,000.00	4,009,189.00	31,168,189.00	1,674,269.00	29,493,920.00	7,419.34	2,066,532.61	26,113,754.88	1,306,213.17
483	M. White E.S.	23,417,000.00		23,417,000.00	0.00	23,417,000.00		266,539.28	22,541,184.55	609,276.17
486	S. Early College H.S.	13,500,000.00		13,500,000.00		13,500,000.00		102,839.74	9,726,989.03	3,670,171.23
660	School Athletics	44,675,000.00	3,734,769.00	48,409,769.00	5,169,941.40	43,239,827.60	5,800.00	354,658.79	41,438,631.98	1,440,736.83
	TOTAL CAMPUSES	1,681,940,000.00	206,262,100.00	1,888,202,100.00	179,915,420.76	1,708,286,679.24	3,709,679.69	383,334,063.77	1,109,367,626.68	211,875,309.10
1998	Middle School Restrooms	35,000,000.00		35,000,000.00		35,000,000.00		399,772.70	25,848,747.30	8,751,480.00
1997	District-wide Technology	100,000,000.00		100,000,000.00		100,000,000.00	440.00	1,010,669.16	34,200,027.94	64,788,862.90
1996	District-wide Safety & Security	17,293,000.00		17,293,000.00		17,293,000.00	20,472.19	736,606.73	16,293,819.52	242,101.56
1995	Land	55,767,000.00		55,767,000.00		55,767,000.00		11,605.10	46,892,395.60	8,862,999.30
1999	Program & Management Cost		6,187,863.00	6,187,863.00	179,915,420.76	186,103,283.76	23.39	8,206,184.05	78,900,307.36	98,996,768.96
	GRAND TOTAL	1,890,000,000.00	212,449,963.00	2,102,449,963.00		2,102,449,963.00	3,730,615.27	393,698,901.51	1,311,502,924.40	393,517,521.82



Worthing High School

Bond Communications Report

Holly Huffman

General Manager, Communications & Strategic Services for Business Operations

3200 Center St., 136A

Houston, Texas 77007

BondInfo@HoustonISD.org

EXECUTIVE SUMMARY

With the opening of nine new schools and additions during the first quarter, the Bond Communications team was heavily engaged in communications planning, opening-day coverage, and strategic follow-up to ensure parents, community members, and all HISD stakeholders were informed of district building successes.

Schools opening new facilities in January included Sharpstown, Scarborough, and North Forest high schools, and Robinson Elementary School. (The construction of North Forest High School and renovation of storm-damaged Robinson Elementary were overseen by the bond team, but not funded with bond dollars.) Also in January, Austin High School opened a temporary campus to house students for the duration of construction on their new building.

Additional openings took place in March after Spring Break, with Parker Elementary School opening its new building, and Westbury High School, Wilson Montessori, and Garden Oaks Montessori opening new additions.

Team members provided advance communications, including project updates and social media teaser videos, as well as comprehensive on-site, first-day coverage and follow-up social media and blog posts showing the buildings in use. The coverage resulted in an increased level of engagement – replies, retweets, likes – on the @Build_HISD twitter account.

The team continued to build on the success of the bond twitter account, providing project updates, photos, and videos through more than 320 tweets during the first quarter. These tweets earned more than 505,000 impressions during this time period, with 9,115 profile views and a followership increase of 65 percent from 250 to 412. Also during this period, the team tallied 1,300 link clicks (an average of 15 per day) 880 retweets (an average of 10 per day), and 2,400 likes (an average of 27 per day).

Team members also wrote and published 39 project updates that were posted on the HISD blog, the Build HISD website, and respective school project pages, and then further circulated to wider audiences via social media, the *Building Excellence* newsletter, and HISD's SchoolMessenger email listserv, which helps send school-specific project updates directly to the corresponding school community.

After completing a redesign of the bond project pages on the BuildHISD.org website last quarter, the team began tackling the development of project pages for construction projects at schools that are not bond funded to provide more easily accessible information on all construction projects across the district.

Also during the first quarter, the bond communications team led the planning, promotion, and execution of three milestone celebrations, including grand opening ceremonies for Kashmere High School and Codwell Elementary School (non-bond), and a wall signing celebration to mark construction progress at Northside High School.

Other grand opening celebrations/building dedications that are in the planning stages for the second quarter include Scarborough High School (April 26), Sharpstown High School (May 3), North Forest High School (May 4), Wisdom High School (May 15), and Furr High School (May 18).

Communications staff continue to attend Project Advisory Team meetings and internal strategy meetings as needed to assess communications needs, as well as provide guidance to district leadership and project managers on strategies to engage more effectively with stakeholders.

First Quarter bond communications by the numbers:

- 39 web stories/blog entries
- 4 press releases and media advisories
- 10 media mentions
- 17 videos
- 7 Project Advisory Team meetings
- 2 grand opening ceremonies (Kashmere High School and Codwell Elementary School; non-bond) and one wall signing celebration (Northside High School)
- 324 Twitter posts and 14 HISD Facebook posts highlighting bond activities
- 412 followers and 505,000 impressions on @Build_HISD
- Building Excellence, HISD's bond newsletter, was sent to more than 4,222 registered subscribers in February and March

RECENT ACCOMPLISHMENTS

MEDIA RELATIONS

Press releases/media advisories

01-07-18	HISD to open four new or renovated schools Jan. 8
01-08-18	Austin High School students move into temporary facility while new campus is constructed
01-22-18	New Kashmere HS to host grand opening celebration on Jan. 23
01-22-18	HISD receives highest honor in school architecture competition
02-07-18	HISD Board of Education to consider contract for rebuilding four Harvey-damaged schools
02-19-18	Milestone ceremonies planned to celebrate construction progress at Codwell ES, Northside HS
03-09-18	New elementary school, three building additions to formally open to students after Spring Break

HOUSTONISD.ORG COVERAGE**Web stories/blog entries**

01-08-18	New year, new building for Sharpstown HS
01-08-18	North Forest celebrates transition into new school with ceremonial walk
01-09-18	Robinson ES students return for 'fresh start' at home campus after post-Harvey renovations
01-09-18	Renovations wrap up at Scarborough HS
01-09-18	Austin HS students move into temporary facility while new campus is constructed
01-19-18	Condit ES receives highest honor in school architecture competition
01-23-18	Kashmere HS celebrates grand opening of renovated campus
01-29-18	Hundreds turn out to beautify grounds of Hilliard ES after Harvey
01-31-18	Eastwood Academy starts new year in new addition
02-01-18	Final phase of renovations underway at YWCPA
02-01-18	Construction on final phase of Worthing HS passes halfway mark
02-02-18	Milby HS awarded LEED Silver certification
02-05-18	Wharton DLA construction project nears halfway mark
02-06-18	Bond Oversight Committee tours North Forest HS, hears update on bond and building programs
02-08-18	HISD Board of Education approves contract for construction of four Harvey-damaged schools
02-09-18	Sam Houston MSTC construction makes steady progress
02-12-18	Construction on new Washington HS nearing completion
02-13-18	New Lamar HS to facilitate innovate approach to learning
02-13-18	HISD to hold subcontractor outreach session for rebuilding of Harvey-damaged schools
02-14-18	Parker ES to open new building after Spring Break
02-19-18	Personal stories exemplify how HISD is rebuilding, reimagining education
02-19-18	HISD Construction Services leads administration members on tour of new HSLJ
02-21-18	Codwell ES celebrates 40th anniversary at grand opening ceremony

02-22-18	Construction on new Madison HS reaches midway point
02-26-18	Jordan HS construction nearly one-third complete
03-01-18	Garden Oaks Montessori to finish out school year in new additions
03-01-18	Westbury HS moving into new building addition
03-01-18	Northside HS community celebrates construction progress, leaves mark on new school
03-01-18	Wilson Montessori prepares to welcome students to new building addition
03-05-18	One new school, three new additions to open this month
03-07-18	Kolter school community bids farewell to Harvey-damaged campus
03-08-18	New Kinder HSPVA construction making great progress
03-09-18	Pilgrim Academy addition set for completion next month
03-19-18	Parker ES students mark first day in new school
03-19-18	Westbury High School opens new addition ahead of schedule
03-19-18	Wilson Montessori opens doors to new building addition
03-19-18	Garden Oaks Montessori welcomes students into new facilities
03-23-18	New Lawson MS set for completion this summer
03-23-18	Yates HS Project Advisory Team tours new school

COMMUNITY AND SCHOOL OUTREACH

SCHOOL SUPPORT

- The Bond Communications Team spent much of the first quarter planning and implementing communications plans for the nine schools and new additions that opened.
- Team members worked with school principals to develop communications materials needed to ensure the transitions and school openings went smoothly. The team also produced social media teaser videos to generate excitement about the new facilities in advance of their openings and carried out extensive, on-site, first-day coverage — blog posts, project updates, photos, videos, and social media posts.

EVENTS

- The team helped coordinate and cover three milestone celebrations including grand opening ceremonies for Kashmere High School and Codwell Elementary School (non-bond), and a wall signing celebration to mark construction progress at Northside High School.

- The team coordinated and covered construction tours and walk-throughs for project advisory team members and trustees at High School for Law and Justice, Kinder HSPVA, Yates and Madison high schools, and Garden Oaks Montessori.

BOND OVERSIGHT COMMITTEE

- Produced, designed, edited, and distributed handbooks for members, and prepared meeting presentation.
- Planned and organized BOC tour of Wilson Montessori.

COMMUNITY ENGAGEMENT

- Continued monthly production of eNewsletter entitled Building Excellence, which is distributed to 4,222 subscribers. Continued to monitor and respond to requests for information and questions submitted to Bondinfo@HoustonISD.org.
- Produced and distributed fliers, callout scripts and letters for principals ahead of milestone events such as groundbreakings, wall signings, and grand openings and school transitions.
- Attended various Project Advisory Team meetings to assist with communication and provide coverage.

PRESS COVERAGE

01-08-18	CW39	New year, new look for four schools in Houston ISD
01-08-18	ABC13	4 HISD schools reopening today, including one damaged by Harvey
01-08-18	CW39	Austin High School students in HISD move to temporary facility during new campus construction
01-08-18	Houston Public Media	Robinson Elementary reopens for spring semester
01-08-18	KRPC	Four HISD schools reopen with new facilities
01-08-18	Houston Chronicle	Months after Harvey's flooding, students of one Houston ISD school back under one roof
01-22-18	Instant News Bellaire	Condit ES design wins top Texas school architecture award
01-23-18	KRPC	Kashmere High School holds ribbon-cutting ceremony After \$19M renovation complete
01-26-18	KRPC	Volunteers work on school hit by Harvey
02-08-18	KRPC	HISD approves contract for construction of four Harvey-damaged schools

02-27-18	Patch.com	New Barbara Jordan High coming along on schedule
----------	-----------	--------------------------------------------------

TWITTER

01-01-18	Cheers to a magical 2018! What better way to start the new year than with four new schools?? Can't wait until opening day on 1/8! #2012Bond #BuiltforLearning #NewSchools @iamsharpstown @ScarborHS @NorthForestHigh @Robinson_HISD
01-01-18	New year. New school. New memories. New @iamsharpstown! Opening Jan. 8! #2012Bond #BuiltforLearning @ddeleon10 @DanaArreola5 @erick_pruitt @hmfv1
01-02-18	Hey there @NorthForestHigh Bulldogs! What better way to begin the new year than with a new school! See you Jan. 8! @DrHenson2 @DanaArreola5 @erick_pruitt @RHONDAJN1 #2012Bond #BuiltforLearning
01-03-18	Take a look at that new front entry! Can't wait for @ScarborHS students to go back to school on 1/8 and see all the work that's been done over winter break! @trevinoSHS1 @stevengutierrez #2012Bond #BuildHISD #BuiltforLearning
01-04-18	Final inspections are underway & landscaping is being installed at new @EnergyHS! Project will be wrapping up in the Spring, with the school formally opening in August! #2012Bond #BuiltforLearning @LoriLambropoul1 @DarylSherman4 @NicoleMooreHisd @DDavilaHisd
01-05-18	Construction of the new addition at @PilgrimHISD is on track to wrap up this spring! Looking good so far! #BuildHISD #2012Bond @Dianac70 @DrBrownEDU @Anne4HISD @HeeryK12
01-06-18	Don't forget! We're just a couple weeks out from the grand opening of the new @KashmereHigh! Come tour the new school & help us celebrate all the great things going on at Kashmere! #2012Bond #BuiltforLearning @Supe_Schools @RHONDAJN1
01-06-18	Looking marvelous over at the new @madisonmarlins! Structural steel & tilt walls are being erected & roof installation is beginning! #2012Bond #BuildHISD @erick_pruitt @Wandaful1913 @HeeryK12 @SatPonInc
01-07-18	Don't forget to set your alarm clocks tonight because the spring semester starts tomorrow! And if you go to @NorthForestHigh, @iamsharpstown, @ScarborHS, or @Robinson_HISD, you're in for a real treat! First day in your new school!
01-07-18	Looking good, @LawsonMS_HISD! Won't be long and the new school will be done! Construction should wrap up in Q2 2018! #2012Bond #BuildHISD @erick_pruitt @Wandaful1913

01-08-18	Faculty at @NorthForestHigh are prepping to welcome students to their new digs. Happy New Year Bulldogs! #BuildingExcellence #2012Bond
01-08-18	New year, new school for @iamsharpstown Apollos! Lots of excitement today as students walk from the old building to the new! @hmfv1 @ddeleon10 @DanaArreola5 @erick_pruitt
01-08-18	Scenes from opening day at new Sharpstown High School! @iamsharpstown @hmfv1 @ddeleon10 @DanaArreola5 @erick_pruitt
01-08-18	Excited students enter new Sharpstown HS for the first time today! #BuildHISD @iamsharpstown @hmfv1 @DanaArreola5 @erick_pruitt
01-08-18	Sharpstown HS students are quickly learning their way around their beautiful new school this morning #BuiltForLearning #BuildHISD @iamsharpstown @hmfv1 @DanaArreola5 @erick_pruitt @ddeleon10
01-08-18	Good morning from the new @ScarborHS! These Spartans are excited to be back & ready to learn in their new facility! #BuiltforLearning #2012Bond #BuildHISD @trevinoSHS1
01-08-18	Spartans in the @ScarborHS percussion class are already making great use of the new band hall! Sounds great!
01-08-18	Renovations at @ScarborHS include a 13,000 sq ft addition for band, choir & JROTC, a new welcome center, & major upgrades throughout the existing building. Looking good, Spartans! #BuiltforLearning #BuildHISD #2012Bond @trevinoSHS1
01-08-18	Hallways are bustling at the new @ScarborHS! The new commons & snack bar space is fantastic! #BuiltforLearning #2012Bond #BuildHISD @trevinoSHS1
01-08-18	Didn't take long for @ScarborHS JROTC students to get settled into their new digs! Nice windows! #JROTCcreed #BuiltforLearning #BuildHISD #2012Bond @trevinoSHS1
01-08-18	It feels soooooo good to be back! @NorthForestHigh students and staff did a ceremonious walk led by Principal @DrHenson2 from the old school to the new. You better werkkkk Bulldogs! @DanaArreola5 @erick_pruitt @RhondaForHISD #BuildingExcellence #HISD
01-08-18	Congrats @NorthForestHigh! Can't wait to see all the teaching and learning going on inside your new school! #BuiltforLearning #BuildHISD
01-08-18	Great first day back at @AustinMustangs! Kudos on a smooth transition into your temporary digs! Construction on your new school starts soon! Can't wait to see it come together! #2012Bond #BuildHISD @GuerreSteve @DDavilaHisd @DrJlarredondo
01-08-18	Our pleasure! All students deserve a safe, comfortable, modern space to learn - even if the space is just temporary! #WhateverItTakes #CountdownToConstruction #2012Bond #BuildHISD @GuerreSteve @AustinMustangs

01-08-18	Can't get enough of these first day back photos at @AustinMustangs! That's a lot of learning going on inside that temporary campus! Construction on new school starts soon! #BuildHISD #2012Bond @GuerreSteve @Drjlarredondo @DDavilaHisd @HeeryK12 @EROArchitects
01-08-18	If you haven't seen the new @iamsharpstown, you're missing out! See how students celebrated their first day in their new school #2012Bond #BuiltForLearning @ddeleon10 @DanaArreola5 @erick_pruitt @hmfv1
01-08-18	Looking good, @PrincipalLira & @EastwoodBoxers! You're almost done! Can't wait for your project to wrap up this quarter! Enjoy the new spaces! #BuiltforLearning #2012Bond @dacrowe1227 @Drjlarredondo @DDavilaHisd
01-08-18	As a @iamsharpstown Alumni & employee. I'm excited for the new school and students! Way to go!!! (@Clothedon)
01-08-18	Super excited for students, teachers, staff and the Sharpstown community for the opening of the new Sharpstown High School! @iamsharpstown @TeamHISD @HISD_Supe @ddeleon10 @erick_pruitt @DanaArreola5 @GeneforTexas (@hmfv1)
01-08-18	Sharpstown High School one of several new or renovated @HoustonISD campuses that opened today. Follow this account for district-wide pics: #khou11 (@JMilesKHOU)
01-08-18	Welcome back Bulldogs to 2018 and our new building! Huge shout out to our alumni for greeting our students as they enter the building for the first time. (@NorthForestHigh)
01-08-18	What a great way to start 2018. Thank you @Build_HISD for the amazing work you've done to our campus. Let's goooo Spartans #2012Bond #SpartanNationshs (@trevinoSHS1)
01-08-18	What an excellent first day back in our new building! Thank you all for a successful start to the spring semester! @Build_HISD (@EastwoodBoxers)
01-08-18	Thank you @Build_HISD for making this happen over the holidays, ya rock!! @HISD_Supe @Busby_isms (@DDavilaHisd)
01-09-18	"People don't realize how impactful it is to have a bldg that is safe & comfortable for learning" - @ScarborHS Principal @trevinoSHS1. The \$12.6M #2012Bond project wrapped up over break. #BuiltforLearning @stevengut1errez
01-09-18	Love seeing @Robinson_HISD kiddos & @Principal_Hohos back at their home school! Kudos to #HISD Construction Svcs for getting the school ready in record time! New classrooms look amazing & these kids look ready to learn! #HomeSweetHome #HISDStrong #BuildHISD #BuiltForLearning

01-09-18	So glad we could get @Robinson_HISD back home so quickly! And give them a facelift to boot! #HomeSweetHome #BuildHISD #HISDStrong #BuiltForLearning
01-09-18	Check out the video to get a look at the amazing new spaces at @ScarborHS! Now this is a makeover! #BuiltForLearning #2012Bond #BuildHISD @trevinoSHS1 @stevengutierrez
01-10-18	Excited to see @AustinMustangs settling into their temp space! We'd love to come hear the @SFA_SonicBoom play sometime! #finearts #sonicboom #2012Bond #BuildHISD
01-10-18	You're all superheroes in our book! Hope your modern, new learning spaces help you building upon all your student success! #21stCenturyLearning #BuiltforLearning #2012Bond @FurrHS @DrJlarredondo
01-10-18	Have you seen @SFA_SonicBoom in action? Check them out as they lead the MLK Youth Parade at 12 p.m. on Saturday in Midtown or at MLK Battle of the Bands Sunday at 4 p.m. at @AldineISD's WW Thorne Stadium! Way to go, @AustinMustangs! @ParadeHouston #finearts #HISD #2012Bond
01-11-18	Love that gym at the new @NorthForestHigh!
01-12-18	That is a great looking learning commons in the new classroom wing at @WorthingColts1! Can hardly wait until the end of this year to see what the rest of the building will look like! #2012Bond #BuildHISD #BuiltforLearning @Supe_Schools
01-12-18	It's great to see how flexible these spaces are at @YWCPAHISD. They're not just for student learning! #ParentEngagement #2012Bond #BuiltforLearning
01-18-18	Congrats @ConditES! New school design wins prestigious Caudill Award for its "transformational learning environment." #ConditProud #2012Bond #BuiltforLearning @VLKArchitects @HeeryK12 @texasbuckeye @DrBrownEDU @Busby_isms @DSanders247 @DanBArch
01-18-18	Lookin' good, @iamsharpstown! Can't wait to see the @Sharpstownband making music in that great space! #BuiltforLearning #2012Bond @ddeleon10 @DanaArreola5 @erick_pruitt
01-18-18	Become a part of history and join us at the @KashmereHigh grand opening!!
01-18-18	#BuiltforLearning #ConditProud
01-18-18	Join us!! #2012Bond #BuildHISD #celebrategoodtimes (@Lesette21)

01-19-18	Productive prep meeting today at @NorthForestHigh. The Bulldogs will host the Q4 2017 Bond Oversight Committee Mtg on Feb. 6. Can't wait to show off this building! @DrHenson2 @erick_pruitt @DanBArchit #BuiltforLearning #BuildHISD #BOC
01-19-18	T minus four days until the grand opening ceremony @KashmereHigh !!
01-19-18	VLK's @ConditES at @HoustonISD Earns Caudill Award (@VLKArchitects)
01-20-18	Small group learning in action at @NorthForestHigh!! Love it! #Bulldogs #BuiltforLearning #BuildHISD
01-20-18	#HISD #BuiltforLearning #DreamBig
01-20-18	It's not too late to make the date! Join us for the @KashmereHigh grand opening ceremony!
01-21-18	Are you ready Rams? Just a couple more days before your grand opening ceremony!! @KashmereHigh #2012Bond #BuildHISD #celebratehistory
01-22-18	Amazing #progress on an amazing space! #2012Bond #BuildHISD @HSPVA @DrAatPVA @SSODiegoLinares @stevengut1errez
01-22-18	Who says learning only happens during regular school hours? #BuiltforLearning #AllTheTime #21stCentury #2012Bond #BuildHISD @ScarborHS @trevinoSHS1 @stevengut1errez
01-22-18	In less than 24 hours we'll be here!! Hope to see you all there! @KashmereHigh #2012Bond #celebrategoodtimes
01-22-18	Celebrity sighting at @NorthForestHigh! I bet @NickSabanUofA was super impressed with the new school and all your smart, talented bulldogs! Hope you showed him your new indoor track! #BuildHISD #BuiltforLearning #RollTide @UofAlabama @DrHenson2 @DanaArreola5 @erick_pruitt
01-22-18	Wow! I got to tour the new Kinder @HSPVA today, and it is amazing! Lots of construction progress to report - bldg has perm power now, walls & interior finishes are going up. Students are going to love it! @DrAatPVA @Build_HISD @McCarthyBuild @gensler_design #BuildHISD #2012Bond (@rkiest)
01-23-18	See the incredible story of @HoustonISD's @ConditES #CaudillAwardWinner #TASA18 (@VLKArchitects)
01-23-18	Watch the @HISD_KashmereHS ribbon-cutting ceremony live now on our Facebook page! #2012bond #buildingHISD #builtforlearning (@HoustonISD)
01-23-18	The countdown is on! 30 minutes until the celebration begins at @KashmereHigh! It's a great day for a grand opening! #BuildHISD #2012Bond #BuiltforLearning @RHONDAJN1 @Supe_Schools.

01-23-18	Lots of good news coming out of @KashmereHigh today! Thanks for coming out @KPRC2! #2012Bond #BuiltforLearning #BuildHISD
01-23-18	Can't make the @KashmereHigh grand opening? Watch live now
01-23-18	Bright lights, open spaces & modernized upgrades in new @KashmereHigh inspire creativity & interest & spark learning - #HISD Trustee @RHONDAJN1 #BuildHISD #2012Bond #BuiltforLearning @Supe_Schools
01-23-18	#HISD Trustee & Alumna @Wandaful1913: @KashmereHigh launched who I am today. I'm so honored to say I am a Ram! #2012Bond #BuildHISD #BuiltforLearning
01-23-18	@KashmereHigh Principal Blackwell recognizes the family of Conrad O. Johnson, former band director who led the Kashmere Stage Band to national acclaim. #GoRams #2012Bond #BuiltforLearning #BuildHISD @Supe_Schools @RHONDAJN1
01-23-18	It's official! The ribbon has been cut! Congrats on the new learning spaces, @KashmereHigh! Very well deserved! @RHONDAJN1 @Supe_Schools #2012Bond #BuildHISD #BuiltforLearning
01-23-18	What an amazing crowd of very important folks, all gathered to show love & support for @KashmereHigh. #2012Bond #BuildHISD #GrandOpening #Gratitude @RHONDAJN1 @Wandaful1913 @Anne4HISD @hmfv1 @sueforhisd @HISD_Supe @Busby_isms @JacksonLeeTX18 @RepHaroldDutton @DavisDistrictB
01-23-18	Way to go, @HISDBusinessOps COO @Busby_isms! We're proud to be part of this amazing team! #HISDStrong #BuildHISD #HardWorkPaysOff #TeamWorkMakesTheDreamWork @hisdpolice @hisd_facilities @HISDSchoolBus @HISDNutri @TeamHISD
01-23-18	@ConditES awarded the highest honor in Exhibit of School Architecture competition #BuildHISD #2012Bond @Build_HISD (@HoustonISD)
01-23-18	Also: Houston ISD mulls a school bond of at least \$1.2 billion, which could go to voters as early as November. Admin predicts it could bring a 3-7 cent tax increase per \$100 in taxable value. Elementary, middle schools would get lift. (@ChronJacob)
01-23-18	Thank you Congresswoman Sheila Jackson Lee for your support for Kashmere HS at our ribbon cutting today! @HoustonISD (@Anne4HISD)
01-23-18	HISD Board, trustees and superintendent believe and will continue to invest in Kashmere HS! #ribboncutting #buildinglegacies (@Supe_Schools)
01-23-18	Gratitude to Conrad Johnson and family for building the infamous Thundersoul legacy at Kashmere HS! (@Supe_Schools)

01-23-18	@HoustonISD renovated Kashmere HS as part of HISD's voter-approved 2012 Bond Program. #abc13eyewitness (@TomAbrahams13)
01-24-18	Amazing changes to the new school. We got to walk the bridge!!! @HSLawAndJustice @TeamHISD @DrJlarredondo (@cmosteit)
01-24-18	Great crowd of @KolterSchool parents as they have gathered at @pinoakms to discuss upcoming construction plans for their school. @jmdickins @Busby_isms @DSanders247 @apeeples01
01-24-18	A few words from District V trustee @sueforhisd as she introduces herself to the @KolterSchool community. This district is so excited to have you!
01-24-18	"Abatement of the old @KolterSchool is expected to begin in March with the new building to open in January 2020." @Busby_isms #BuildHISD
01-24-18	Wow! What a view! Great progress on the new @HSLawAndJustice! Work is wrapping up this quarter! #2012Bond #BuildHISD @DrJlarredondo @DDavilaHisd
01-24-18	At @MilbyHighSch, culinary arts students go to class in an on-site, working restaurant. How about that for real-world experience?? #2012Bond #BuiltforLearning #21stCentury @PrincipalDMilby @erick_pruitt @LiraSerg
01-24-18	Construction of a new school begins long before crews arrive on site. It all starts here, in a small conference room w/ lots of very talented folks. Brainstorming session underway! @KolterSchool @Braeburn_HISD @Mitchell_Elem @ScarboroughElem @PflugerArch
01-24-18	Here at @MilbyHighSch to do some filming of their UH-MAZING kitchen and dining space. Can we say YUM??! #2012Bond #BuildHISD #hungry (@Lesette21)
01-24-18	State-of-the-art kitchen equipment = Pulled BBQ pork sandwiches, mac & cheese, and baked beans. @MilbyHighSch #professionalstastetester #2012Bond #BuildHISD #lunchtime (@Lesette21)
01-24-18	What a day!! Congratulations again @KashmereHigh on your awesome upgrades! (@Lesette21)
01-26-18	Great brainstorming session w/ @PrincipalLove at @CodwellIES. You HAVE to see this school. Completely gutted, renovated & reconfigured. Mark your calendars & come celebrate the #GrandOpening w/ us at 8:30 a.m. on 2/21/18. #BuildHISD #BuiltforLearning #celebration
01-26-18	PAT members are touring new @GardenOaksMont this morning! They're excited to move in to Phase 1 buildings over spring break. @PollockLindsey #2012Bond #BuiltforLearning @balfourbeatty

- 01-26-18** A few more photos of @GardenOaksMont PAT sneak peek of new facility today. The countdown is on to a spring break move! @PollockLindsey #2012Bond #BuildHISD @c_berger29 @stevengut1errez
-
- 01-26-18** A big thank you to the 650 volunteers from @GoNumotion as they are hard at work at the newly renovated @Hilliard_ES beautifying the campus with lush landscaping and asphalt games such as hopscotch and tic-tac-toe! @RhondaForHISD @Busby_isms @RecoveryHouston #amazing
-
- 01-26-18** But wait.....there's MORE! What's a great way to complement a beautiful exterior? A shiny new interior! Renovations to the new @Hilliard_ES are set to wrap up during Q1 of this year! @RhondaForHISD @Busby_isms #BuildHISD #BuiltforLearning #perfection
-
- 01-26-18** Check you out @Hilliard_ES !!! #BuildHISD #BuiltforLearning (@Lesette21)
-
- 01-28-18** My mind is completely blown how quickly the new @btw_hsep has come together! Construction is set to wrap up Q1!!! @RhondaForHISD @_cphilli2 #BuildHISD #BuiltforLearning #beautiful (@Lesette21)
-
- 01-29-18** Did you miss the @KashmereHigh #GrandOpening last week? Get a full recap & sneak peek inside the school right here #2012Bond #BuiltforLearning #GoRams @RHONDAJN1 @Wandaful1913 @Supe_Schools
-
- 01-29-18** I don't know about you, but Monday is making us feel more motivated than ever! Construction on the new @LawsonMS_HISD is set to wrap during 2Q of this year! #greatprogress #BuiltforLearning @RonaSimmons27 @erick_pruitt @Wandaful1913 @HK_Architects @TurnerSouthTX
-
- 01-29-18** Looks like we've found our next crop of architects at @ScarboroughElem! Way to go, first graders! Nice work! #BuildHISD #HISDStrong #FutureSchoolDesigners #HurricaneHarvey #Rebuild @HISDNorth @RHONDAJN1
-
- 01-29-18** Amazing progress has been made on the new @BJHSC_HISD. The building is slated for completion Q4 of this year! #speechless #BuiltforLearning #BuildingtheFuture @RhondaForHISD @JRMcAlpine @alundyja1 @HISDNorth @HeeryK12 @CadenceMcShane @CorganInc
-
- 01-29-18** Read about how hundreds of people from across the country helped @Hilliard_ES after #Harvey. #HISD (@Lesette21)
-
- 01-29-18** Great to see @HoustonISD's @ConditES recognized today for the Caudill Award at the @tasanet General Session! #TASA18 (@VLKArchitects)
-

01-30-18	MY HOW TIME FLIES!!!@madisonmarlins #awesome (@Lesette21)
01-30-18	Those purple tinted windows look pretty cool! @northside_hs #purpleisyourcolor (@Lesette21)
01-30-18	No one can rock purple quite the way you do @northside_hs! Aren't you excited for your Q4 completion date?! #BuiltforLearning #NorthsidePride @santos4hisd @HeeryK12 @SatPonInc @BayIBIGroup
01-30-18	Trust the process @madisonmarlins #transformationtuesday #progress #mindblown #startedfromthebottom @Wandaful1913 @HeeryK12 @SatPonInc
01-30-18	Click on the link below to find out about the @Hilliard_ES beautification project. @RhondaForHISD @Busby_isms @GoNuMotion @RecoveryHouston #teamworkmakesthedreamwork #BuiltforLearning #BuildingExcellence
01-30-18	Congratulations to @Busby_isms & @HISD_Supe for proudly representing @HoustonISD & @ConditES during Caudill Awards Presentation #TASA18 #Austin #InspiringLeaders (@SuarezRebecca)
01-30-18	We are beyond proud of these three and the entire project team for @HoustonISD's @ConditES! Congratulations on earning the Caudill Award! #TASA18 (@VLKArchitects)
01-31-18	#SouthsideTakeover (@Lesette21)
01-31-18	The countdown is on for Wilson Montessori! Move-in to this beautiful new addition will happen over spring break. We think they're going to love it! @Wilson_HISD @WilsonMontPTO @Anne4HISD @stevengutierrez @Jason_Bernal1 #BuildHISD #2012Bond #BuiltForLearning
01-31-18	We're proud of our inspirational leaders and of the beautiful new @ConditES #BuiltForLearning #2012Bond #BuildHISD
01-31-18	Awesome!
01-31-18	We love what you've done with the place, @WHS_HUSKIES! This new addition at Westbury HS is nearing completion & set for a spring break move in. (Add'l campus construction & site work will continue into Q1 2019.) #2012BOND @erick_pruitt @Wandaful1913 @RonaSimmons27 @SatPonInc
01-31-18	Great turnout here at the Bond Office for Workshop Wednesday! This month's presentation will focus on doing business with HISD. Look out for the story tomorrow! #HISDSupplierDiversity
01-31-18	Project Advisory Team for @WorthingColts1 met today to hear an update on building progress. Construction is now more than halfway complete. @Wandaful1913 #2012Bond

- 02-01-18** Congrats @MilbyHighSch on @USGBC #LEEDSilver status! LEED schools boost student health, test scores & faculty retention w/ better acoustics, lighting, temp control & air quality. And they cost less to operate! #2012Bond #BuiltForLearning #GreenSchools @KirkseyNews @HeeryK12
-
- 02-01-18** Loving the new digs @EastwoodBoxers! And looking forward to completion of your next building addition in the spring! @DDavilaHisd @PrincipalLira @DrJlarredondo @dacrowe1227 #2012Bond
-
- 02-01-18** Lots of construction activity is happening at @Parker_hisd The beautiful new bldg will house the school's top notch music programs & provide 21st century learning spaces for students. Here's a look inside! @Wandaful1913 @DrBrownEDU @delesa1994 #BuiltForLearning #2012Bond
-
- 02-01-18** Check out the latest project update on @YWCPAHISD! Construction is in its final phase with work to wrap up this summer! @april_williams4 @JonesJolanda @HeeryK12 @SatPonInc @NatexArchitects #2012Bond #BuiltforLearning
-
- 02-01-18** The new @HSLawAndJustice will have some pretty amazing features: state-of-the-art forensic labs, mock courtroom, massive learning stairs, a cool catwalk bridge overlooking the commons area, and impressive views #2012Bond #BuiltForLearning @cmosteit @DDavilaHisd @DrJlarredondo
-
- 02-01-18** HISD's Supplier Diversity team teach local business owners and vendors how to fill out the M/WBE participation report.
-
- 02-02-18** Next #HISD Bond Oversight Committee mtg is 8:30 a.m. on 2/6. Lots of prep work underway! Can't wait to show off the new @NorthForestHigh! #BulldogPride #BuiltForLearning #BOC @DrHenson2 @Busby_isms @DSanders247 @DanBArcht @apeeples01
-
- 02-02-18** Alllll rise!! @HSLawAndJustice #BuiltForLearning #excited (@Lesette21)
-
- 02-02-18** Most definitely one of our great schools to showcase!!! @NorthForestHigh (@Lesette21)
-
- 02-03-18** Mark your calendars because @CodwellIES is throwing a party! Join us at 8:30 a.m. on 2/21/18 for a #grandopening to celebrate the complete renovation of their school. #BuiltforLearning #BuildHISD @PrincipalLove @NicoleMooreHisd @Busby_isms @JonesJolanda
-
- 02-04-18** Are you ready to leave your mark on @northside_hs? Join us at 5 p.m. on 2/28/18 for a #WallSigning Ceremony to celebrate the construction progress made on the new campus! #2012Bond #BuildHISD @cgonzal456 @DiegoLinage1 @stevengut1errez @Santos4hisd @Busby_isms
-

02-05-18	Construction on the new @WhartonDual is nearly halfway complete! Check out the project update! http://bit.ly/2nL319q @DDavilaHisd @HeeryK12 #BuiltforLearning #progress #exciting
02-06-18	BOC committee members and attendees are just minutes away from touring the brand new @NorthForestHigh!! Top of the morning Bulldogs!! @Busby_isms @DrHenson2 @RhondaForHISD @apeeples01 @DSanders247 #BuiltforLearning #HISD
02-06-18	First stop is at the main entryway and dining commons area. Check out those gorgeous floor-to-ceiling windows. @Busby_isms @DrHenson2 @RhondaForHISD @DSanders247 @apeeples01 @NorthForestHigh #BuiltforLearning #gorgeous #elbosque
02-06-18	Just right upstairs is an extension of the dining area complete with a weight room and the ONLY indoor track in the district. @NorthForestHigh @Busby_isms @DrHenson2 @DSanders247 @RhondaForHISD #BuiltforLearning #goals #elbosque
02-06-18	Check out this CTE wing area. @NorthForestHigh @RhondaForHISD @DrHenson2 @apeeples01 @Busby_isms @DSanders247 #BuiltforLearning
02-06-18	Class is now in session! BOC committee members will spend the duration of the meeting sitting in the new modern, flexible furniture! @Busby_isms @RhondaForHISD @DSanders247 @apeeples01 @NorthForestHigh #BuiltforLearning #popquizafter #elbosque
02-06-18	Wow!!!! I feel like the groundbreaking was just yesterday! #unbelievableprogress #BuiltforLearning (@Lesette21)
02-06-18	Fun times at today's tour of the new @NorthForestHigh with the Bond Oversight Committee. Looking good Bulldogs!! #BuiltforLearning (@Lesette21)
02-06-18	Great Bond Oversight Committee meeting & school tour this morning at the new @NorthForestHigh! Thanks to Principal @DrHenson2 & all the Bulldogs for being such great hosts! #BuiltforLearning #BuildHISD #BulldogPride #BOC (@hf Huffman)
02-07-18	#HISD's Bond Oversight Committee held their quarterly meeting at @NorthForestHigh this week and got a firsthand look at the newly opened facility #21stCenturySchool #BuildHISD #BuiltForLearning @DrHenson2 @RHONDAJN1 @HoustonISD @Busby_isms
02-08-18	Looking good at @WhartonDual! This is going to be an amazing school!
02-08-18	@LamarHS Project Advisory Team & SDMC are hearing a project update on their #2012Bond construction today. Lots of progress visible every day! #BuildHISD @LamarPTO @James_McSwain @stevengutierrez @Anne4HISD

02-08-18	The 4 schools ravaged by Hurricane Harvey have been approved to be rebuilt by our CMAR, Satterfield & Pontikes. Can't wait to see the kids of those neighborhood schools walk in, in 2020! @Busby_isms
02-08-18	Have you heard? Construction on our new Wharton campus is almost 50% complete!... (@WhartonDual)
02-09-18	#BuildHISD #2012Bond #Progress
02-09-18	Great news! #HISD trustees approved the construction contract to rebuild 4 schools damaged by #Harvey. Schools could be rebuilt & open by 2020! #BuildHISD #HISDStrong @ScarboroughElem @Mitchell_Elem @KolterSchool @Braeburn_HISD @Busby_isms @RHONDAJN1 @LiraSerg @DeigaardS
02-09-18	#HISD Board of Education approves contract for construction of four Harvey-damaged schools! @Busby_isms @KolterSchool @ScarboroughElem @Mitchell_Elem @Braeburn_HISD @SatPonInc #BuiltforLearning
02-09-18	Construction on the new Sam Houston MSTC @SHMSTC is now 40% complete! #2012Bond #BuildHISD #21stCenturySchool @Al_Lee_Summers @Santos4hisd @HISDNorth @HoustonISD
02-09-18	This....is....HUGE. Looking forward to getting the word out about these projects!! #HISDStrong (@Lesette21)
02-12-18	We're in the home stretch @btw_hsep!!!!!! Construction will be wrapping up Q1! @RhondaForHISD @_cphilli2 @FanningHowey #BuiltforLearning
02-12-18	Just a good word on this good Monday afternoon! Cheers to a great rest of the week! #MondayMotivation #2012Bond #BuiltforLearning #BuildingtheFuture
02-12-18	That aerial photo is AMAZING! #BuildHISD #BuiltforLearning (@Lesette21)
02-13-18	The new @LamarHS is designed to facilitate the school's innovative approach to teaching and learning #21stCenturySchools #2012Bond #BuiltForLearning #BuildHISD @James_McSwain @LamarPTO @Anne4HISD @HoustonISD
02-13-18	Gearing up for @ScarboroughElem community meeting. 15 minutes and counting. #BuiltforLearning
02-13-18	"Students are expected to move into the new @ScarboroughElem by Jan. 2020." - HISD COO Brian Busby @Busby_isms @RhondaForHISD @DSanders247 @SatPonInc @HISDNorth #BuiltforLearning
02-14-18	"We're going to have a beautiful building." - @ScarboroughElem Principal Miriam Medina @Busby_isms @DSanders247 @SatPonInc @RhondaForHISD #BuiltforLearning

02-14-18	"Your kids will get a great new facility just for them." - HISD Board President Rhonda Skillern-Jones @RhondaForHISD @ScarboroughElem @Busby_isms @SatPonInc @DSanders247 #BuiltforLearning
02-14-18	Calling all minority-and women-owned businesses! Interested in becoming a subcontractor for our four Harvey rebuild schools? Check out info on HISD's Business Assistance Supplier Diversity outreach event happening this Friday!
02-14-18	YES please!!! Enjoy a walk-through of one of our 2012 Bond schools that opened for the 2017-2018 school year! Click on the link below! #BuiltforLearning #2012Bond #AugmentedReality
02-14-18	Who doesn't like money?! Follow @HISD_MWBE to get the latest info on upcoming events and workshops targeted specifically to Minority-and Women-Owned Business Enterprises! #networking
02-14-18	How about a tour of Milby High School? (@MilbyHighSch)
02-15-18	Students and staff at @Parker_hisd will find themselves in their new building right after Spring Break! Read the full story here! @Busby_isms @Wandaful1913 @DSanders247 #2012Bond #BuiltforLearning
02-15-18	Impressive! Lots of very talented kids from #2012Bond schools showing off their #21stcenturyskills today at #HISDSOTS! #BuildHISD #BuiltforLearning @EnergyIHS @MilbyHighSch @SouthEarly @YWCPAHISD
02-15-18	This cool #hisdots photo booth was designed & built by @WaltripRam students using a computer drawing program & laser cutter #21stcenturyskills @HISD_Supe @RhondaForHISD @colibri713 @HoustonISD
02-15-18	Way to go @YWCPAHISD! These smart girls coded Now, a robot that helped them introduce the @HISD_Supe at #HISDSOTS! #2012Bond #BuildHISD #BuiltforLearning @HoustonISD
02-15-18	@HISD_Supe gives a shoutout to the #2012Bond, noting that half of all projects are now complete & open to students! This school year alone, #HISD has opened 13 schools, & will wrap up construction of almost 20 more by end of 2018. #majormilestone #BuildHISD @HoustonISD
02-15-18	Have you been inside the new @NorthForestHigh? @HISD_Supe just grabbed a pair of VR goggles and gave everyone at #HISDSOTS a sneak peak of the school, which just opened last month! Looking good, Bulldogs! #BuildHISD #BuiltforLearning #21stcentury @HoustonISD @DrHenson2
02-15-18	Congrats @ConditES! I guess this makes it officially official! #2012Bond #BuiltforLearning

02-15-18	The plaque is up, it's official! #conditproud @VLKArchitects @Build_HISD (@ConditES)
02-15-18	We couldn't have said it better! We are so excited for @Parker_hisd! Looking forward to being there with students and staff on the first day!
02-15-18	Thanks to the #2012Bond, we have new schools that are bright, open, and modern. They foster project-based learning and collaboration among students — just the skills you need to be successful in college and the workforce. #HISDSOTS (@HoustonISD)
02-15-18	Gracias al programa de bonos #2012Bond, tenemos escuelas nuevas, iluminadas, abiertas y modernas que favorecen el aprendizaje basado en proyectos y la colaboración -dos de las habilidades necesarias para el éxito en la universidad y el mercado laboral. #HISDSOTS (@HoustonISD)
02-15-18	Vamos a mitad de camino del #2012Bond. Eso significa que la mitad de los proyectos están terminados y esas escuelas han abierto. Desde septiembre, hemos abierto 13 escuelas y prevemos terminar el trabajo en 20 escuelas más para fines de 2018, dice @HISD_Supe. #HISDSOTS (@HISDEspanol)
02-15-18	We're halfway through the #2012Bond. That means half of all projects have been completed and opened to students. We've opened 13 schools since September, and we're on track to finish almost 20 more by the end of 2018, @HISD_Supe says. #HISDSOTS (@HoustonISD)
02-15-18	@HISD_Supe guía a la audiencia en una gira virtual de una de las escuelas del programa de bonos #2012Bond. #HISDSOTS (@HISDEspanol)
02-15-18	@HISD_Supe is leading the audience in a virtual reality tour of one of the #2012Bond campuses. #HISDSOTS (@HoustonISD)
02-15-18	I am so Happy for the parents students and faculty of Parker ES. @Wandaful1913
02-18-18	Let the church say YEAHHHHH! #2012Bond #BuildingtheFuture #teamworkmakesthedreamwork (@Lesette21)
02-18-18	I know this move-in has been long awaited, but I'm so thrilled for the Parker community! #2012Bond #BuiltforLearning (@Lesette21)
02-19-18	What are you looking to achieve on this wonderful Monday?!! #MondayMotivation #teamworkmakesthedreamwork #BuildingtheFuture #thegrindbeginsnow
02-19-18	Construction team is taking @DDavilaHisd on a tour of the new @HSLawAndJustice! @DSanders247 @apeeples01 @DanBArcht @Busby_isms @Drjlarredondo @balfourbeatty @michael_love2 @Eugene_Salazar5 #2012Bond #BuiltforLearning #workfieldtrips

02-19-18	Forensic labs, a cafetorium, and a courtroom are just some of the spaces that will be featured at the new @HSLawAndJustice!! #2012Bond #BuiltforLearning #checkoutthatview @DDavilaHisd @Busby_isms @DSanders247 @apeoples01 @DanBArcht @Drjlarredondo @balfourbeatty
02-19-18	I'm still in awe of the new @HSLawAndJustice. Ladies and gentlemen this is the future!! #2012Bond #BuiltforLearning #views (@Lesette21)
02-20-18	District administrators tour the new @HSLawAndJustice! Check out the latest project update! @DDavilaHisd @busby_isms @DSanders247 @danbarcht @apeoples01 #2012Bond #BuiltforLearning #allrise
02-20-18	#TuesdayThoughts #TuesdayMotivation #goals #StayFocused
02-20-18	Just a few more minutes before the @BJHSC_HISD PAT meeting begins!! Excited to hear about the progress! #2012Bond #BuiltforLearning @JRMcAlpine @RhondaForHISD
02-20-18	The progress is absolutely AMAZING over at @BJHSC_HISD!! Steel framing is already underway! @JRMcAlpine @CadenceMcShane @CorganInc #2012Bond #BuiltforLearning #progress
02-21-18	Truly enjoyed our collaboration with Principal Love @CodwellIES. Today we celebrate the Grand Opening and 40th Anniversary. #BuildHISD #BuiltForLearning @HoustonISD (@STSbrandTX)
02-21-18	We're one hour away from the grand opening and 40th anniversary celebration of @CodwellIES Join us! Their beautiful new building is #BuiltForLearning #BuildHISD @PrincipalLove @GrenitaLathan @NicoleMooreHisd @HoustonISD
02-21-18	Grand opening celebration kicks off with performance by @CodwellIES violin ensemble #FineArtsMagnet #BuildHISD @PrincipalLove @JonesJolanda @GrenitaLathan @NicoleMooreHisd @Busby_isms
02-21-18	Thanks to @SterlingRaider NJROTC for supporting @CodwellIES with posting of colors at today's grand opening celebration #NeighborhoodSchools #BuildHISD @JonesJolanda @PrincipalLove
02-21-18	Wonderful student performances at @CodwellIES grand opening celebration today! #FineArtsMagnet #LeaderInMe @JonesJolanda @PrincipalLove @GrenitaLathan
02-21-18	Trustee @JonesJolanda: I am so happy #HISD found a way to rebuild this school, we are reinvesting in your neighborhood. @CodwellIES @Busby_isms @GrenitaLathan
02-21-18	#HISD schools chief @GrenitaLathan thanks @PrincipalLove @JonesJolanda @Busby_isms & @DSanders247 for their leadership: @CodwellIES Students now have modern classrooms & state-of-the-art technology, today is a day of celebration." #BuildHISD

02-21-18	@PrincipalLove thanks #HISD team & reminds audience that all the hard work that went into the new @CodwelLES is for these beautiful children @JonesJolanda @Busby_isms @GrenitaLathan #BuiltForLearning #BuildHISD
02-21-18	And the grand opening ribbon has officially been cut! Congratulations @CodwelLES on your beautiful new building! May all the students who walk your halls today and in the future be blessed with success and happiness! @PrincipalLove @JonesJolanda @GrenitaLathan #BuildHISD
02-21-18	Dr. John Codwell, grandson of the school's namesake, spends time visiting with @CodwelLES students after today's grand opening celebration #BuildHISD #BuiltforLearning @PrincipalLove
02-21-18	Congrats @CodwelLES! Fantastic building for a fantastic group of kiddos! Very well deserved! #BuildHISD #BuiltforLearning #21stCentury #CodwellPride (@hfuffman)
02-22-18	@CodwelLES celebrates 40th anniversary at grand opening ceremony! #BuiltforLearning #celebrategoodtimes #itspartytime @PrincipalLove @Busby_isms @JonesJolanda @DSanders247 @apeeples01 @DanBArcht
02-22-18	Passion. Purpose. Progress. @BJHSC_HISD #ThrowbackThursday #2012Bond #BuiltforLearning #progress #teamworkmakesthedreamwork @RhondaForHISD @JRMcAlpine @HeeryK12 @CadenceMcShane @CorganInc
02-22-18	Read about what's happening with construction on the new @madisonmarlins @MHSAAMarlins!!! @Wandaful1913 @HeeryK12 @SatPonInc #2012Bond #BuiltforLearning
02-23-18	GREATNESS in the making. @YatesMagnet @yates @JonesJolanda @krollins41 @MoodyNolan @TurnerSouthTX #FlashbackFriday #2012Bond #BuiltforLearning #progress
02-23-18	Crews are putting finishing touches on the new Westbury HS addition - set to open next month! We think you're going to love it, @WHS_HUSKIES! #2012Bond #21stCenturySchool #BuildHISD @Wandaful1913 @erick_pruitt @Busby_isms
02-23-18	Celebrate good times! @CodwelLES @JonesJolanda @PrincipalLove @Busby_isms @DSanders247 @DanBArcht @apeeples01 #2012Bond #BuiltforLearning #congratulations
02-23-18	Coming along nicely. I love to see progress! #BuiltforLearning (@PMHouston)
02-26-18	Building beautiful, 21st century homes for the many students and faculty of HISD. As we enter into a new week, remember to continue focusing on your goals. #MondayMotivation #2012Bond #BuiltforLearning #teamworkmakesthedreamwork #Buildingthefuture

02-26-18	The new @BJHSC_HISD is nearly one-third complete!! Click on the link to hear the latest on the project! @RhondaForHISD @HeeryK12 @CadenceMcShane @CorganInc @JRMcAlpine #2012Bond #BuiltforLearning #progress #onestepcloser
02-26-18	Wow! These are the types of things that are so exciting to see! Just imagine what great things will be created in the amazing, 21st century spaces of the new @HSPVA! @DDavilaHisd @DrAatPVA @McCarthyBuild @GenslerTexas #2012Bond #BuiltforLearning #goals #cantwait
02-27-18	Happy Tuesday! #TuesdayThoughts #tuesdaymorning
02-27-18	We can't thank Houston voters enough for their support of the #2012Bond. We are building the future of our students and as you can see...the hard work is paying off! @MilbyHighSch @LiraSerg @PrincipalDMilby @HeeryK12 @KirkseyNews #BuiltforLearning #wow #grateful
02-28-18	We're less than 24 hours from the @northside_hs Wall Signing! Stop by tomorrow at 5 p.m. to leave your mark on this great school! #BuildHISD #2012Bond #leaveyourmark @SSODiegoLinares @stevengutierrez @HeeryK12 @Santos4hisd
02-28-18	#WisdomWednesday #wednesdaythoughts
02-28-18	It's almost showtime! @northside_hs @Santos4hisd @BayIBIGroup @SatPonInc @HeeryK12 #2012Bond #BuiltforLearning #itsacelebration
02-28-18	Beautiful musical selection by the @northside_hs choir. @Santos4hisd @SatPonInc @HeeryK12 @SSODiegoLinares #2012Bond
02-28-18	And nowwww the mariachi of @northside_hs!! @Santos4hisd @SSODiegoLinares #2012Bond #BuiltforLearning #itsacelebration
02-28-18	¡Y ahora el mariachi de @northside_hs! @Santos4hisd @SSODiegoLinares # 2012Bond #BuiltforLearning #itsacelebration (@HISDEspanol)
02-28-18	A beautiful rendition of @AndraDayMusic "Rise Up" by the @northside_hs choir. @Santos4hisd #beautiful #2012Bond #itsacelebration
02-28-18	"I want to thank you for everything you do." - Sr. Class President Jacqueline Hernandez @northside_hs #2012Bond #BuiltforLearning
02-28-18	"Quiero agradecerles por todo lo que hacen". - dijoJacqueline Hernandez, presidente de su generación @northside_hs # 2012Bond #BuiltforLearning (@HISDEspanol)
02-28-18	"We cannot wait to see it." @northside_hs Principal Cecilia Gonzales @Santos4hisd @BayIBIGroup @SatPonInc @HeeryK12 #2012Bond #BuiltforLearning

02-28-18	"Here we celebrate accomplishments and overcome challenges." - HISD Board of Education Trustee @Santos4hisd @BayIBIGroup @SatPonInc @HeeryK12 @northside_hs #2012Bond #BuiltforLearning
02-28-18	"We honor your history today." - Northwest Area Superintendent @stevengutierrez @northside_hs @SatPonInc @HeeryK12 @BayIBIGroup #2012Bond #BuiltforLearning
02-28-18	"I'm 100% certain we are going to deliver a great facility." - @SatPonInc Vice President John Marshall @northside_hs #2012Bond #BuiltforLearning
02-28-18	"The real heroes are the graduates and residents of this community ensuring excellent high schools for this community." @northside_hs #2012Bond #BuiltforLearning
02-28-18	"The school will be what both students and the community make it to be. Let's continue to rise up together." - State Rep. @SenatorSylvia @northside_hs #2012Bond #BuiltforLearning
02-28-18	"You are our future." Houston City Councilwoman @Karla4Houston speaking to @northside_hs students. #2012Bond #BuiltforLearning
02-28-18	"I'm honored to be able to speak to you today." - Former HISD Board Trustee @AnnaEforHISD @northside_hs #2012Bond #BuiltforLearning
02-28-18	"I want to thank you for supporting our schools." - HISD Superintendent @HISD_Supe @northside_hs #2012Bond #BuiltforLearning
02-28-18	The @northside_hs Pantherettes jamming out!!! #itsacelebration #2012Bond #BuiltforLearning
02-28-18	Let the wall signing commence! Thank you to all who attended and made this evening great! @northside_hs @Santos4hisd @HISD_Supe @BayIBIGroup @SatPonInc @HeeryK12 #2012Bond #BuiltforLearning #MarkingHistory
02-28-18	Attendees are ending the ceremony with a beautiful serenade by the @HISD_Supe and the @northside_hs mariachi. @BayIBIGroup @SatPonInc @HeeryK12 @Santos4hisd @stevengutierrez @SSODiegoLinares #2012Bond #itsacelebration
02-28-18	@northside_hs @Santos4hisd @HeeryK12 @SatPonInc @BayIBIGroup #beautifulmusic #goodnightv
02-28-18	We do toooooo! @colibri713 #mce #oursupeisbetterthanyours
02-28-18	#oursupeisbetterthanyours
02-28-18	It was such a pleasure to have you! @SenatorSylvia
02-28-18	"Ya lo queremos ver". @northside_hs Directora Cecilia Gonzales @Santos4hisd @BayIBIGroup @SatPonInc @HeeryK12 @Build_HISD #2012Bond #BuiltforLearning (@HISDEspanol)

02-28-18	"Son nuestro futuro" dijo la concejal de la ciudad de Houston @Karla4Houston mientras habla con los estudiantes de @northside_hs. #2012Bond #BuiltforLearning (@HISDEspanol)
02-28-18	La ceremonia termina con una hermosa serenata @HISD_Supe y @northside_hs mariachi. . @BayIBIGroup @SatPonInc @HeeryK12 @ Santos4hisd @stevengutierrez @SSODiegoLinares @Build_HISD #2012Bond #itsacelebration (@HISDEspanol)
02-28-18	A wonderful way for @northside_hs students and the community to commemorate this new HS building! #celebrategoodtimes #2012Bond (@CBRE_Heery)
02-28-18	#SupeSelfie @Build_HISD @HeeryK12 @VladimirNaranjo @northside_hs #BuiltforLearning (@PMHouston)
02-28-18	Even @HISD_Supe got in on the fun! @Build_HISD @HoustonISD #BuiltforLearning (@PMHouston)
02-28-18	It's a pleasure to celebrate a milestone w/Northside HS. Students deserve to have a school they are proud of & can feel safe in. Excited to see all of the upgrades benefit the students & community. (@SenatorSylvia)
03-01-18	Congratulations!!!! I guess once construction is completed on the new @Braeburn_HISD that will be the icing on the cake. #greatthingsaresoontocome #BuiltforLearning
03-01-18	Such a beautiful common space that the new @iamsharpstown has! The floor-to-ceiling windows offer a nice view of one of their exterior courtyards. 21st century indeed! #2012Bond #BuiltforLearning #amazing
03-01-18	Students at @GardenOaksMont will walk the halls of their new building after spring break! @PollockLindsey @Santos4hisd Click on the link to learn more about the project. #firstdayofschool #2012Bond #riceandgardner #hillswartchuaarchitects #B3CI
03-01-18	Read about the festive @northside_hs wall-signing celebration held to mark construction progress on their new school @Santos4hisd @HISD_Supe @Busby_isms @BayIBIGroup @SatPonInc @HeeryK12 #2012Bond #BuiltforLearning #PantherPrideontheNorthside
03-02-18	Students at @WHS_HUSKIES will move into their new building next week! @Santos4hisd @SatPonInc #2012Bond #BuiltforLearning #riceandgardner #joinerpartnershipsinc
03-02-18	Students at @Wilson_HISD will begin moving into their new building addition next week! Click on the link to read more about the project. @Anne4HISD #2012Bond #BuiltforLearning #riceandgardner #drymallaconstruction #smithandcoarchitects
03-02-18	Congrats @MilbyHighSch for winning @PresHou Good Brick Award for outstanding contributions to #preservation, restoration & enhancement of #HTX's architectural & cultural heritage. #2012Bond @HoustonISD @KirkseyNews @HeeryK12 @PrincipalDMilby @DanBArchT @DSanders247 @Busby_isms

03-03-18	This morning students, staff, and parents of @KolterSchool are hosting their "Donuts before Demo event! Attendees are leaving their mark on the old building with their painted handprints on the school's exterior. @sueforhisd @SatPon @Busby_isms #funtimes
03-03-18	The demolition and rebuild of @KolterSchool will occur on the same site with the new school opening in 2020. @sueforhisd @SatPonInc @Busby_isms @DanBArcht @apeoples01 @jmdickins #funtimes #BuiltforLearning
03-03-18	Attendees gathered to hear a few words from @KolterSchool Principal @jmdickins, faculty members, and students. Kolter is one of four Harvey-damaged schools within the that is being rebuilt. #KolterProud #HISDStrong
03-05-18	Staff at @Parker_hisd are getting their first glimpse of their new building! Students hold their first day of classes on March 19. @Wandaful1913 @PatriotCont @DSanders247 @Busby_isms @apeoples01 #2012Bond #BuiltforLearning #excited
03-05-18	Early reviews are in for new @HSPVA: "Very impressive" says Trustee @DDavilaHisd; @DrAatPVA says "It's perfect" #2012Bond @GenslerTexas @McCarthyBuild @DSanders247 @Busby_isms #BuiltForLearning&Arts #TheaterDistrict #DowntownHouston
03-05-18	Trustee @DDavilaHisd is getting a sneak peek at new @HSPVA this morning #2012Bond @DrAatPVA @DSanders247 @GenslerTexas
03-05-18	Lots going on at @WHS_HUSKIES as kids spent the morning in the school's new building addition! @Wandaful1913 @SatPonInc @Busby_isms #2012Bond #BuiltforLearning #goodtimes
03-05-18	These are just a few of the things in the new building addition at @Wilson_HISD @WilsonMontPTO that will welcome students on March 19! @Anne4HISD #2012Bond #BuiltforLearning
03-05-18	Students at @GardenOaksMont will enter the doors of their two new building additions after Spring Break! @PollockLindsey @Santos4hisd #2012Bond #BuiltforLearning
03-06-18	Extra! Extra! Read all about the latest bond construction in our current "Building Excellence" newsletter. #2012Bond #constructionupdates #progress
03-06-18	A big congratulations to the men of @MLelandPrep @KNIGHTS_PTO as they celebrated with the @TAMU Agriculture department the Grand Opening of "The Knight's Glade," their new sustainable communities garden! @RhondaforHISD #awesome #veggiesareyummy #2012Bond
03-06-18	One new school @Parker_hisd and three building additions @Wilson_HISD @GardenOaksMont @WHS_HUSKIES opening after spring break! #2012Bond #BuiltforLearning
03-07-18	#WisdomWednesday #wednesdaythoughts #wedothisforthekids

03-07-18	#HISD Facilities Design GM @DanBArcht & Washington's @Northshore_SD Planning Administrator Lee Hall are touring @MLelandPrep this morning. We love sharing ideas & showing off our #2012Bond schools! Next stop: @Wilson_HISD! #BuiltforLearning @HoustonISD @DSanders247 @Busby_isms
03-07-18	Tour Stop #2: @Wilson_HISD addition - opens 3/19 & has modern, inviting spaces w/ lots of texture. Thanks to #HISD Facilities Design GM @DanBArcht for the tour & to @Northshore_SD Planning Administrator Lee Hall for coming to check us out! #2012Bond #BuiltforLearning @HoustonISD
03-07-18	Sounds like this month's Workshop Wednesday was yet another hit! #WorkshopWednesday #HISDMWBE
03-08-18	#21stcenturylearning
03-08-18	Ladies and gentlemen we present to you.....the NEW @Parker_hisd!! Opening to students on March 19! @Wandaful1913 @Busby_isms @DSanders247 @DanBArcht @PatriotCont @HoustonISD #2012Bond #BuiltforLearning #welcomehome #thekidsaregoingtohaveaball
03-08-18	Congrats on your awesome new addition and reno, @WHS_HUSKIES! We totes love it! For all you non-Huskies, see what you're missing #YouWishYouWentHere #CoolHighSchool #BuildHISD #2012Bond @Wandaful1913 @Busby_isms @erick_pruitt
03-08-18	We're excited for the opening of Wilson Montessori's new three-story addition! We think it's wonderful! Congrats to Principal @BethBonnette and her #Montessori team! #2012Bond #BuiltForLearning @WilsonMontPTO @Anne4HISD @stevengut1errez
03-08-18	#HISD Construction Svcs Officer @DSanders247 gives trustees an update on the #2012Bond program. In just 2 years, we'll be 98% done w/ all projects! #GreatNews #Progress #BuildHISD #BuiltforLearning @Busby_isms
03-09-18	The countdown to Spring Break begins now! #cantwait #schoolsout #springbreak #enjoylife
03-09-18	Two new building additions will open at @GardenOaksMont this month! Enjoy your spring break while our crew works to get everything ready to welcome students on March 19! #BuiltForLearning #2012Bond #RiceAndGardner @PollockLindsey @Santos4HISD @Busby_isms @stevengut1errez
03-09-18	The new @PilgrimHISD addition is set for completion next month! #2012Bond #BuildHISD @Dianac70 @Anne4HISD @DrBrownEDU @HeeryK12
03-10-18	Such an architectural beauty! @SterlingRaider #2012Bond #BuiltforLearning

03-10-18	We just love that exterior courtyard! Great to see the students enjoying themselves! @MilbyHighSch #2012Bond #BuiltforLearning
03-12-18	Wishing everyone a great spring break! #MondayMotivation #stayfocused #goalgetter
03-12-18	One week from today students will walk the halls of the new @Parker_hisd! @ParkerPTO @Wandaful1913 @Busby_isms @DSanders247 @DanBArchT @PatriotCont #2012Bond #BuiltforLearning #thecountdownbegins #homestretch #excited
03-12-18	This Monday is for our Marlins. The project reached the halfway mark just last month and doesn't seem to be slowing down anytime soon! @madisonmarlins @MadisonHighCTE @VernitraShivers @SatPonInc @HeeryK12 @CBRE_Heery #2012Bond #BuiltforLearning #MarlinNation
03-13-18	The view changes every day at @LamarHS! Steel is now four stories high! @LamarPTO @Anne4HISD @GilbaneHouston #2012Bond #LookingGoodTexans #GoingUpFast
03-13-18	The new Askew ES building is nearing completion & on track to welcome students for start of 2018-2019 school year. We think you're going to love it! #2012Bond #BuiltForLearning @hmfv1 @EbonyCumby @AskewPTO
03-13-18	Here's a bird's eye view of the newly built @EnergyIHS Furniture is being delivered this month & we can't wait for you to see it! #2012Bond #EnergyCapitaloftheWorld @EnergyHighPTO @JonesJolanda @LoriLambropoul1
03-14-18	Coming soon to a theater district near you: The new Kinder @HSPVA! Now 80 percent complete! @DrAatPVA is making final furniture selections this month @HSPVAFriends @DDavilaHisd
03-14-18	Building these schools not only to last, but to better the future for all HISD students. #WisdomWednesday #WednesdayThoughts #HISDStrong
03-14-18	The new addition at @PilgrimHISD is nearing completion. Features include a new science lab, a gymnasium, flexible learning areas, teacher work spaces and additional classrooms #2012Bond #Kthru8School @Dianac70 @Anne4HISD
03-15-18	We love what you've done with the place, @WHS_Huskies! The school formally opens its new addition March 19. It features 26 classrooms, flexible learning centers, two new gyms, & a multi-purpose dining commons area. #2012Bond #BuiltForLearning @Wandaful1913 @WHSSuccess
03-15-18	Just a little walk down memory lane at the beam-signing of @LawsonMS_HISD. The new school is slated to open to students during Q2 of this year!! @Wandaful1913 @HK_Architects @TurnerSouthTX #ThrowbackThursday

03-16-18	Two new additions at @GardenOaksMont will open to students on March 19. Crews are working throughout spring break to get everything shipshape. The buildings have lots of classroom space, and a new gym. #2012Bond #Montessori #BuiltForLearning @PollockLindsey @Santos4HISD
03-16-18	Donuts, paint and a little nostalgia at @kolterelem. @sueforhisd @jmdickins @SatPonInc #FlashbackFriday #BuildingFarewell #greatthingstocome #BuiltforLearning
03-16-18	We love Wilson Montessori's new three-story addition, opening to students March 19. Features include a large library w/ floor-to-ceiling windows, flexible learning center, drama room, & more! #2012Bond #Montessori #BuiltForLearning @BethBonnette @WilsonMontPTO @Anne4HISD
03-16-18	That moment when you realize construction on your school will be completed by the end of the year! @WorthingColts1 @Wandaful1913 @Busby_isms #FridayFeeling #2012Bond #BuiltforLearning #tooexcited
03-17-18	Walls are going up quickly on the new @WhartonDual! The project is set for completion at the end of 2018! @DDavilahisd @HeeryK12 @CBRE_Heery #2012Bond #BuiltforLearning #progress
03-17-18	We wish you all a festive Saturday! #saintpatricksdays
03-18-18	We're loving the 7th & 8th grade Kiva in the new Wilson Montessori addition! These kids look right at home on their first day in the new facility! And the library's not too shabby either! #2012Bond #Montessori #BuiltForLearning @BethBonnette @WilsonMontPTO @Anne4HISD
03-18-18	We have a delivery for @EnergyIHS! Furniture has arrived! It's comfy, functional, flexible, & colorful. Now they have to put it all together! #SomeAssemblyRequired #2012Bond #EnergyCapitaloftheWorld @EnergyHighPTO @JonesJolanda @LoriLambropoul1 @NicoleMooreHisd @Busby_isms
03-18-18	It all goes DOWN TOMORROW! @Parker_hisd #tooexcited #classisinession
03-19-18	Congrats @MilbyHighSch!! It's officially official. #LEED #BuiltforLearning @KirkseyNews @Build_HISD @USGBC (@PMHouston)
03-19-18	Students at @Parker_hisd @ParkerPTO are being welcomed to their new school this morning! @Wandaful1913 @Busby_isms @DSanders247 @PatriotCont #funtimes #2012Bond #BuiltforLearning
03-19-18	Students are making their way to their new classrooms! @Parker_hisd @ParkerPTO @Wandaful1913 @Busby_isms @DSanders247 @PatriotCont #classisnowinession #2012Bond #BuiltForLearning
03-19-18	Good morning @WHS_HUSKIES! We're so happy to see you learning in your new classrooms this morning! #BuiltForLearning #2012Bond @Wandaful1913 @erick_pruitt @Busby_isms

03-19-18	"Our new school is really, really big, and it's really, really cool! We have the coolest music rooms ever! I hope you have a wonderful first day in your new school." - @Parker_HISD Principal, Ms. Lori Frodine @Wandaful1913 @Busby_isms @DSanders247 @PatriotCont @apeeples01
03-19-18	WHS senior Roger Wells: "The new addition is amazing, especially the gyms and weight room. I think it will bring neighborhood kids back to Westbury" Go @WHS_HUSKIES! #YouWishYouWentHere #BuiltForLearning #2012Bond @Wandaful1913 @erick_pruitt @Busby_isms
03-19-18	Spring Break is over, but the fun is just starting for @GardenOaksMont! Students and staff are celebrating the opening of their new addition, which includes new classrooms and a gym. #2012Bond #BuiltForLearning @PollockLindsey @Santos4hisd @Busby_isms
03-19-18	Mr. Clayborne is helping his students get used to their new surroundings. A tour of the @GardenOaksMont new addition includes a reminder to walk, not run! #2012Bond #BuiltForLearning @PollockLindsey @Santos4HISD @Busby_isms
03-19-18	It's a great Monday morning for @Wilson_HISD students! It's their first day in their gorgeous new school. It looks like these students are settling right into their new common spaces. #BuiltforLearning #2012Bond #Montessori @HoustonISD @WilsonMontPTO @Anne4HISD
03-19-18	Check out these amazing views at the new @Wilson_HISD #2012Bond #BuiltforLearning @Anne4HISD @Busby_isms @WilsonMontPTO @HoustonISD @BethBonnette #montessori
03-19-18	"Montessori goes back to the environment and taking care of the environment." @Wilson_HISD Principal @BethBonnett. Environmental elements are a huge part of the beautiful interiors at this newly renovated #montessori. #2012Bond @BethBonnett @WilsonMontPTO @HoustonISD @Busby_isms
03-20-18	HISD COO @Busby_isms and HISD Construction Services Officer @DSanders247 made a stop by @Parker_hisd @ParkerPTO this morning to check out the new digs. #2012Bond #BuiltforLearning #lookinggoodparker
03-20-18	Next stop is @WHS_HUSKIES!!! Such a beautiful addition!! @Busby_isms @DSanders247 #BuiltforLearning #2012Bond #YouWishYouWentHere
03-20-18	Hey there @Wilson_HISD! It's so wonderful to see you guys in your new space! @WilsonMontPTO @BethBonnette @Busby_isms @DSanders247 #2012Bond #BuiltforLearning #Montessori

03-20-18	And now a walk-through of the new building additions at @GardenOaksMont! We can tell there's going to be tons of learning happening here! @Busby_isms @DSanders247 @Santos4hisd @PollockLindsey #2012Bond #BuiltforLearning
03-20-18	Westbury High School opened its new addition this month ahead of schedule! Attendees of tonight's community meeting at the school will get a first hand look at 6 p.m. #2012Bond @Wandaful1913 @WHS_HUSKIES #YouWishYouWentHere
03-20-18	Garden Oaks Montessori welcomed students into new facilities this week! #2012Bond #BuiltForLearning #BuildHISD @PollockLindsey @GardenOaksMont @Santos4hisd
03-20-18	The first community meeting is under way in @WHS_HUSKIES beautiful new addition! #2012Bond @Wandaful1913
03-20-18	Principal Monaghan tells community about new fine arts space that is next up on the @WHS_HUSKIES bond project list. Orchestra and mariachi programs are being planned! #FineArtsFeeder #ParkerMeyerlandWestbury #2012Bond #BuildHISD @Wandaful1913 @NicoleMooreHisd
03-20-18	Community members are touring new @WHS_HUSKIES addition after meeting wrapped up. #2012Bond #BuiltForLearning #YouWishYouWentHere @Wandaful1913 @NicoleMooreHisd @WVVM_HISD
03-21-18	Students at @Parker_hisd @ParkerPTO were all abuzz on the first day in their new building! @Wandaful1913 @Busby_isms @DSanders247 @HoustonISD #2012Bond #BuiltforLearning #magnetschoolsrule
03-21-18	Way to go Buffs!! @MilbyHighSch @HeeryK12 @KirkseyNews #greatachievement #congratulations #keepupthegoodwork
03-22-18	It's amazing to see what a modern, 21st century learning space can provide! @texasbuckeye @HeeryK12 @VLKArchitects @Busby_isms #2012Bond #BuiltforLearning #Investinginourfuture #beautifulspaces
03-22-18	The beautiful building addition at @Wilson_HISD @WilsonMontPTO opened its doors to students on Monday. @Anne4HISD @BethBonnette @Busby_isms #2012Bond #BuiltforLearning #lovethatview
03-22-18	Project Advisory Team meeting here at @btw_hsep is about to get underway! @FanningHowey #2012Bond #progress
03-22-18	The building is now fully enclosed and electricity and HVAC systems have been installed throughout. @btw_hsep @FanningHowey #2012Bond #Builtforlearning #inthehomestretch
03-22-18	Project Advisory Team members are getting their first glimpse of the new @YatesMagnet this evening! @TurnerSouthTX @Busby_isms #2012Bond #BuiltforLearning #progress

03-22-18	Heyyyy there @DowntownHouston! The new @YatesMagnet features a second-floor classroom with a STUNNING view of the Houston skyline. @JonesJolanda @TurnerSouthTX #2012Bond #BuiltforLearning #progress #views
03-22-18	Walking the new Jack Yates High School. @YatesMagnet @JackYatesMath @krollins41 @jackyatesELA (Retweet from @tiffanyg924)
03-22-18	Love this! #21stcentury #2012Bond #BuiltforLearning #conditproud
03-23-18	Who's excited that it's FriYAY? @Parker_hisd @ParkerPTO @Busby_isms @DSanders247 #FlashbackFriday #firstday #BuiltforLearning
03-23-18	The new @LawsonMS_HISD is almost 90 percent complete! @Wandaful1913 @HK_Architects @TurnerSouthTX #2012Bond #BuiltforLearning #progress #inthehomestretch
03-23-18	Project Advisory Team members had the opportunity to tour the new @YatesMagnet! @JonesJolanda @krollins41 @TurnerSouthTX #2012Bond #BuiltforLearning #progress #almostfinished
03-26-18	#MondayMotivation #strengthennumbers #teamworkmakesthedreamwork
03-26-18	Check out how HISD Logistics Manager Jade Mays spends her time "moving and shaking." #TeamHISD #EmployeeSpotlight
03-26-18	All #HISD schools and district offices to be closed Friday, March 30 for the spring holiday. (Retweet from @HoustonISD)
03-27-18	It's great to be a Westbury Husky! Check out this video of the new @WHS_HUSKIES addition! #CoolHighSchool #BuiltForLearning #2012Bond #YouWishYouWentHere @Wandaful1913 @Busby_isms @DSanders247 @SatPonInc @erick_pruitt @NicoleMooreHisd @HoustonISD @GrenitaLathan
03-27-18	@ConditES @VLKArchitects @HeeryK12 @CBRE_Heery #2012Bond #BuiltforLearning #theworkspeaksforsitself #conditproud
03-27-18	Lots of interested folks at the @BellaireHigh Project Advisory Team mtg this afternoon to get a glimpse of the new campus master plan. #2012Bond #BuildHISD @PBK @HeeryK12
03-27-18	Construction of new @BellaireHigh will be done in phases, allowing students to remain on site throughout the process. Phase 1 includes 3-story addition, gyms, pool, locker room, kitchen, small dining area & multipurpose rooms. #2012Bond #BuildHISD @PBK @HeeryK12
03-27-18	Work on the new @BellaireHigh could begin as early as June, with construction of a detention area and temporary parking lot. #2012Bond #BuildHISD @PBK @HeeryK12

03-28-18	One school at a time, we are creating what will be one of the most modern portfolios of urban high schools in the country. #WisdomWednesday #wisdomquotes #2012Bond #Buildingthefuture #teamworkmakesthedreamwork
03-28-18	And it's only going to get better! @YWCPAHISD final phase of construction is set to wrap up in the third quarter of this year. @april_williams4 @HeeryK12 @CBRE_Heery @SatPonInc @NatexArchitects @JonesJolanda #2012Bond #BuiltforLearning #Buildingforthefuture
03-28-18	Renovations on the auditorium and third-floor of @YWCPAHISD is progressing well towards its Q3 completion! @april_williams4 @JonesJolanda @HeeryK12 @CBRE_Heery @SatPonInc @NatexArchitects #2012Bond #BuiltforLearning #progress
03-28-18	We do too! #2012Bond #BuiltforLearning #buildingthefuture
03-28-18	Walk-through of the new @MadisonHighCTE @MHSAAMarlins with the Project Advisory Team! @Wandaful1913 @HeeryK12 @SatPonInc #2012Bond #BuiltforLearning #progress
03-28-18	Making stops in the auditorium, CTE spaces, dining commons and gym! @MadisonHighCTE @MHSAAMarlins @Wandaful1913 @CBRE_Heery @HeeryK12 @SatPonInc #2012Bond #BuiltforLearning #progress
03-28-18	Move-in into the new @MadisonHighCTE @MHSAAMarlins is slated to take place over winter break! @Wandaful1913 @HeeryK12 @CBRE_Heery @SatPonInc #2012Bond #BuiltforLearning #progress
03-28-18	Three teachers were able to see the new school today! They loved it!! @HSLawAndJustice (@cmosteit)
03-28-18	Another project on the fast track to completion! Great work by @HeeryK12 and the Houston project team! #2012Bond #Buildingforthefuture (@CBRE_Heery)
03-29-18	We are @Robinson_HISD ! @Principal_Hohos #ThrowbackThursday #HISDStrong #TeamHISD #homeiswheretheheartis
03-29-18	It's hard to believe move-in will begin this summer! @EnergyIHS @LoriLambropoul1 #2012Bond #BuiltforLearning #inthehomestretch
03-29-18	The beautiful state-of-the-art kitchen at @MilbyHighSch definitely gives the students a true culinary experience! @LiraSerg @PrincipalDMilby @HeeryK12 @KirkseyNews @HISDSupe #2012Bond #BuiltforLearning #whatsonthemenu
03-30-18	Happy Spring! Enjoy the three-day weekend! #springholiday #schoolsout
03-30-18	Seems like only yesterday we were celebrating the grand opening ceremony of @DebaKeyHSHP. It's always wonderful to see our students thriving in their new spaces! @sueforhisd @HeeryK12 #2012Bond #BuiltforLearning

03-30-18	How's that modern, flexible furniture @DebakeyHSHP? #FlashbackFriday #fbf #2012Bond #BuiltforLearning #21stcentury
03-30-18	Looking good @YatesMagnet!!!! Cant wait to see students' reactions to their new space after construction is complete!! @krollins41 @JonesJolanda @HISDSupe @TurnerSouthTX #2012Bond #BuiltforLearning #inthehomestretch
03-31-18	Truly one of our favorite areas of the new @NorthForestHigh! The floor-to-ceiling windows provide tons of natural light and a great view of the neighboring forest. @DrHenson2 @RhondaForHISD #2012Bond #BuiltforLearning #elbosque #views #beautiful

FACEBOOK

01-08-18	Welcome back Robinson Elementary students and staff!! Today is the first day in their renovated post-Harvey building!!
01-08-18	Welcome back!! #RobinsonElementary
01-09-18	Students at Robinson Elementary School were so excited to see their newly renovated school and be reunited under one roof! Read all about the first day of school after post-Harvey renovations
01-10-18	It was an exciting first day of school after break for Robinson Elementary School, which is back at its home campus after #Harvey renovations! #HISD
01-10-18	See the reaction to Scarborough High School's renovations and new addition under the 2012 Bond!
01-23-18	Condit Elementary School awarded the highest honor in Exhibit of School Architecture competition #BuildHISD#2012Bond
01-23-18	We are live at Kashmere HS Ribbon-Cutting ceremony! #2012bond #buildingHISD #builtforlearning
01-23-18	#HISD Chief Operating Officer Brian Busby given President's Award by Trustee Wanda Adams for outstanding work after #Harvey
01-26-18	600 volunteers planting shrubbery and trees and more at Hilliard Elementary #RecoveryHouston #Numotion
02-19-18	Personal stories, like that of Robinson Elementary School Principal Paige Fernandez-Hohos, exemplify how #HISD is rebuilding, reimagining education
02-21-18	We are live from John E. Codwell Elementary School opening celebration.
02-21-18	Codwell Elementary celebrates its 40th anniversary at grand opening ceremony
02-28-18	We are at Northside High School Wall signing celebration



Parker Elementary School

Glossary

Glossary

GLOSSARY OF TERMS

BAS

Building Automation System (HVAC and lighting controls)

Change order

A modification to the original construction contract authorizing a change in the work or an adjustment in the amount of the contract or the contract time. The original contract price may not be increased by more than 25% by change order.

Competitive Bidding

A procurement method by which a governmental entity contracts with a contractor for the construction, alteration, rehabilitation, or repair of a facility by awarding the contract to the lowest responsible bidder.

Competitive Sealed Proposal (CSP)

A procurement method by which a governmental entity may request proposals and pricing information based on the scope of work provided, rank the offers, negotiate a contract, and then award the project to the contractor that offers the best value to the entity.

Construction commissioning

A collaborative process whose purpose is to ensure that buildings and systems perform according to contract.

Commissioning agent

An independent party, unaffiliated with the design team or contractors, that takes charge of the construction commissioning process.

Construction documents

Extremely detailed drawings and specifications showing and describing all of the details required to construct the building.

Construction Manager at Risk (CMAR)

A construction delivery method by which a governmental entity contracts with an architect or engineer for design and construction phase services and contracts separately with a construction manager-at-risk to serve as the general contractor and to provide consultation during the design and construction, rehabilitation, alteration, or repair of a facility. A CMAR is selected based upon qualifications and price proposal that would provide the best value for the governmental entity.

Daylighting

A planned energy conservation strategy that utilizes illumination from sunlight.

Design development

Process in which schematic design drawings are further developed to include more detail, including: detailed site plan; room layouts; door and window types; interior and exterior elevations; reflected ceiling plans; plumbing, mechanical, structural, and electrical drawings; and kitchen layouts.

Design team

A group of professionals from architectural and engineering firms that is engaged to design a facility.

Educational Specifications

A document that details the number of rooms required, the size of each room, how those rooms should relate to each other (adjacencies), and the elements (sinks, electrical outlets, markerboards, cabinets, etc.) that should be included in each room. Districtwide Educational Specifications will be adapted for the specific needs of the campus.

Encumbrance Accounting

The recognition of commitments that will subsequently become expenditures when goods and services are received.

FF&E

Furniture, fixtures, and equipment. This describes all contents that are not a permanent part of the structure.

Hard costs

Expenses associated with direct construction of a project.

HVAC

Heating, ventilation, and air-conditioning

Job Order Contract (JOC)

A procurement method used for maintenance, repair, alteration, renovation, remediation, or minor construction of a facility when the work is of a recurring nature, but the delivery times, type, and quantities of work required are indefinite.

Leadership in Energy and Environmental Design (LEED)

A building certification process developed by the U.S. Green Building Council (USGBC) to enhance environmental awareness among architects and building contractors and to encourage the design and construction of energy-efficient, water-conserving buildings that use sustainable or green resources and materials.

MEP

Mechanical/electrical and plumbing systems.

Program or Concept design

Single-line drawings that illustrate room adjacencies and scale

Public Facility Corporation

The PFC is a non-profit corporation, the creation of which was sponsored by the District pursuant to the Public Facility Corporation Act. The Public Facility Corporation act authorizes the creation and utilization of school district public facility corporations to issue bonds for capital renovation programs. The Houston Independent School District Public Facility Corporation (HISD-PFC) has utilized this structure to issue \$48M for four of the news schools in the 2007 Facilities Capital Program (FCP).

Schedule of values

An itemization of costs that comprises the entire contract amount.

Schematic Design

Typically includes a simple site plan, floor plans, simple building cross-sections, an outline specification with general information about building systems, a table comparing required square footages from the educational specifications with actual square footages shown on the drawings, a preliminary estimate of cost options, and three-dimensional depictions of the exterior of the building.

Schedule of values

An itemization of costs that comprises the entire contract amount.

Scope-to-Budge

An analytical review conducted by the architectural/engineering team to ensure the proposed scope of work and project requirements are aligned with the established construction budget. The approved findings from this review become the basis for the design and preparation of the construction documents.

Schematic Design

The schematic design submission typically includes a simple site plan, floor plans (simple scale drawings that show room sizes, relationships, doors, and windows), simple building cross sections, an outline specification with general information about building systems, a table comparing required square footages from the educational specifications with actual square footages shown on the drawings, a preliminary estimate of cost options, and possibly 3-dimensional depictions of the exterior of the building

Soft costs

A construction industry term, but more specifically a contractor accounting term for an expense item that is not considered direct construction cost. Soft costs include architectural, engineering, financing, legal fees, and other pre- and post-construction expenses.

Swing space

A school building or a portion of an existing school building or other facility that will house the student population and its teachers and staff during the school-construction process.



Jordan High School for Careers

Appendix

Bond Oversight Committee Status Report

February 2018

The Houston Independent School District Bond Oversight Committee got an up-close and personal look at a 21st-century learning environment on Tuesday when they toured the new North Forest High School during their regular quarterly meeting.

The eight-member group gathered first in the auditorium for a brief introduction and a chance to see the space's retractable seating, before moving on to the dramatic main hall, which serves as a focal point for the school.

The space features modern chandeliers and lots of windows providing both natural light and views of the surrounding landscape. It connects to a food-court-style dinning commons with two levels of flexible seating.

Led by North Forest Principal Darryl Henson and HISD Facilities Design General Manager Dan Bankhead, the tour also featured the school's two gymnasiums and a unique, second-level, indoor running track — the first of its kind in HISD. Committee members also got a chance to see one of the second-floor learning stairs and career and technical education rooms.

The \$59.5 million facility, located directly across Mesa Drive from the original school, opened on Jan. 8. The project was funded with state money, but construction was managed by the district's bond team.

Following the tour, committee members gathered in an upstairs classroom, where HISD Construction Services Officer Derrick Sanders provided the committee with a status report on the 2012 Bond Program.

Fifty percent of projects are now complete, Sanders said, noting that almost 80 percent would be complete by the end of this year. By the end of next year, he added, all but one school will be completed and opened.

Five new campuses opened to students for the first time on Jan. 8. They include Sharpstown, Scarborough, and North Forest high schools, as well as Robinson Elementary, which underwent a major renovation after being damaged during Hurricane Harvey. The district also opened a new temporary campus to house Austin High School students and staff during the rebuilding of their school.

[See video on HISD's newest schools](#)

Eight more projects are expected to wrap up by June, Sanders said. They are Parker and Hilliard elementary schools, Lawson Middle School, Washington and Yates high schools, High School for Law and Justice, and Eastwood and Pilgrim academies. Hilliard is not part of the 2012 Bond, but is undergoing renovation due to damages sustained during Hurricane Harvey.

HISD Chief Operating Officer Brian Busby also briefed the committee on his proposed 20-Year Capital Plan, which calls for four bonds over the next two decades. Each bond would have a similar structure. In addition to funding for new relief schools and existing facility repair and replacement, each bond would include money earmarked for technology, transportation, safety and security upgrades, and building automation, HVAC and lighting controls.

Busby said a new bond could be approved by the HISD Board of Education and put on the ballot for voter approval in November 2018 or May 2019.

The oversight committee also heard updates on the financial status of the 2012 Bond Program, which continues to maintain a AAA rating, as well as minority- and women-owned business enterprise participation rates, which continue to track above board-established goals.

Additionally, members were informed about communications and community engagement efforts, including the team's work to provide bond principals with targeted updates and parent. The team also is continuing to coordinate and cover project milestone celebrations and promote and use the new twitter account — @Build_HISD — to provide updates and information to targeted stakeholder groups.

HISD's \$1.89 billion bond program was approved by Houston voters in 2012. In addition to campus-based projects, the program also includes work benefiting students across the district, including \$100 million in technology upgrades, \$44.7 million to replace regional fieldhouses and improve athletics facilities, \$35 million to renovate middle school restrooms, and \$17.3 million for safety and security improvements.

The next quarterly meeting of the Bond Oversight Committee is scheduled for April 2018.



MEETING NOTES

MEETING: **Bond Oversight Committee Meeting**
2012 HISD Facilities Capital (Bond) Program

LOCATION: North Forest High School
10726 Mesa Dr.
Houston, TX 77078

DATE: Feb. 6, 2018

TIME: 8:30 A.M.

PRESENT: **Bond Oversight Committee (BOC)**

Mr. Gary J. White
Mr. Michael G. Davis
Mr. Craig Johnson
Mr. Robert M. Eury
Ms. Phoebe Tudor
Mr. D.V. "Sonny" Flores
Mr. David Quan
Mr. Gusta Booker

Houston Independent School District (HISD)

Mr. Brian Busby, Business Operations
Mr. Derrick Sanders, Construction Services
Mr. Dan Bankhead, Construction Services
Mr. Andreas Peeples, Construction Services
Ms. Alexis Licata, Business Logistics/Transportation
Ms. Yesinia Taylor, Business Solutions
Ms. Tonya Savoie, Business Solutions
Ms. Sherrie Robinson, Controller's Office
Mr. James Moore, Capital Project Accounting
Ms. Holly Huffman, Bond Communications
Ms. Rebecca Kiest, Bond Communications
Ms. Mariauna Hernandez, Bond Communications
Mr. Eugene Salazar, Business Operations
Ms. Mary Rochon, Construction Services
Ms. Veronica Bush, Construction Services
Ms. Christine Manrique, Construction Services
Ms. Sheleah Reed, Strategic Engagement/Outreach
Mr. Darryl Henson, North Forest High School
Mr. Dennis Frazier, Internal Audit
Mr. John Gerwin, Internal Audit

ABSENT:

The general purpose of the meeting was to brief the Bond Oversight Committee on the fourth quarter progress of the new construction and renovation projects funded through the 2012 Facilities Capital Program. Related issues, questions, and activities were also discussed:

Item 1

Welcome

Construction Services Officer Derrick Sanders welcomed Bond Oversight Committee members and other guests just after 8:30 a.m. The group met initially in the auditorium of the North Forest High School. He informed members that the meeting would begin with a tour of the new school prior to the usual proceedings. He then introduced Facilities Design General Manager Dan Bankhead and North Forest Principal Darryl Henson to lead the tour.

Item 2 North Forest High School Tour

Mr. Bankhead and Principal Henson led the committee and other attendees on a tour of the new North Forest High School. Stops were made in the dining commons, gymnasium, and various classrooms, including the automotive shop. Committee members had the opportunity to ask questions about the new school. The tour concluded in a second-floor upstairs classroom, where the remainder of the meeting was held. The meeting was held in the classroom to showcase the technology and flexibility of the space.

Item 3 Minutes from October 31 Meeting

Mr. Sanders asked the group to approve the minutes from the October 31 meeting. They were approved unanimously.

Item 4 Video Presentation

Mr. Sanders began the meeting with a video presentation highlighting the four schools — Sharpstown, Scarborough, North Forest high schools, and Robinson Elementary School — and that opened on the first day of the Spring 2018 semester.

Item 5 Fourth Quarter Construction Update

Mr. Sanders showcased photos of the five new campuses that opened in January — Sharpstown, Scarborough, North Forest high schools, and Robinson Elementary School, and the new Austin High School temporary campus. Sharpstown was rebuilt and Scarborough was renovated as part of the district's voter-approved 2012 Bond Program. The construction of the new North Forest High School and renovation of storm-damaged Robinson Elementary School (where everything below four feet had to be replaced due to flooding) were overseen by the bond team, but not funded with bond dollars. At Austin, a new temporary campus was built to house the school while its original building — located directly across the street — was rebuilt as part of the 2012 Bond Program. Committee Member Phoebe Tudor asked if Hurricane Harvey repairs would be covered by insurance. Mr. Sanders responded that insurance had helped, noting that \$88 million in Harvey-related damages, \$25 million had been funded by insurance. He noted that some of that \$25 million had been fronted by the insurance company and the district still needed to file additional paperwork related to it. He also noted that the \$88 million does not include the cost of rebuilding four elementary schools that were significantly damaged by the storm. The district has estimated that it will cost \$126 million to rebuild those four schools. Mr. Sanders and Chief Operating Officer Brian Busby noted that the district decided to rebuild those four schools after determining that they would need to be significantly raised due to new, post-Harvey building codes. It was determined to be cheaper to rebuild than renovate and raise the schools. The new building codes will require the new schools to be raised by almost six feet to prevent future flooding.

Mr. Sanders also displayed photos of schools that were set to be completed in coming quarters. Parker Elementary School, Eastwood Academy, High School for Law Enforcement, and Hilliard Elementary School will all be done by the end of the first quarter, with Parker planning to open to students after Spring Break. Additionally, Lawson Middle School, Pilgrim Academy, and Washington and Yates high schools are set to wrap up by the end of the second quarter. Three additional schools — Wilson Montessori, Westbury High School, and

Garden Oaks Montessori — will move into new wings over Spring Break as part of scheduled construction phasing.

Mr. Sanders also noted that the 2012 Bond Program had hit a major milestone with 50 percent of all projects completed. By the end of 2019, the program will be 98 percent complete, with only Bellaire High School still under construction. Before moving on to the next agenda item, Mr. Bankhead told the committee that Condit Elementary School recently had received the Caudill Award for excellence in school design.

Item 6 Supplier Diversity (M/WBE) Report and Community Outreach

Business Logistics and Transportation Officer Alexis Licata began her presentation by introducing Yesinia Taylor as the new general manager of Business Solutions. Ms. Taylor told the committee about three M/WBE workshops that had been held during the previous quarter, as well as other outreach the team had done with various community groups and organizations. She noted that the M/WBE participation rate was almost 30 percent, which was well above the baseline set by the HISD Board of Education.

Item 7 Financial Report

Controller Sherrie Robinson reported that the total budget for the 2012 bond program was \$2.1 billion, with total commitments of \$1,695,139,404, including \$486,926,280 in encumbrances and \$1,208,213,124 in expenditures. Available funding is \$407,310,559.

Item 8 Bond Communications

Bond Communications Manager Holly Huffman reported that the Bond Communication Team had spent most of the last quarter focused on the five new campuses opening in January. The team created teaser videos for three of the schools to generate buzz in advance of the opening. Leading up to the opening, the team working with administrators to provide parent communication, including letters, callouts, maps, FAQs, etc. And on the first day, the team provided full, on-site coverage of all five new campuses. Ms. Huffman said the team also was continuing to grow the @Build_HISD twitter account, noting that the following was small, but growing steadily at a rate of two new followers per day. She further noted that the team had held three milestone events during the last few months and that planning was underway for about seven more.

Item 9 Looking Ahead

Mr. Sanders noted that eight schools would be finished by the end of June, which would equate to a 59 percent completion rate. By the end of 2018, the district would have an 80 percent completion rate. He then asked Chief Busby to give a presentation on the district's plans for future bond elections.

Item 10 Building HISD: Planning for the Future

Chief Busby told the committee he was developing a 20-year capital plan that would call for four bond elections — each requiring little-to-no tax increase — held over the next two decades. Each bond would be at least \$1.2 billion and would earmark funds for new relief schools as well as facility repair and replacement. The district would use facilities assessment and student growth data to determine what new schools needed to be built and what old schools needed to be rebuilt. In addition to campus construction, each bond program also



would allot money for district technology, safety and security upgrades, transportation/light fleet and building automation systems, HVAC, and lighting controls. The first bond election could be held in November 2018 or May 2019.

The information outlined above reflects the author's understanding of the key discussions and decisions reached during this meeting. Should you have any additions and/or clarifications to these meeting notes, please notify the author in writing promptly. These notes will be relied upon as the approved record of the meeting, unless a written notice to the contrary is sent to the author within seven (7) days of the submission of these meeting notes.

Prepared by HISD Bond Communications.
